

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना ।

पत्रांक 1719355

दिनांक 11/12/22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR(3054) under Bihar Rural Road Maintenance
Policy-2018 योजना अन्तर्गत पथ का आवंटन का अधियाचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि शीर्ष-MR(3054) under Bihar
Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथ का आवंटन का
अधियाचना का मांग विहित-प्रपत्र में तैयार कर अधियाचना हेतु भेजी जा रही है। पथ का
कार्य विशिष्टियों के अनुरूप किया जा चुका है।

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा
की जाये ताकि संवेदक का भुगतान किया जा सके।

विश्वासभाजन

अनु० :- यथोक्त।


11/12/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।


11/12/22


11/12/22

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Patna

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PA/PAT/22/0004	Patna Jahanabad SH To Fatehpur Punpun Suraksha Bandh	1111035024	Lett No.-1525 dated 29.03.2022	0.490	34.36800	29.73990	2.24290	10-MBD/2022-2023	29.03.2023	-	3.56250	25 mm	5%	0.00000	0.00000	22.32713	कराये गये कार्य गुणवत्तापूर्ण एवं विधिबद्धि के अनुरूप है एवं सहायक अभियंता द्वारा 50 प्रतिशत एवं अप्रोप्रियेटरी द्वारा 10 प्रतिशत मापी का सत्यापन कर लिया गया है।
Total																	22.32713	

- Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- Up-to-Date Physical Progress has been uploaded in MIS.

[Signature]
Executive Engineer

RWD Works Division, Patna

C
11/12/22

ashe
11/12/22



NAME OF THE ROAD: PATNA JEHANABAD SH TO FATEHPUR PUNPUN SURAKSHA BANDH

LENGTH OF THE ROAD: 0.49 KM

PACKAGE NO.: MR-N/22-23/PATNA/04

DIVISION: PATNA

BLOCK: PATNA SADAR

AGENCY: M/S R COM

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD					$Y = 0 * X^2 + 0.936 * X + 278.4$		
18/ 11/ 22	11: 25: 11	3	0.1	230	0	2300	2431	G	3.34	25.50933	85.191575	Normal	X = 2000		
18/ 11/ 22	11: 25: 21	3	0.1	250	30.3	2500	2618	G	3.56	25.50941	85.1906816	Normal	Y = 2150		
18/ 11/ 22	11: 25: 47	3	0.1	270	30.3	2700	2805	G	3.79	25.50953	85.1899316	Normal			
18/ 11/ 22	11: 26: 0	3	0.09	250	30.3	2500	2618	G	3.56	25.50957	85.18941	Normal	(R) RURAL ROAD		
TOTAL			0.39	1000	90.9	10000	10472		14.25	102.0378	340.7615982		Good	Average	Poor
AVERAGE						2500	2618		3.5625				<4000	4001-5000	>5001

fail
18/11/22

18/11/22

18.11.22
32.

18/11/22
AE

18/11/22
E-E



Name of Customer : M/S R. COM

Name of Work/ Road : PATNA JEHANABAD SH TO F.

Lab Job number :

Date : 18-11-2022

Section No. : 3

Test Date : 18-11-2022

Road Name : PUNPUN SUPAKSHA BANDH

Machine No :

Road Type : (R) RURAL ROAD

Start S No :

Side :

Interval :

Weather :

UIV Range : 1431 To 4000 1000 mm/km

Start Location :

Dist Range : 0 To 0.5 0.1 * 1000 m

End Location :


Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View

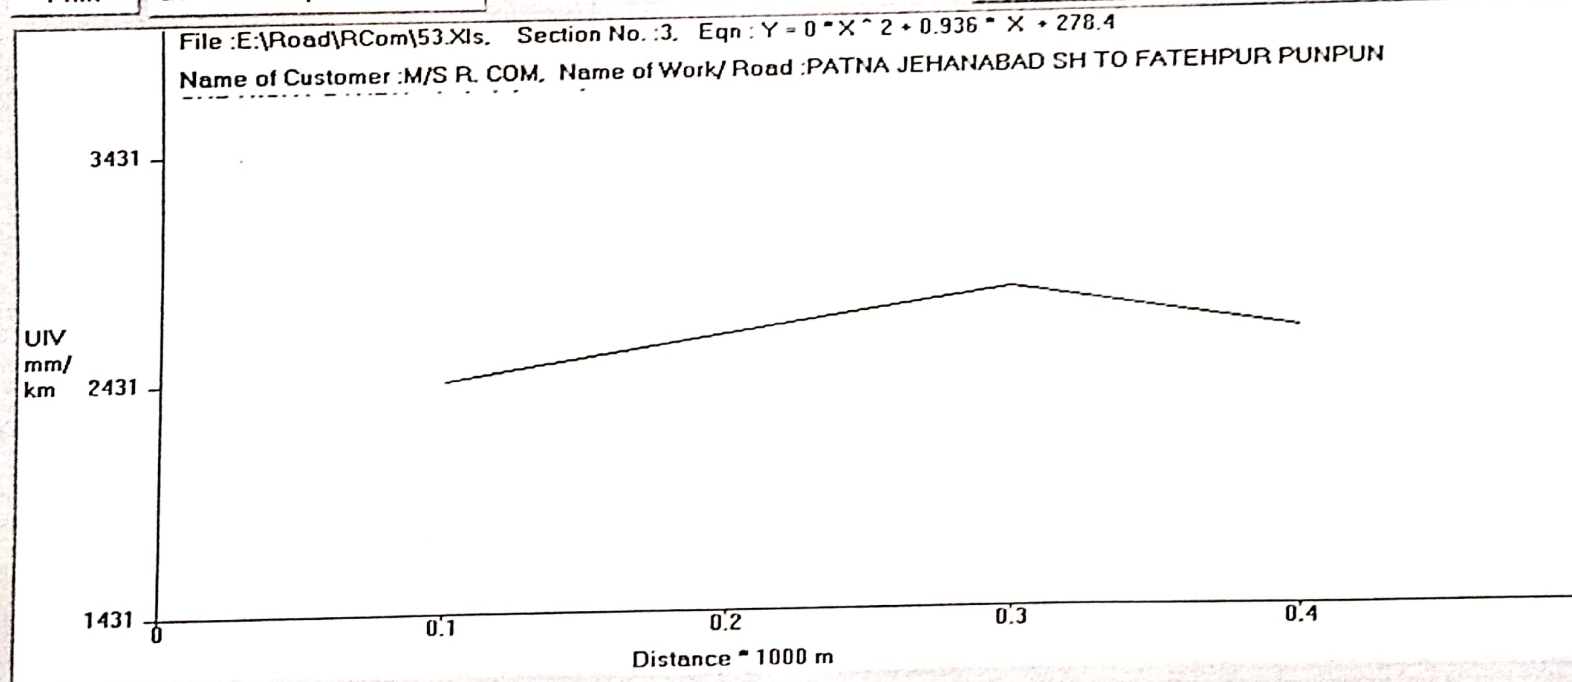

16/22

18.11.22
for

18/11/22
AE

18/11/22
EE

