

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक—**2430.83**

दिनांक—**19-12-22**

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :— शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति 2018” योजनान्तर्गत पथ:—

DHOBNI GRAM SE CHIUTAHA GRAM TAK PATH NIRMAN.

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना
विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:—यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज

19/12/2022

**Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj**

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RENEWAL/220/0023	DHOBNI GRAM SE CHUTAH GRAM TAK PATH NIRMAL.	318009001000	48 30.05.2022	2.630	159.930	143.90105	24.69530	16/22-23 16.09.2022	15.09.2023		2580	SDBC-25mm	5%	0.00000	0.00000	143.89655	Surface Complete

(Signature)
Divisional Account Officer
Rural Works Department
Works Division Narkatiaganj

(Signature)
Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

Name of Road - DHOBNI GRAM SE CHIUTAHA GRAM TAK PATH NIRMAN (Sec-21)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km				
22/11/22	11:39:5	21	0.1	220	0	2200	2189	ROAD	27.139670	84.610300	Normal
22/11/22	11:40:13	21	0.1	260	20.2	2600	2631	G	27.138760	84.610060	Normal
22/11/22	11:40:48	21	0.1	270	20.2	2700	2705	G	27.138010	84.609270	Normal
22/11/22	11:41:0	21	0.1	210	20.2	2100	2105	G	27.137320	84.608800	Normal
22/11/22	11:41:0	21	0.1	280	20.2	2800	2770	G	27.136540	84.608280	Normal
22/11/22	11:41:23	21	0.1	280	20.2	2800	2758	G	27.135870	84.607620	Curve
22/11/22	11:41:23	21	0.1	270	20.2	2700	2666	G	27.135280	84.607810	Normal
22/11/22	11:42:0	21	0.1	230	10.1	2300	2294	G	27.134960	84.608760	Normal
22/11/22	11:42:0	21	0.1	290	20.2	2900	2875	G	27.134650	84.609730	Curve
22/11/22	11:42:34	21	0.1	280	20.2	2800	2770	G	27.134270	84.610510	Normal
22/11/22	11:43:0	21	0.1	240	20.2	2400	2399	G	27.133340	84.610260	Normal
22/11/22	11:43:9	21	0.1	230	10.1	2300	2294	G	27.132490	84.610030	Normal
22/11/22	11:44:0	21	0.1	290	20.2	2900	2875	G	27.131670	84.609500	Normal
22/11/22	11:44:0	21	0.1	280	20.2	2800	2770	G	27.130770	84.609600	Normal
22/11/22	11:44:19	21	0.1	250	23.2	2500	2503	G	27.129900	84.609330	Curve
22/11/22	11:44:54	21	0.1	250	25.1	2500	2451	G	27.129040	84.609140	Normal
22/11/22	11:45:0	21	0.1	250	23.4	2500	2496	G	27.128160	84.609040	Curve
22/11/22	11:45:29	21	0.1	290	23.6	2900	2868	G	27.127390	84.608510	Normal
22/11/22	11:45:29	21	0.1	260	23.1	2600	2601	G	27.127750	84.607560	Normal
22/11/22	11:46:9	21	0.1	260	23.1	2600	2634	G	27.127880	84.606530	Normal
22/11/22	11:46:16	21	0.1	250	20.3	2500	2465	G	27.127440	84.605710	Normal
22/11/22	11:46:27	21	0.1	250	20.3	2500	2461	G	27.126910	84.604860	Curve
22/11/22	11:46:40	21	0.1	280	21.4	2800	2812	G	27.126330	84.604120	Normal
22/11/22	11:47:11	21	0.1	240	21.3	2400	2364	G	27.125650	84.603520	Normal
22/11/22	11:47:32	21	0.1	290	22.3	2900	2929	G	27.124860	84.603020	Normal
22/11/22	11:47:43	21	0.1	290	23.5	2900	2939	G	27.124110	84.602480	Normal
22/11/22	11:47:54	21	0.03	260	23.5	2600	2635	G	27.123360	84.601940	Normal
							Average IRI Value=				
							2580				

 J.E.
 A.E.

Executive Engineer
 Rural Works Department
 Works Division, Narkatiyaganj

Name of Customer : YOGENDRA SAH
 Name of Work/ Road : DHOBNI GRAM SE CHIUTAH
 Lab Job number :
 Date : 22-11-2022
 Section No. : 21

Test Date : 22-11-2022
 Machine No : 402
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : DHOBNI GRAM SE CHIUTAH
 Road Type : (R) RURAL ROAD
 Side :
 UV Range : 1105 To 4000
 Dist Range : 0 To 2.7
 Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Print

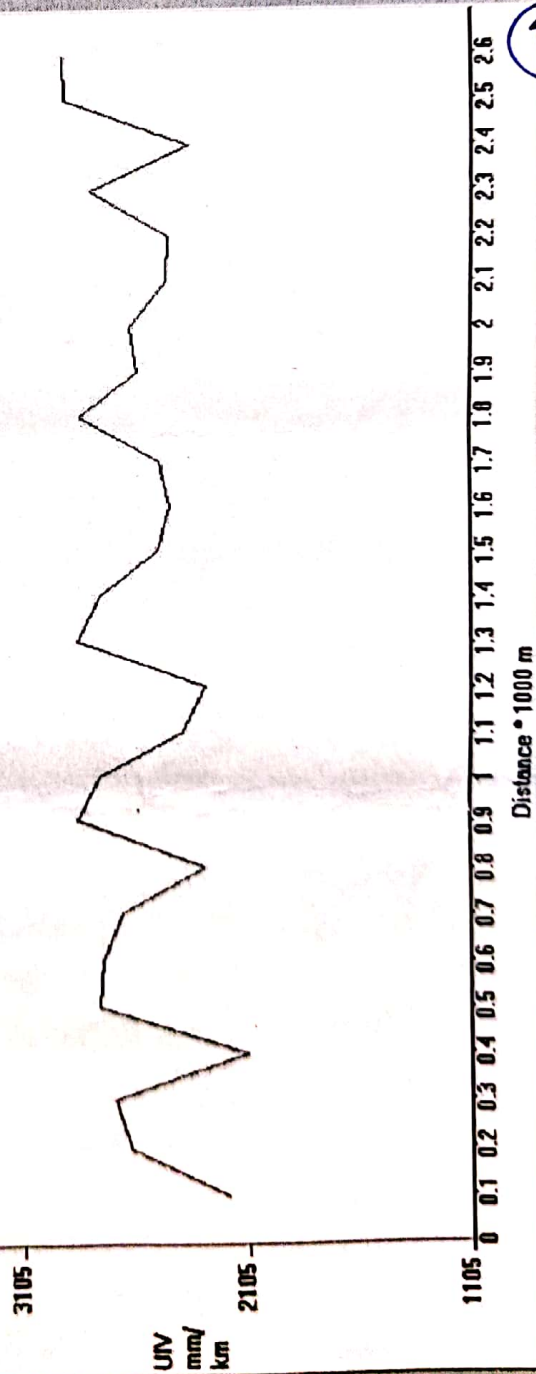
Generate Report and Graph

Redraw Graph

Map View

File : G:\635428742.xlsx, Section No. : 21, Eqn : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : YOGENDRA SAH, Name of Work/ Road : DHOBNI GRAM SE CHIUTAH GRAM TAK PATH



Distance * 1000 m


[Handwritten signatures and initials]

Executive Engineer
 Rural Works Department
 Works Division, (Narkatiyaganj)


Office of the Executive Engineer RWD Works Division, Narkatiaganj

Name of Road :- DHOBNI GRAM SE CHIUTAHA GRAM TAK PATH NIRMAN.
Name of Scheme :- MR 3054 New Maintenance Policy 2018
Name of Contractor :- Yogendra Sah
Length of Road :- 2.630 Km
Project ID :- 31808901009
Package No :- RM/WE/NAR/22/0023
Name of Block :- Mainatanr

Certified that all item wise 100% measurement has been taken by me

100%

J.E

Certified that all item wise 50% measurement has been Verified by me

A.E

10/12/22

Certified that all item wise 10% measurement has been taken by me


कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल
नरकटियागंज
