

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- ९६१

सासाराम/दिनांक:- 16.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।


प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- ER PARWEZ ALAM

1st Quarter - 27/08/2021 - 26/11/2021

1	Name of the Road	NAKATA ROAD - PHULWARI		
2	Batch No.	RM / RO / SAS / 20 / 0001		
3	Project ID	10301102060		
4	Total Length of Road (in Km)	0.55 KM		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.55 KM		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	5.06949 Lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.25347 Lakh		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGATATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.25347 Lakh

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav
Name and Designation of person inspection road

06.06.22
(Signature)

Date 06/06/22

Signature of person inspection road

AE

Certify by E/I [signature] Date:-

Name of Road : NAKTA PATH SE PHULWARIYA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
4/6/22	9:9:0	22	0.1	330	30.3	3300	3881 G	ROAD	24.98408	83.819528	Normal
4/6/22	9:9:10	22	0.1	320	20.2	3200	3767 G		24.983795	83.820437	Normal
4/6/22	9:10:0	22	0.1	330	20.2	3300	3881 G		24.98347	83.821312	Normal
4/6/22	9:10:20	22	0.1	300	20.2	3000	3540 G		24.983143	83.822205	Normal
4/6/22	9:10:20	22	0.1	290	20.2	2900	3426 G		24.982873	83.823315	Curve
Average IRI							3699				



$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001


 06.06.22
 J P

 06/06/2022
 A E
Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer : SHARDA BHAWANI INFRAST
Name of Work / Road : NAKTA PATH SE PHULWAR
Lab Job number : 22
Date : 4/6/2022
Section No. : 22

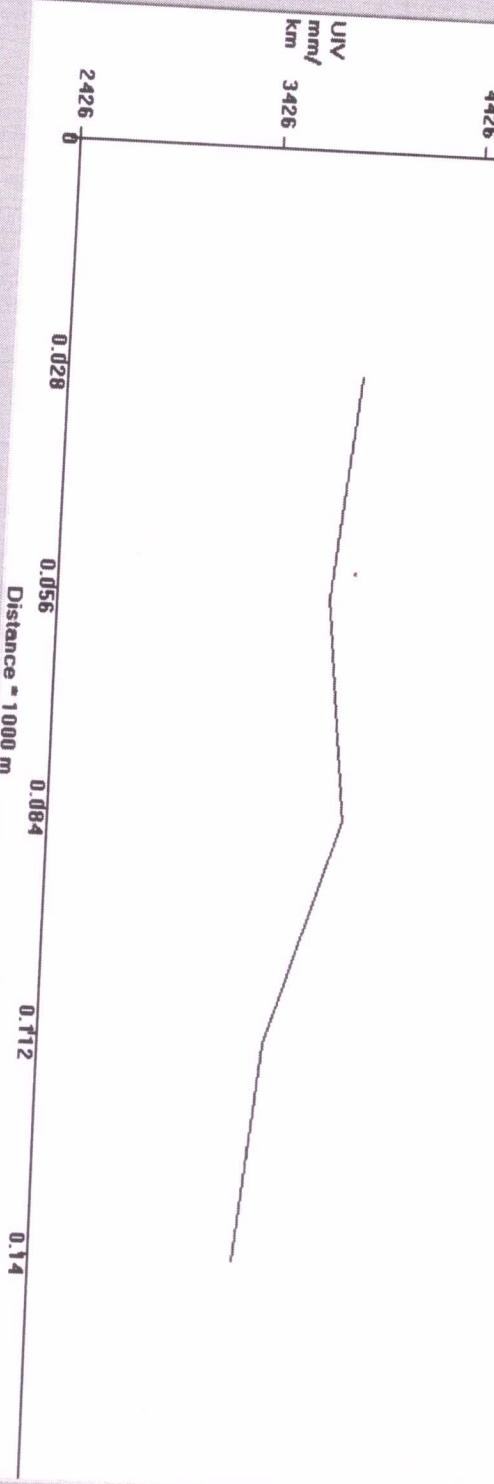
Test Date : 4/6/2022
Machine No. : 391
Start S No. : 264
Start E No. : 268
Weather : NORMAL
Start Location : 24.98408
End Location : 24.982873
Road Name : NAKTA PATH SE PHULWAR
Road Type : (R) RURAL ROAD
Side : CHENARI
U/V Range : 2426 To 5000 Interval 1000 mm/km
Dist Range : 0 To 0.168 Interval 0.028 = 1000 m
Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

File : E:\BUM INDICATOR REPORT\2022-23\JUN-24-6-24-6-2022.Xls, Section No. : 22, Eqn : test
 Name of Customer : SHARDA BHAWANI INFRASTRUCTURE, Name of Work / Road : NAKTA PATH SE



06.06.22
 06/06/2022
 AE
 16/6/22
