

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- 905 3170

सासाराम/दिनांक:- 31.5.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(30/06/2021 - 29/09/2021)

1	Name of the Road	Badkadih Viheo - Sishanpura		
2	Batch No.	RM/RO/SAS/19/0023		
3	Project ID	10301002148		
4	Total Length of Road (In Km)	1.6 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	1.6 Km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	12.94132		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.64707		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGETATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.64707

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road : BADKADIH UHRI ROAD SE SHIGANPURA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/5/22	16:49:21	11	0.1	310	20.2	3100	3654 G		24.855297	83.891413	Normal
27/5/22	16:50:0	11	0.1	260	30.3	2600	3086 G		24.855372	83.890437	Normal
27/5/22	16:50:0	11	0.1	260	20.2	2600	3086 G		24.855462	83.889393	Normal
27/5/22	16:50:33	11	0.1	280	20.2	2800	3313 G		24.854935	83.88882	Speed Breaker
27/5/22	16:50:33	11	0.1	270	30.3	2700	3199 G		24.854037	83.88872	Normal
27/5/22	16:51:0	11	0.1	310	30.3	3100	3654 G		24.853103	83.888687	Normal
27/5/22	16:51:8	11	0.1	310	20.2	3100	3654 G		24.852265	83.88872	Normal
27/5/22	16:51:8	11	0.1	260	20.2	2600	3086 G		24.851307	83.888635	Speed Breaker
27/5/22	16:51:44	11	0.1	280	20.2	2800	3313 G		24.85038	83.888535	Normal
27/5/22	16:51:44	11	0.1	300	20.2	3000	3540 G		24.849512	83.888	Curve
27/5/22	16:52:0	11	0.1	310	20.2	3100	3654 G		24.849598	83.887357	Normal
27/5/22	16:52:19	11	0.1	300	10.1	3000	3540 G		24.84969	83.886312	Normal
27/5/22	16:52:54	11	0.1	290	20.2	2900	3426 G		24.85007	83.885437	Normal
27/5/22	16:53:0	11	0.1	320	10.1	3200	3767 G		24.8503	83.884477	Normal
27/5/22	16:55:14	11	0.1	270	20.2	2700	3199 G		24.850298	83.884662	Normal
27/5/22	16:55:14	11	0.1	310	20.2	3100	3654 G		24.85003	83.885588	Normal
Average IRI							3427				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD
Good
Average 4001-5000
Poor >5001

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

28-05-22
JE

28/5/22
A.C.

Name of Customer : SHIVSHANKAR SINGH IFRA F
Name of Work/ Road : BADKADIH ULHI ROAD SE SH
Lab Job number : 11
Date : 27-05-2022
Section No. : 11

Test Date : 28-04-2010
Machine No. : 391
Road Name : BADKADIH ULHI ROAD SE SH
Road Type : (R) RURAL ROAD
Start S No. : 333
Side : SHEROSAGAP
Start E No. : 348
Interval :
Weather : NORMAL
U/V Range : 2086 To 5000 mm/km
Start Location : 24 855297
Dist Range : 0 To 0.532 0.028 ~ 1000 m
End Location : 24 85003
Equation : test


Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\27-5-22\1 TO 5.xlsx Section No. : 11, Egn : test

Name of Customer : SHIVSHANKAR SINGH IFRA PVT. LTD., Name of Work/ Road : BADKADIH ULHI ROAD SE

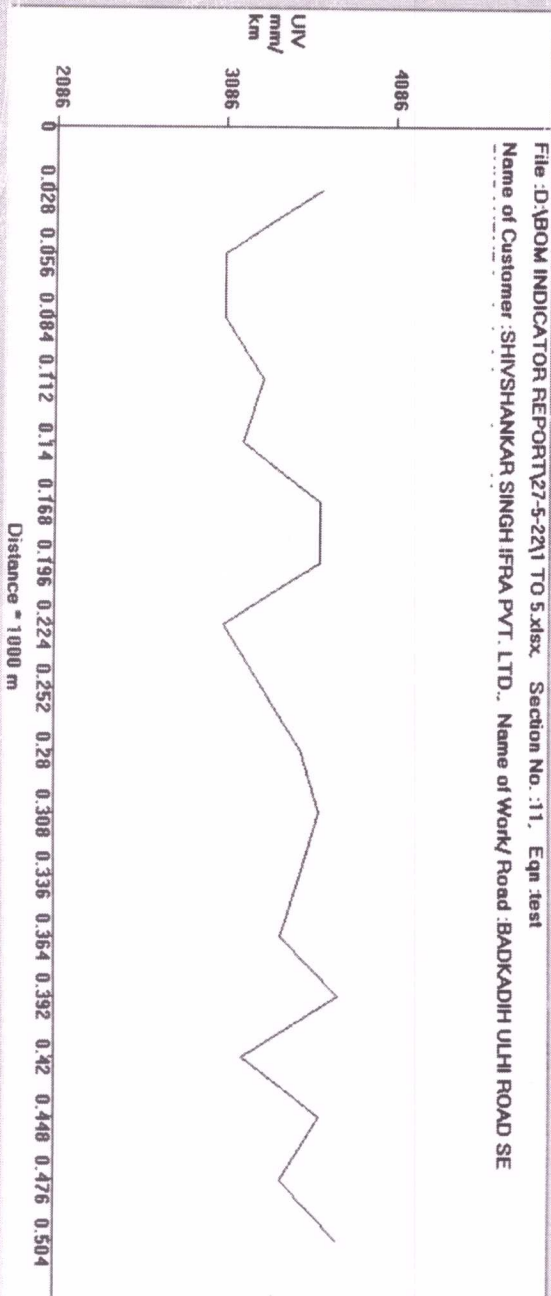

SHV
28/5/22
28/5/22
