

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1012

सासाराम/दिनांक:- 28.06.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-

Sasaram-1

2nd quarter
From 03/07/2021 to 02/10/2021

1	Name of the Road	Saxalya More to kali mandir in village kauaklonch		
2	Batch No.	AM/RD/SAS/19/0004		
3	Project ID	10301101048		
4	Total Length of Road (In Km)	1.83km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	1.83km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9.77349		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.48867		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	—
II	SHOULDERS AND EMBANKMENTS		10%	—
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	—
IV	SIGNAGE AND ROAD SAFETY		10%	—
V	VEGETATION		5%	—
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	—
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.48867

Date of inspection by E/I of his agent

Mahesh Prasad Sd
J.E.

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

Mahesh Prasad Sd
10-06-22.
(Signature)

Date 10/06/22

A. Prasad
10/06/22

Signature of person inspection road

28/6/22

Certify by E/I [signature] Date:-

Name of Road : KAUAAKHUCH SRAIYA MODE KALI MANDIR SE KAUAAKHUCH

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/5/22	10:11:5	94	0.1	330	10.1	3300	3881 G		24.931048	83.899225	Normal
27/5/22	10:11:40	94	0.1	310	20.2	3100	3654 G		24.931058	83.898265	Normal
27/5/22	10:12:0	94	0.1	340	10.1	3400	3994 G		24.931588	83.897575	Normal
27/5/22	10:12:17	94	0.1	300	20.2	3000	3540 G		24.931998	83.897053	Normal
27/5/22	10:13:28	94	0.1	260	20.2	2600	3086 G		24.931922	83.896278	Normal
27/5/22	10:19:4	94	0.1	300	30.3	3000	3540 G		24.934228	83.899512	Normal
27/5/22	10:19:4	94	0.1	250	30.3	2500	2972 G		24.935048	83.899697	Normal
27/5/22	10:19:39	94	0.1	340	30.3	3400	3994 G		24.935407	83.898905	Normal
Average IRI							3583				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

info@ssd
10-06-22
7/12

AE
10/06/22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1


Name of Customer :	NAVAL KISHOR SINGH
Name of Work/ Road :	KALUAKHOCH SPRATYA MODE
Lab Job number :	34
Date :	27-05-2022
Section No. :	34

Test Date :	27-05-2022	Road Name :	KALUAKHOCH SPRATYA MODE
Machine No :	391	Road Type :	(R) RURAL ROAD
Start S No :	149	Side :	KARGAHHAR
Start E No :	156	Interval :	
Weather :	NORMAL	U/V Range :	1972 To 5000 mm/km
Start Location :	24.931048	Dist Range :	0 To 0.252 0.028 = 1000 m
End Location :	24.935407	Equation :	test

Print **Generate Report and Graph**

Redraw Graph

Map View

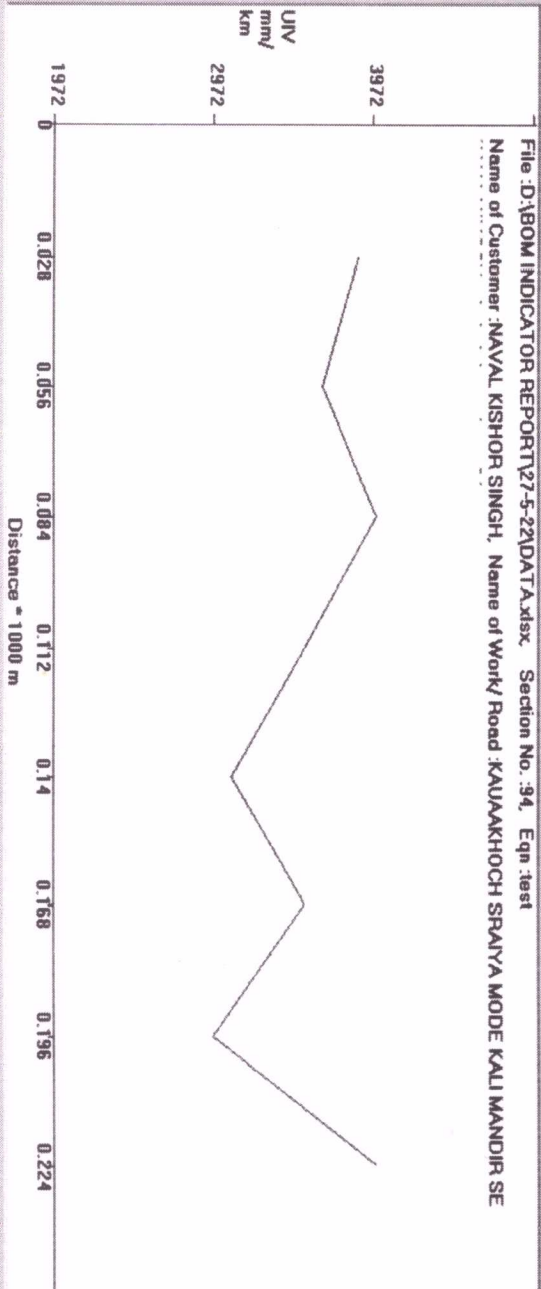

10-06-22
0'12

10/6/22
AE

28/6/22
