

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम-1

पत्रांक:- 1177 अ/30 दिनांक:- 19.7.2022

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सासाराम-1

सेवा में

नोडल पदाधिकारी,
3054 एम0 आर0 नई अनुरक्षण नीति-2018

ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष 3054 एम0 आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग:- विभागीय पत्रांक मु0 अ0-4(मु0) 3054-04-229/2021-97 अनु0/पटना
दिनांक- 07.01.2022

महाशय

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु-यथोक्त।

विश्वासभाजन

N. Kumar
19.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(02/07/2021 - 01/10/2021)

1	Name of the Road	Hardaspur - Barhua		
2	Batch No.	RM/RO/SAS/19/0012		
3	Project ID	10301002170		
4	Total Length of Road (In Km)	1.72 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	1.72 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	16.04028		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.80201		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGETATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.80201

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Customer:	Nawal Kishore Singh
Name of Work/Road:	Hardaspur To Bharathua
Lab Job number:	80
Date:	6/24/2022
Section No.	80


Test Date:	6/24/2022	Road Name:	Hardaspur To Bharathua
Machine No:	391	Road Type:	(R) RURAL ROAD
Start S No:	195	Side:	Kochas
Start E No:	212	Interval:	
Weather:	Normal	UIV Range:	1858 To 5000 mm/km
Start Location:	355.83.91.45.45	Dist Range:	0 To 0.532 0.028 * 1000 m
End Location:	012.83.91.9813	Equation:	test

Print

Generate Report and Graph

Redraw Graph

Map View

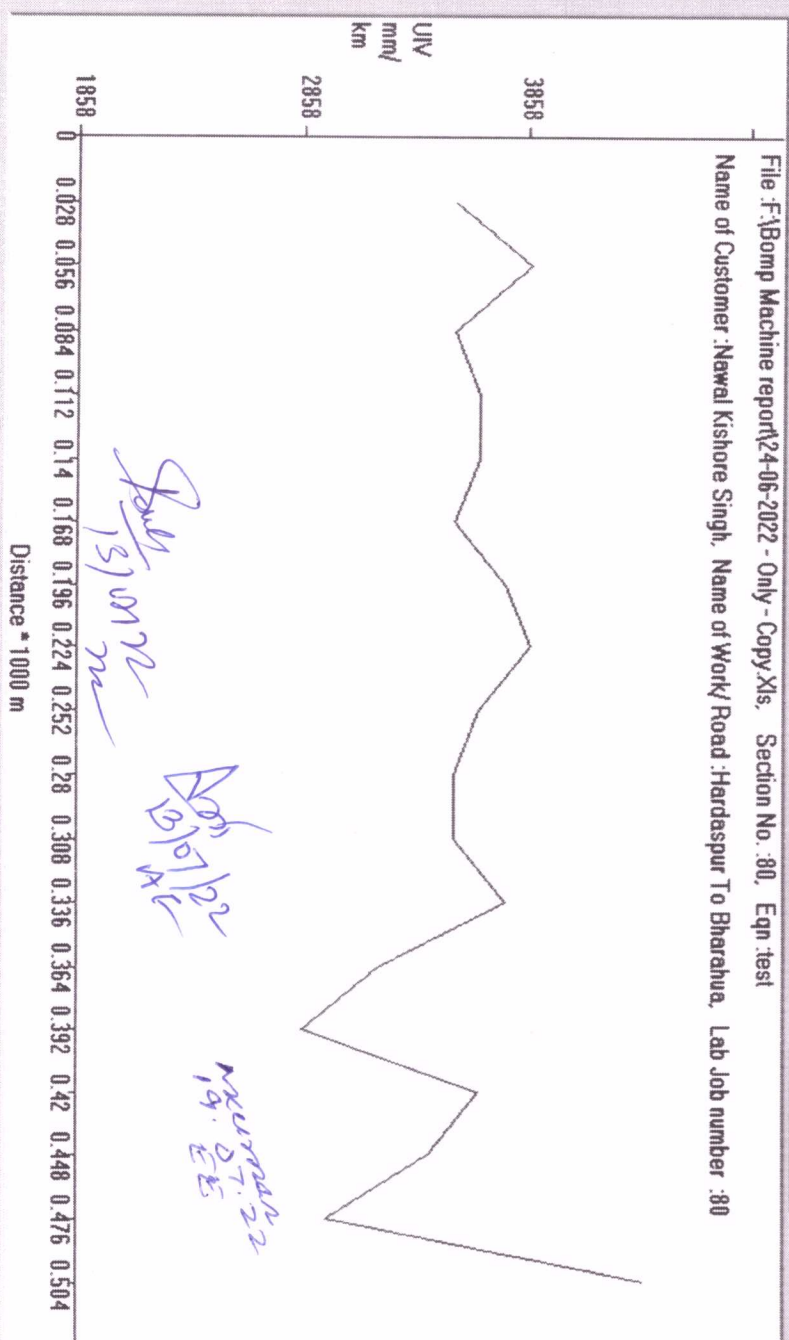

Name of Road:- Hardaspur To Bharahua

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGOR	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
24/6/22	11: 7: 1	80	0.1	300	0	3000	3540	G	25.291355	83.914545	Normal
24/6/22	11: 7: 36	80	0.1	330	20.2	3300	3881	G	25.29048	83.914747	Normal
24/6/22	11: 7: 36	80	0.1	300	30.3	3000	3540	G	25.289535	83.914882	Culvert
24/6/22	11: 8: 0	80	0.1	310	30.3	3100	3654	G	25.2887	83.914848	Normal
24/6/22	11: 8: 11	80	0.1	310	30.3	3100	3654	G	25.287748	83.914915	Normal
24/6/22	11: 8: 11	80	0.1	300	10.1	3000	3540	G	25.286823	83.914865	Normal
24/6/22	11: 8: 47	80	0.1	320	10.1	3200	3767	G	25.285952	83.914797	Normal
24/6/22	11: 9: 22	80	0.1	330	10.1	3300	3881	G	25.285073	83.914965	Normal
24/6/22	11: 9: 22	80	0.1	310	10.1	3100	3654	G	25.284177	83.91507	Normal
24/6/22	11: 10: 0	80	0.1	300	10.1	3000	3540	G	25.283465	83.915235	Curve
24/6/22	11: 10: 0	80	0.1	300	20.2	3000	3540	G	25.283102	83.916212	Normal
24/6/22	11: 10: 32	80	0.1	320	20.2	3200	3767	G	25.28277	83.917103	Normal
24/6/22	11: 11: 0	80	0.1	270	20.2	2700	3199	G	25.28241	83.918063	Normal
24/6/22	11: 11: 8	80	0.1	240	20.2	2400	2858	G	25.28207	83.918955	Normal
24/6/22	11: 11: 8	80	0.1	310	30.3	3100	3654	G	25.281727	83.919898	Normal
24/6/22	11: 12: 54	80	0.1	290	10.1	2900	3426	G	25.281127	83.920168	Normal
24/6/22	11: 13: 0	80	0.1	250	10.1	2500	2972	G	25.280273	83.919865	Normal
24/6/22	11: 13: 29	80	0.016	60	50.5	3750	4392	A	25.28012	83.919813	Normal
Average IRI:							3581				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3085$$

$$Y = 3637$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

802/13/08/22

13/07/22

Executive Engineer
Rural Work's Department
Works Division, Sasaram-1

19.07.22
