

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक- 1061 31/0

सासाराम/दिनांक:- 2.7.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :-

शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :-

विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महोदय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-

2nd Quarter [29/7/2021 to 28/10/2021]
Constn of Road from PWD Road to Kumbhari
Village upto Anurkuchi Banti
RM/RO/SAS/19/0021

1	Name of the Road			
2	Batch No.			
3	Project ID			
4	Total Length of Road (In Km)	10.30/10/18 1.92 km		
5	Length of Road to Meet Required Service Level [Complete Length] (in Km) [1]	1.92 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	15.79604		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.789802		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	
II	SHOULDERS AND EMBANKMENTS		10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	
IV	SIGNAGE AND ROAD SAFETY		10%	
V	VEGETATION		5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]	0.789802	

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav
Name and Designation of person inspection road

26.06.22
(Signature)

Date

26/5/22
Signature of person inspection road

26/5/22
Certify by E/I [signature] Date:-

Name of Road : PWD ROAD PATADI SE KEVTADI GAW SE ANUSUCHIT BASTI

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/5/22	7:43:0	76	0.1	330	0	3300	3881	G	24.909588	83.949528	Normal
25/5/22	7:43:0	76	0.1	230	30.3	2300	2745	G	24.908785	83.949932	Normal
25/5/22	7:43:0	76	0.1	200	30.3	2000	2404	G	24.907897	83.949882	Normal
25/5/22	7:43:0	76	0.1	200	40.4	2000	2404	G	24.90698	83.949865	Normal
25/5/22	7:43:34	76	0.1	330	20.2	3300	3881	G	24.906278	83.949965	Normal
25/5/22	7:43:34	76	0.1	280	30.3	2800	3313	G	24.906148	83.950875	Normal
25/5/22	7:44:9	76	0.1	320	20.2	3200	3767	G	24.906143	83.95173	Normal
25/5/22	7:44:9	76	0.1	260	30.3	2600	3086	G	24.905813	83.952693	Curve
25/5/22	7:44:9	76	0.1	260	30.3	2600	3086	G	24.906658	83.952945	Normal
25/5/22	7:44:45	76	0.1	310	20.2	3100	3654	G	24.907535	83.953215	Curve
25/5/22	7:45:0	76	0.1	260	30.3	2600	3086	G	24.907343	83.954057	Normal
25/5/22	7:45:0	76	0.1	230	30.3	2300	2745	G	24.907122	83.95503	Normal
25/5/22	7:45:20	76	0.1	240	40.4	2400	2858	G	24.906857	83.95606	Normal
25/5/22	7:45:20	76	0.1	340	20.2	3400	3994	G	24.90625	83.95648	Normal
25/5/22	7:45:20	76	0.1	210	30.3	2100	2518	G	24.905352	83.956312	Normal
25/5/22	7:45:55	76	0.1	190	30.3	1900	2290	G	24.904448	83.95616	Curve
25/5/22	7:46:0	76	0.1	260	10.1	2600	3086	G	24.904278	83.957205	Speed Breaker
25/5/22	7:47:6	76	0.1	340	10.1	3400	3994	G	24.903463	83.957288	Normal
25/5/22	7:48:0	76	0.1	330	10.1	3300	3881	G	24.904007	83.957272	Normal
Average IRI								3193			

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

26.05.22
Jc
26/5/22
A.E

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

26/5/22


Name of Customer : LALAN SHUKLA
Name of Work/ Road : PWD ROAD PATADI SE KEVT
Lab Job number : 76
Date : 25-05-2022
Section No. : 76

Test Date : 25-05-2022
Machine No. : 391
Road Name : PWD ROAD PATADI SE KEVT
Start S No. : 870
Road Type : (R) RURAL ROAD
Start E No. : 888
Side : SHEOSAGAR
Weather : NORMAL
Interval :
Ultrasonic Range : 1230 To 5000 mm/km
Start Location : 24.909588
Dist Range : 0 To 0.56 0.028 * 1000 m
End Location : 24.904007
Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

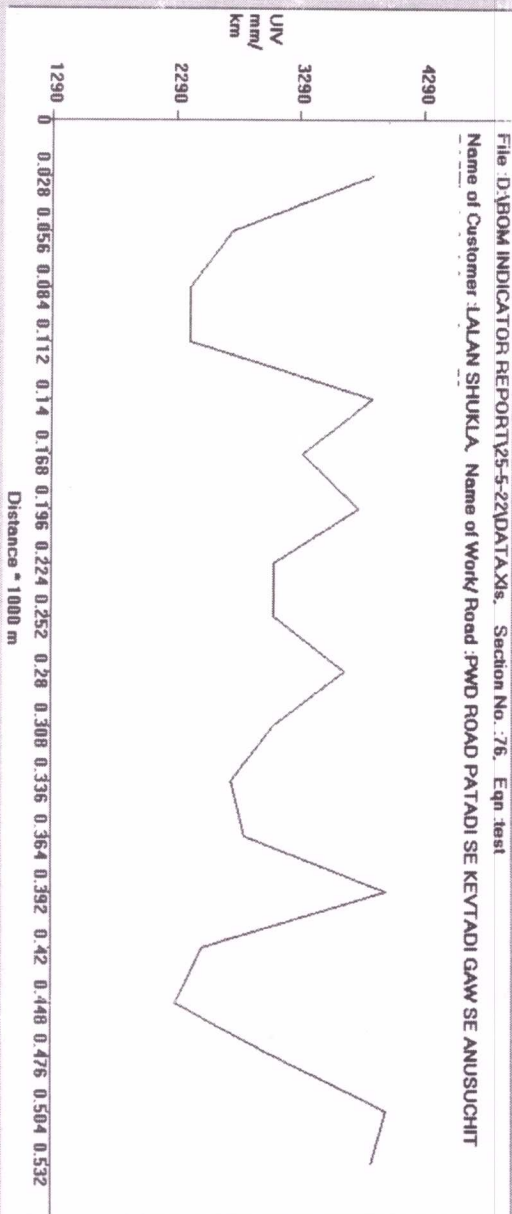

by 16.05.22

16.05.22

26/5/22
