

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल इमामगंज

पत्रांक १५०९..... इमामगंज/ दिनांक १५.०४.२०२२

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल इमामगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
(BRRDA)
बिहार - पटना।

विषय :- MR (3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक- मु0अ0 04(मु0)3054-04-229/2021-1135 (अनु0)/ पटना, दिनांक- 09.03.2022 एवं पत्रांक- 97 दिनांक- 07.01.2022


महाशय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR (3054) New Maintenance Policy-2018 (Package No.- RM/GA/IMA/20/0004) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- Standard Format for Roads
Quarterly Statement

विश्वासभाजन


कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल इमामगंज


STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (2nd Quarter)

NAME :- Rural Works Department Works Division Imamganj

1	Name Of Road	Beni Nagar to Vijua Road Via Vishunpur		
2	Batch No.	RM/GA/IMA/20/0004		
3	Project ID	10502307002		
4	Total Length Of Road(in Km)	4.5		
5	Lenth Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	4.5		
6	NO. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	41.73900		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.08695		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.08695

date of Inpection by E/I Or His Agent

Prepared by Contractor's Self Control Unit

Signature of Contractor

Name and Designation of person inspecting road

date

Signature of person inspecting road

(Signature)

Executive Engineer
Certify by E/I (Signature) date
RWD Works Division
Imamganj (Gaya)

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)													
Name Of Woks Division:- Imamganj				1 Year (2nd Quarter)									
Government Of Bihar													
OM01													
Rural Works Department													
SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT													
Road From:- Beni Nagar to Vijua Road Via Vishunpur (Package No.MR-N/19-20 Imamganj/20/0004)				To:- Executive Engineer RWD, Woks Division Imamganj									
Length of Road :- 4.500 Km				Date:-									
Period :- From:- 25-07-2021 To 24-10-2021				Position :- J.E									
Inspector :- J.E, Block : Dumaria													
No	Standard Of Work Item	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N/A	N/A	N/A	N/A							Not Required
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							N/A
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item	Work Unit	Unit Of Required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	302	Nil	2200	550							Defects Rectified within stipulated time
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

Shivani

Appendix

Executive Engineer, Works Division, Mangal

Name of Customer : SATYENDRA KUMAR
Name of Work/ Road : BENI NAGAR VIJUA ROAD VJ
Lab Job number :
Date : 20-07-2022
Section No. : 25


Test Date : 20-07-2022 Road Name : BENI NAGAR VIJUA ROAD VJ
Machine No : 212 Road Type : (R) RURAL ROAD
Start S No : Side : DUMARIA
Start E No : Interval
Weather : NORMAL UIV Range : 1478 To 5000 1000 mm/km
Start Location : BENI NAGAR Dist Range : 0 To 42 0.1 * 1000 m
End Location : VIJUA ROAD Equation : $Y = 0 * X^2 + 0.984 * X + 510.70$

Print

Generate Report and Graph

Redraw Graph

Map View

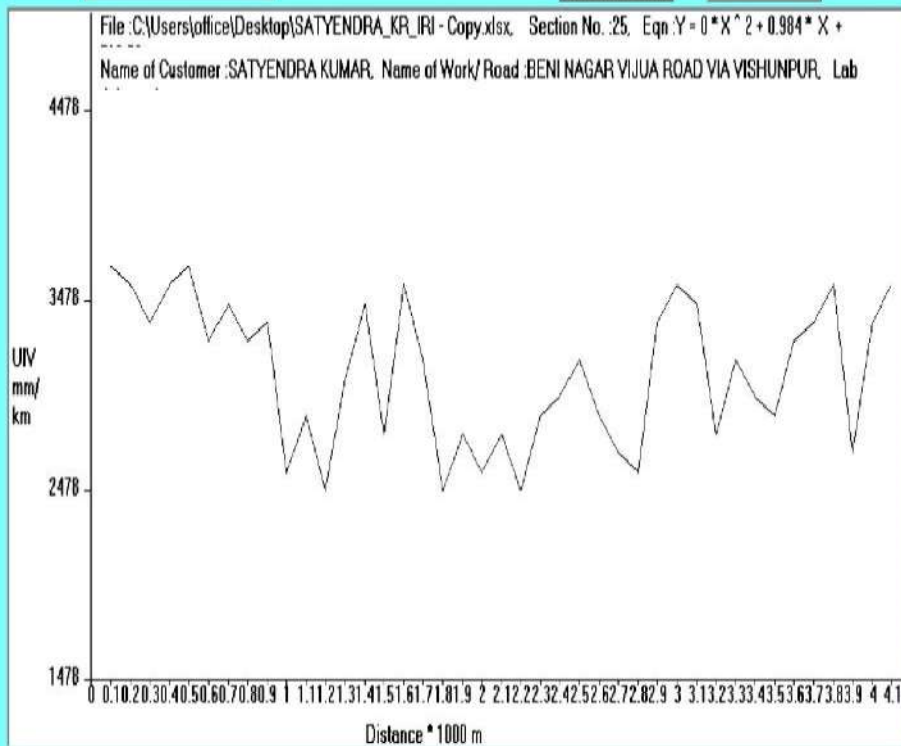

22/07/22

25/07/22

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI,TEGORY mm/km	Latitude .ongitude	Event
20-07-2022	16:40:0	25	0.1	320	32.5	3200	3659 G	24.4251 84.44741	Normal
20-07-2022	16:40:13	25	0.1	310	31.2	3100	3561 G	24.42442 84.44704	Normal
20-07-2022	16:40:13	25	0.1	290	32.5	2900	3364 G	24.42459 84.44635	Normal
20-07-2022	16:40:13	25	0.1	310	31.2	3100	3561 G	24.4253 84.44593	Normal
20-07-2022	16:41:0	25	0.1	320	32.5	3200	3659 G	24.42538 84.44498	Normal
20-07-2022	16:41:0	25	0.1	280	31.2	2800	3265 G	24.42606 84.44436	Normal
20-07-2022	16:41:23	25	0.1	300	32.5	3000	3462 G	24.42676 84.4438	Curve
20-07-2022	16:41:23	25	0.1	280	31.2	2800	3265 G	24.42678 84.44279	Normal
20-07-2022	16:41:23	25	0.1	290	32.5	2900	3364 G	24.42686 84.44182	Normal
20-07-2022	16:41:58	25	0.1	210	31.2	2100	2577 G	24.42688 84.44081	Normal
20-07-2022	16:42:0	25	0.1	240	32.5	2400	2872 G	24.42682 84.4398	Normal
20-07-2022	16:42:0	25	0.1	200	30.3	2000	2478 G	24.42685 84.43887	Normal
20-07-2022	16:42:0	25	0.1	260	31.2	2600	3069 G	24.42688 84.43781	Normal
20-07-2022	16:42:33	25	0.1	300	30.3	3000	3462 G	24.427 84.43687	Normal
20-07-2022	16:42:33	25	0.1	230	30.3	2300	2773 G	24.42716 84.43588	Normal
20-07-2022	16:43:9	25	0.1	310	30.3	3100	3561 G	24.42734 84.43495	Normal
20-07-2022	16:43:9	25	0.1	270	30.3	2700	3167 G	24.42753 84.43392	Normal
20-07-2022	16:43:44	25	0.1	200	30.3	2000	2478 G	24.42784 84.43301	Normal
20-07-2022	16:44:19	25	0.1	230	32.5	2300	2773 G	24.42799 84.432	Normal
20-07-2022	16:44:54	25	0.1	210	31.2	2100	2577 G	24.42805 84.43103	Normal
20-07-2022	16:45:0	25	0.1	230	30.3	2300	2773 G	24.42812 84.43003	Normal
20-07-2022	16:45:30	25	0.1	200	32.5	2000	2478 G	24.42832 84.42897	Normal
20-07-2022	16:45:30	25	0.1	240	31.2	2400	2872 G	24.42864 84.42806	Normal
20-07-2022	16:46:0	25	0.1	250	32.5	2500	2970 G	24.42899 84.42721	Normal
20-07-2022	16:46:5	25	0.1	270	30.3	2700	3167 G	24.42929 84.42621	Normal
20-07-2022	16:46:5	25	0.1	240	30.3	2400	2872 G	24.42957 84.41525	Normal
20-07-2022	16:46:40	25	0.1	220	31.2	2200	2675 G	24.4201 84.41461	Normal
20-07-2022	16:46:40	25	0.1	210	30.3	2100	2577 G	24.42039 84.41362	Normal
20-07-2022	16:47:0	25	0.1	290	32.5	2900	3364 G	24.42068 84.41271	Normal
20-07-2022	16:47:15	25	0.1	310	31.2	3100	3561 G	24.42117 84.41185	Normal
20-07-2022	16:47:15	25	0.1	300	32.5	3000	3462 G	24.42165 84.41106	Normal
20-07-2022	16:47:15	25	0.1	230	30.3	2300	2773 G	24.42212 84.41025	Normal

Y = 0 * X ^

X = 2700

Y = 3167

(R) RURAL

Good

<4000

20-07-2022	16:47:51	25	0.1	270	31.2	2700	3167 G	24,42262	84,40938	Normal
20-07-2022	16:48:0	25	0.1	250	30.3	2500	2970 G	24,42345	84,40899	Normal
20-07-2022	16:48:0	25	0.1	240	30.3	2400	2872 G	24,42421	84,40845	Normal
20-07-2022	16:48:0	25	0.1	280	30.3	2800	3265 G	24,42464	84,40759	Normal
20-07-2022	16:48:26	25	0.1	290	32.5	2900	3364 G	24,42485	84,40678	Normal
20-07-2022	16:48:26	25	0.1	310	31.2	3100	3561 G	24,42395	84,40663	Normal
20-07-2022	16:48:26	25	0.1	220	32.5	2200	2675 G	24,42367	84,40581	Normal
20-07-2022	16:49:0	25	0.1	290	31.2	2900	3364 G	24,42396	84,40488	Normal
20-07-2022	16:49:1	25	0.1	310	32.5	3100	3561 G	24,42417	84,40391	Normal


22/07/22


25/07/22
