

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।

पत्रांक - 923 / सिकहरना, ढाका, दिनांक- 30.06.2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
विश्वसरैया भवन, पाच्चा तल्ला, बिहार, पटना।

विषय :-


M/R (3054) New Maintenance Police 2018 योजना हेतु आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत M/R (3054) New Maintenance Police 2018 योजना के अधीन कराये गये कार्य के विरुद्ध भुगतान हेतु आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनुलग्नक :- यथोक्त।

विश्वासभाजन

 30.6.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।

FORM GFR 19-A


(See Government of India's Decision (1) below Rule-150)
Form of Utilization Certificate Upto the Month of upto.....

MR-3054

PIU :- EE RWD (W) DIVISION DHAKA

Sl.	Name of the Scheme	Sanction No. & Date with Amount (Rs. In Lakh)	Amount Received (Rs. In Lakh)	Particulars
1	Construction of Rural Roads Under MR-3054			Certified that out of Rs. Nil Lacs received the year 2022-23 in favor of Executive Engineer, R.W.D. (W), Division Dhaka a sum of Rs Nil lacks has been utilized for the purpose of MR-3054 Schemes as given in the margin for which it was sanctioned of Rs.Nil Remaining unutilized at the end of the period under.
Total :-				

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Divisional Account Officer


R.W.D. (W) Div., Dhaka

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conduct by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal Formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D.(W) Div., Dhaka

Steco Analyzer

Name of Customer : M/S Munna Kumar
Name of Work/ Road : ri Dhaka Senwariya se Khartari
Lab Job number :
Date : 27-03-2022
Section No. : 55

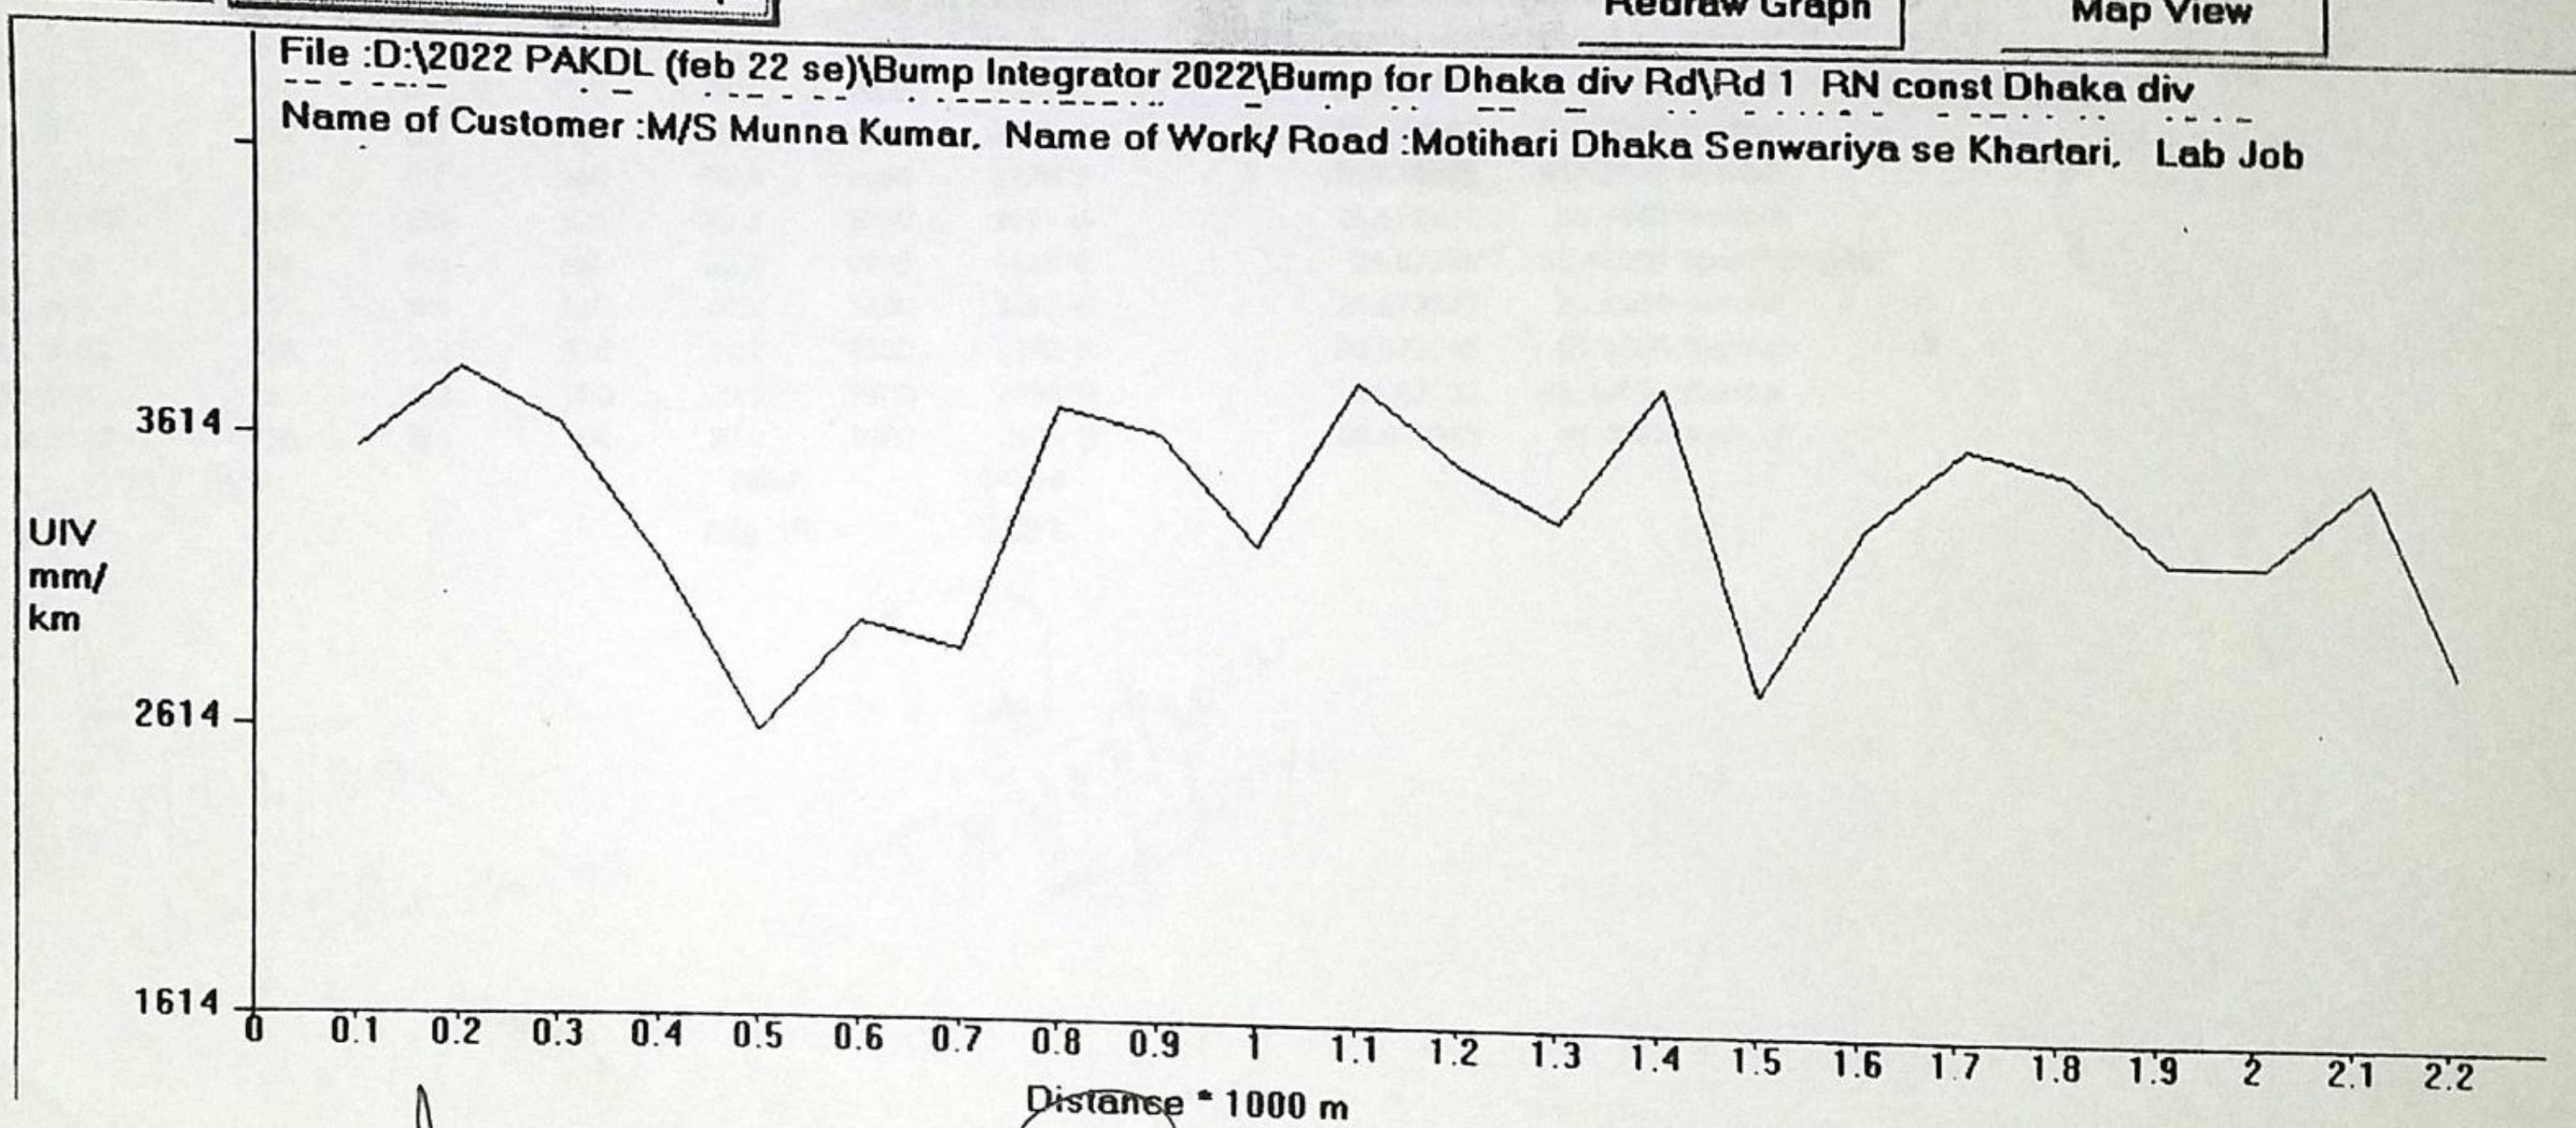
Test Date : 27-03-2022 Road Name : ri Dhaka Senwariya se Khartari
Machine No : 437 Road Type : (R) RURAL ROAD
Start S No : 0.000 Side :
Start E No : 2.200 Interval
Weather : Normal UIV Range : 1614 To 5000 1000 mm/km
Start Location : 26.682578, 85. Dist Range : 0 To 2.3 0.1 * 1000 m
End Location : 2358, 85.4749 Equation : $Y = 0 * X^2 + 0.954 * X + 134.5$

Print

Generate Report and Graph

Redraw Graph

Map View



27/03/22
JE/Chirmiya

27/03/2022
AB/Chirmiya

Name of Road :- Motihari Dhaka Senwariya se Khartari
Contractor Name:- M/S Munna Kumar

Scheme:- MR New Policy
Division:- Dhaka

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/3/22	13:56:26	55	0.1	360	0	3600	3568	G	26.682578	85.35185	Normal
27/3/22	13:56:26	55	0.1	390	20.2	3900	3855	G	26.68226	85.3611	Normal
27/3/22	13:57:1	55	0.1	370	30.3	3700	3664	G	26.681963	85.3712	Normal
27/3/22	13:57:1	55	0.1	320	30.3	3200	3187	G	26.681438	85.37895	Normal
27/3/22	13:57:1	55	0.1	260	30.3	2600	2614	G	26.680603	85.38215	Normal
27/3/22	13:57:36	55	0.1	300	30.3	3000	2996	G	26.67968	85.38502	Normal
27/3/22	13:57:36	55	0.1	290	20.2	2900	2901	G	26.678828	85.38	Normal
27/3/22	13:58:0	55	0.1	380	20.2	3800	3759	G	26.677947	85.3835	Normal
27/3/22	13:58:11	55	0.1	370	20.2	3700	3664	G	26.67705	85.3845	Normal
27/3/22	13:58:11	55	0.1	330	20.2	3300	3282	G	26.676232	85.37945	Normal
27/3/22	13:58:11	55	0.1	390	20.2	3900	3855	G	26.67533	85.37743	Curve
27/3/22	13:59:0	55	0.1	360	20.2	3600	3568	G	26.675057	85.38635	Normal
27/3/22	13:59:0	55	0.1	340	30.3	3400	3378	G	26.674865	85.39645	Normal
27/3/22	13:59:21	55	0.1	390	30.3	3900	3855	G	26.674635	85.40673	Normal
27/3/22	13:59:21	55	0.1	280	30.3	2800	2805	G	26.674498	85.41648	Normal
27/3/22	13:59:21	55	0.1	340	30.3	3400	3378	G	26.674355	85.42677	Normal
27/3/22	13:59:56	55	0.1	370	30.3	3700	3664	G	26.673837	85.4348	Normal
27/3/22	14:0:0	55	0.1	360	20.2	3600	3568	G	26.67308	85.44107	Speed Breaker
27/3/22	14:0:0	55	0.1	330	20.2	3300	3282	G	26.672842	85.4503	Normal
27/3/22	14:0:32	55	0.1	330	20.2	3300	3282	G	26.672595	85.4606	Normal
27/3/22	14:1:7	55	0.1	360	20.2	3600	3568	G	26.67252	85.47053	Normal
27/3/22	14:1:42	55	0.1	290	20.2	2900	2901	G	26.672358	85.4749	Normal
Total:-							74594				
Avg IRI :-							3391				

$$Y = 0 * X^2 + 0.954 * X + 134.5$$

$$X = 11695$$

$$Y = 11291$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

27/03/2022
J.E / Chiraiya

27/03/2022
AR / Chiraiya

Standard Format For Roads Quarterly Statement

5th Quarter

PIU Name :- R.W.D., Works Div. Dhaka

1	Name of Road	Motihari Dhaka Senwariya to Khartari		
2	Batch No.	RM/EA/SIK/13/0004		
3	Project ID	31708701004		
4	Total Length of road (in K.M)	2.20		
5	Length of road to Meet Required Service Level (Completed Length) (In K.M.)	2.20		
6	No. of Total Quarter (ie 3 months as a unit) in 5 Year	20		
7	Ordinary Maintenance Cost as per Schedule {Agreement Amount For maintenance (In Lakh)}	21.41077		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (In Lakh)	1.07000		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment (6) = (3)/(1)*(2)*(4)
		Length Non Compliant	Weighted Value for Payment Reduction (%)	
	Paved Roads (Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
Quarterly Payment as per Agreement				1.07000
Agreement Below 0.1 %				0.00107
To be paid for the Quarter/Demand (In Lakh)				1.06830

Date of Inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name of Designation of Person inspecting

(Signature)

[Signature]
30.6.22

Date :-

Signature of Person inspecting road

[Signature]
30/06/2022
JE

Certified by E/I (Signature) Date

Government of Bihar OM01 Rural Works Department			Summary of Ordinary Maintenance Inspection Report										
Road From :- Motihari Dhaka Senuwariya to Khartari (Package No.- RM/EA/SIK/19/0004)			To		Date :-								
Length of Road :- 2.200 Km Period From :- 16.06.2021 to 15.09.2021 Inspector :- AE, RWD, Sub Division, Chiraiya			Executive Engineer RWD, Works Division, Dhaka		Position :- A.E								
No.	Standard of Works Item Name	Work Unit	Unit of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Seales Payment												No Pot Hole Found
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							
OM102	Surface Depression and Rut Patching	m3	Nil	Nil	Nil	Nil							No Crack Sealing area Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							
OM104	Surface Treatment												No Loss of Aggregates not found
	(a) Loss of Agreegate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							
	© Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
105	Edge Repair	m2	Nil	Nil	Nil	Nil							Not Required
106	Digouts	m2	Nil	Nil	Nil	Nil							
107	Concrete pavement	m3	Nil	Nil	Nil	Nil							
	Other Activities		Nil	Nil	Nil	Nil							
OM200	Shoulder		Nil	Nil	Nil	Nil							
OM201	Unsealed Shoulder		Nil	Nil	Nil	Nil							
	(a) Edge Drop-off		Nil	Nil	Nil	Nil							Not Required
	(b) Roughness Scouring or potholes	Lm	Nil	Nil	Nil	Nil							
	© Holding Water	Lm	Nil	Nil	Nil	Nil							
OM202	Embankment Repair	Lm	Nil	Nil	Nil	Nil							
	Other activities (Rain Cuts)	M3	Nil	Nil	Nil	Nil							
OM300	Drainage including culverts major		Nil	Nil	Nil	Nil							
OM301	Surface Drains & Verge	Lm	Nil	Nil	Nil	Nil							Not Required
OM302	Culvert Cleanning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and Pit Repair	M3	Nil	Nil	Nil	Nil							
	Other activities (Whilw Washing)	M2	Nil	Nil	Nil	Nil							
	Standard of Work Item	Work	Nil	Nil	Nil	Nil	5	6	7	8	9	10	Comments
No.	Name	Unit	1	2	3	4							
OM400	Vegetation		Nil	Nil	Nil	Nil							
	Gross Control		Nil	Nil	Nil	Nil							
OM401	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							
	(b) Clear near Safety signs, Kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							
	Cutting of Branches of Trees	No	Nil	Nil	Nil	Nil							
	Cutting of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other Activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							
OM500	Safety Signage and Road		Nil	Nil	Nil	Nil							Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	Nil	Nil	Nil	Nil							Not Required
OM503	Distance Stones	No	Nil	Nil	Nil	Nil							
OM504	Road Marking	M2	Nil	Nil	Nil	Nil							
	Other activities												

Executive Engineer
RWD, Works Division, Dhaka

Bidder

Appendix

30/06/2022
JE
