

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अगु / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0- यथोक्त।

विश्वासभाजन,


कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :

1	Name of the Road	Jangiratha Bazar to Jangiratha Bazar		
2	Batch No.	RM/170/HAT/19/0003		
3	Project ID	31406901003		
	Total Length of Road (in Km)	3.5		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	3.5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	31.89065		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.5945325		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	00
II	SHOULDERS AND EMBANMENTS		10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	00
IV	SIGNAGE AND ROAD SAFETY		10%	00
V	VEGATAION		5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.59453

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

Certify by E/I [signature] Date:-

Name of work : Jagmohan Bazar to Jakhana Khas via Bara dhari Road
 Name of customer : GANDHU CHAPAR CONSTRUCTION PRIVATE LIMITED

(R/Rural Road	
Good	Average
< 4800	4801 - 5000
	Poor
	> 5000

Date	Time	Test No.	Distances	Total	Height	Speed	Ultrasonic	Corrected LR	RI	Status	Latitude	Direction	Longitude	Direction	Remarks
05/04/22	13:55:47	17	0	0	0.0 cm	16.2 Km/hr	0.0 mm/Km	245	0.43	Good	28.480247	N	84.289279	E	Normal
05/04/22	14:13:08	17	100	100	37.6 cm	16.2 Km/hr	3700.0 mm/Km	3709	4.87	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:18:49	17	100	200	37.6 cm	26.2 Km/hr	3700.0 mm/Km	3709	4.87	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:19:30	17	100	300	38.0 cm	30.2 Km/hr	2900.0 mm/Km	2960	3.88	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:19:41	17	100	400	38.0 cm	33.3 Km/hr	3600.0 mm/Km	3615	4.76	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:19:57	17	100	500	34.0 cm	34.2 Km/hr	3400.0 mm/Km	3428	4.54	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:11:01	17	100	600	37.0 cm	37.0 Km/hr	3700.0 mm/Km	3709	4.87	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:11:16	17	100	700	39.0 cm	26.7 Km/hr	3900.0 mm/Km	3896	5.09	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:11:30	17	100	800	37.0 cm	25.2 Km/hr	3100.0 mm/Km	3147	4.2	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:11:42	17	100	900	34.0 cm	33.0 Km/hr	3400.0 mm/Km	3428	4.54	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:11:54	17	100	1000	38.0 cm	28.4 Km/hr	3800.0 mm/Km	3802	4.88	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:12:11	17	100	1100	38.0 cm	21.8 Km/hr	3500.0 mm/Km	3521	4.85	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:12:27	17	100	1200	36.0 cm	22.7 Km/hr	3500.0 mm/Km	3653	4.09	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:12:47	17	100	1300	33.0 cm	16.1 Km/hr	3300.0 mm/Km	3334	4.43	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:13:01	17	100	1400	36.0 cm	22.8 Km/hr	3500.0 mm/Km	3521	4.05	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:13:17	17	100	1500	37.0 cm	23.0 Km/hr	3700.0 mm/Km	3709	4.87	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:13:28	17	100	1600	39.0 cm	31.3 Km/hr	3900.0 mm/Km	3896	5.09	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:13:37	17	100	1700	36.0 cm	30.2 Km/hr	3600.0 mm/Km	3615	4.76	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:13:48	17	100	1800	35.0 cm	33.8 Km/hr	3500.0 mm/Km	3521	4.85	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:14:00	17	100	1900	32.0 cm	31.2 Km/hr	3200.0 mm/Km	3241	4.32	Good	28.4611387	N	84.2896373	E	Normal
05/04/22	14:14:37	17	100	2000	33.0 cm	33.0 Km/hr	3300.0 mm/Km	3334	4.43	Good	28.4611387	N	84.2896373	E	Normal

R/R 14/13/10K

14/13/22
 14/13

14/13/22
 14/13

Name of work : Jagamatha Bazar to Jakhanna Khas via Baira dhar Road

Name of customer : GANDHU CHHAPAR CONSTRUCTION PRIVATE LIMITED

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000


05/04/22	14.14.50	17	100	2700	26.0 cm	17.6 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.15.50	17	100	2200	26.0 cm	6.6 Km/Hr	2900.0 mm/Km	2960	3.96	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.16.06	17	100	2300	27.0 cm	22.0 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.16.20	17	100	2400	31.0 cm	26.4 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.16.53	17	100	2500	36.0 cm	27.7 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.17.05	17	100	2600	33.0 cm	11.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.17.26	17	100	2700	33.0 cm	15.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.18.00	17	100	2800	35.0 cm	11.6 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.18.47	17	100	2900	35.0 cm	7.2 Km/Hr	2900.0 mm/Km	2960	3.96	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.20.06	17	100	3000	26.0 cm	4.3 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4611367	N	84.2865373	E	Normal
05/04/22	14.21.49	17	100	3100	26.0 cm	3.5 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4677420	N	84.2875333	E	Normal
05/04/22	14.22.30	17	100	3200	31.0 cm	8.7 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4675627	N	84.2694107	E	Normal
05/04/22	14.23.00	17	100	3300	37.0 cm	12.1 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4672135	N	84.2667006	E	Normal
05/04/22	14.23.16	17	100	3400	36.0 cm	20.4 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4681368	N	84.2697763	E	Normal
05/04/22	14.23.31	17	100	3500	34.0 cm	24.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4692665	N	84.2705393	E	Normal

R/R
12/col/100

12/3/22

12/3/22
A.R.

name of Customer: GANDHI CHHAPAR CONSTRUCTION PRIVATE LIMITED, Machine no: 19193, Road: Jagamatha Bazar to Ikhanna Khaz via Bara dhur Road, Date: 05/04/22, Section No: 17, Equation: $V=0.936X+24$

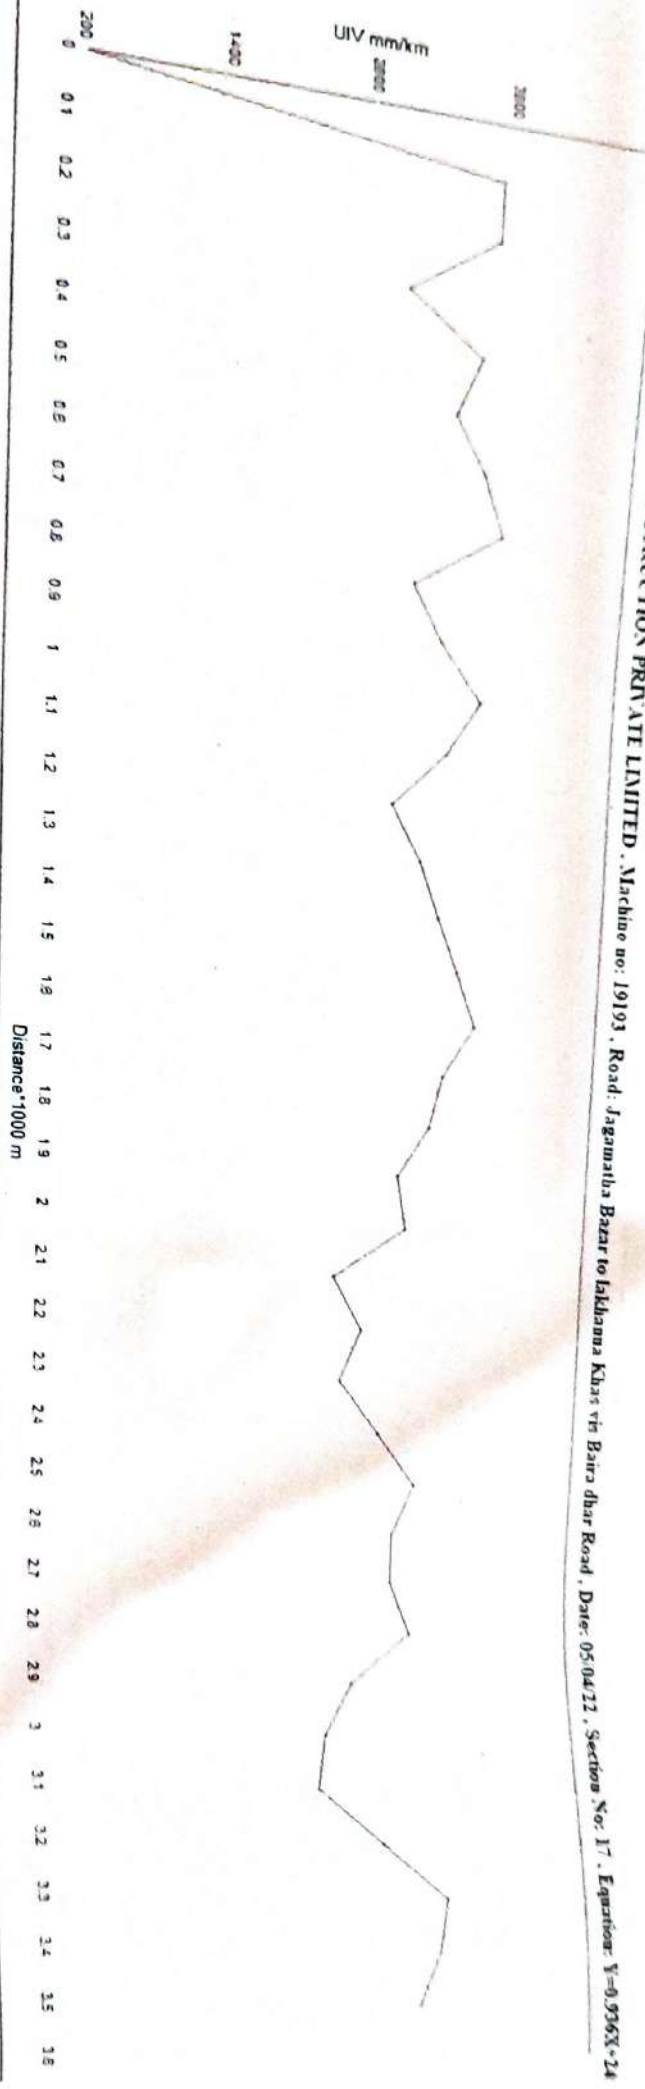

Rising 17/04/22

22/04/22

05/05/22

RWD, Works Division Hathua
Government Of Bihar
OMD1
Rural Works Department

Requisition Form for Scheme Head MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
1 Year (1st Quarter)

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road from:- Jagannatha Bajar to lakhana thas via baiba dhar road
Length of Road :- 3.500 Km
Inspector :- J.E RWD Sub Division : uchkagaon

To:-
Executive Engineer
RWD, Works Division Hathua
Position :- J.E

Date:-

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whitewashing)	M ²	Nil	Nil	Nil	Nil							Not Required

12/10/22

12/10/22

12/10/22

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
OM400	Vegetation	Unit	1	2	3	4	5	6	7	8	9	10	
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Ref: 17/01/2012

12/12/12
AE

12/05/12
BB
