

**कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल, पूर्वी चम्पारण।**

पत्रांक.....695 ३६२

पकड़ीदयाल,

दिनांक 3.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA,
बिहार, पटना।

**विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।**

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक—मु0अ0—4 (मु0)
3054—04—229 / 2021—2021—1135 अनु0 पटना दिनांक—09.03.2022

महाशय,

उपरोक्त विषयक एवं प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति—2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054 (New Maintenance Policy 2018) के अन्तर्गत MR-N/19-20 Pakridayal/-08 (1). Champapur To Mahamadipur. (2). Mangani Chowk To Alisherpur Via Brahaman Tola. (3) Pathkhauliya Siwan To Bakhari Main Road. (4) Shikarganj Pitch Road At Pakar Tree To Chamar Toli. पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाए। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए0टी0आर0 लंबित नहीं है।

अनु0 :- यथोक्त।

विश्वासभाजन

[Signature]
3/6/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

Standrad Format For Roads Quarterly Statement (4 th Quarter)

Name:- R.W.D.(W) Division, Pakridayal

1	Name of the Road	Pathkauliya Siwan To Bakhari Main Road.		
2	Batch No.	RM/EA/PAK/19/0008		
3	Project ID	31708607036		
4	Total Length of Road(in K.M.)	1.9		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	1.9		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	19.53770		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	0.97689		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				0.97689

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

Signature of Person inspecting road

(Signature)

Certify by E/I (Signature) Date

Requisition Form for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Division Pakridayal

Dist Of Bihar

Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

1 Year (4th Quarter)

From: Pathkauliya Siwan To Bakhari Main Road.
Package No. MR-N/19-20 Pakridayal/-08)

To:-

Executive Engineer
RWD, Works Division Pakridayal

Date:-

Length of Road :- 1.900 Km
Period :- From:- 16-07-2021 To 15-10-2021
Inspector :- A.E RWD Sub Division : Patahi

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment	m ²	16.03	10.69									Defects Rectified within stipulated time
OM101	Pothole Patching	m ³	0.05	0.03									Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	Lm	684.00	456.00									Defects Rectified within stipulated time
OM103	Crack Sealing												
	Surface Treatment	m ²	16.03	10.69									Defects Rectified within stipulated time
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil									No Bleeding/ Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil									No Crocodile Cracking Found
	© Crocodile Cracking	m ²	Nil	Nil									No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil									Defects Rectified within stipulated time
106	Digouts	m ³	1.20	0.80									
107	Concrete pavement	m ³	N.A	N.A									
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder	Lm	Nil	Nil									No Edge Drop-Off Required
OM201	(a) Edge Drop-off	Lm	179.55	119.70									Defects Rectified within stipulated time
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil									No Holding Water Found
	(c) Holding water	M ³	26.93	17.96									Defects Rectified within stipulated time
OM202	Embankment Repair		Nil	Nil									Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major	Lm	N.A	N.A									Not Required
OM301	Surface Drains & Verge	No	2	1									Defects Rectified within stipulated time
OM302	Culvert Cleaning	M ³	Nil	Nil									Not Required
OM303	Culvert and pit Repair	M ²	40	23									Defects Rectified within stipulated time
	Other activities (Whitewashing)												

Sl. No.	Work Item	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
	Vegetation Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
	Tree and Shrub Management	No	Nil	Nil									Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil									Defects Rectified within stipulated time
	Cutting Of Shrubs From Road Way	No	684.00	456.00									Defects Rectified within stipulated time
OM402	Other activities (Trimming of Grass)	M ²	1436.40	957.60									Not Required
OM500	Safety Signage and Road		Nil	Nil									Defects Rectified within stipulated time
OM501	Signs Maintenance	No	0.95	Nil									Defects Rectified within stipulated time
OM502	Guard Stones	Lm	2	2.56									Defects Rectified within stipulated time
OM503	Distance Stones	No	0.95	Nil									Not Required
OM504	Road Marking	M ²	Nil	Nil									
	Other activities												

2/16/22
G.E

2/16/22
SPM
Ar

2/16/22
Executive Engineer,
RWD, Works Division, Pakridayal.

Name of Road :- Patkhailiya Siwan to Bakhari Main road
Contractor Name:- M/S S. K. BUILDERS

Date Time

Section No.

Length in km

Bumps in mm

Speed Rate

OR mm/km

IRI mm/km ROAD

CATEGORY

Latitude

Longitude

Event

Scheme:- MR New Policy
Division:- Pakridayal

Y = 0 * X ^ 2 + 0.954 * X + 134.5
X = 11695
Y = 11291

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

	NO.	in km	in mm	Rate	mm/km	mm/km ROAD	Latitude	Longitude	Event
12/5/22	16: 5: 0	28	0.1	390	0	3900	3855 G	26.597408	85.174797 Curve
12/5/22	16: 6: 1	28	0.1	370	20.2	3700	3664 G	26.59822	85.174848 Normal
12/5/22	16: 6: 1	28	0.1	310	10.1	3100	3091 G	26.59909	85.175185 Normal
12/5/22	16: 6: 36	28	0.1	350	30.3	3500	3473 G	26.59936	85.174377 Normal
12/5/22	16: 6: 36	28	0.1	370	30.3	3700	3664 G	26.599527	85.17338 Normal
12/5/22	16: 7: 0	28	0.1	310	10.1	3100	3091 G	26.59968	85.172373 Normal
12/5/22	16: 7: 11	28	0.1	350	20.2	3500	3473 G	26.59987	85.171548 Normal
12/5/22	16: 7: 11	28	0.1	340	20.2	3400	3378 G	26.600103	85.170572 Normal
12/5/22	16: 7: 46	28	0.1	330	30.3	3300	3282 G	26.60062	85.169865 Normal
12/5/22	16: 8: 0	28	0.1	280	40.4	2800	2805 G	26.601345	85.169225 Curve
12/5/22	16: 8: 0	28	0.1	280	30.3	2800	2805 G	26.601732	85.16838 Normal
12/5/22	16: 8: 21	28	0.1	360	30.3	3600	3568 G	26.602092	85.16739 Normal
12/5/22	16: 8: 21	28	0.1	330	20.2	3300	3282 G	26.602095	85.166548 Normal
12/5/22	16: 9: 0	28	0.1	320	20.2	3200	3187 G	26.60234	85.165555 Normal
12/5/22	16: 9: 0	28	0.1	320	20.2	3200	3187 G	26.60175	85.164932 Normal
12/5/22	16: 9: 32	28	0.1	270	20.2	2700	2710 G	26.601008	85.164427 Normal
12/5/22	16: 9: 32	28	0.1	310	10.1	3100	3091 G	26.600487	85.163737 Normal
12/5/22	16: 10: 0	28	0.1	370	30.3	3700	3664 G	26.600798	85.162845 Normal
12/5/22	16: 10: 7	28	0.1	340	20.2	3400	3378 G	26.600163	85.162355 Normal

S.K. Builders
3/6/22
S.E.

3/6/22
S.E.

3/6/22
S.E.

Name of Customer : M/S S. K. BUILDERS
Name of Work/ Road : Pakhailiya Siwan to Bakhari M Road
Lab Job number :
Date : 12-05-2022
Section No. : 28


Test Date : 12-05-2022
Machine No : 437
Start S No :
Start E No :
Weather : Normal
Start Location :
End Location :
Road Name : Iya Siwan to Bakhari Main road
Road Type : (R) RURAL ROAD
Side :
Interval :
UV Range : 1710 To 5000 mm/km
Dist Range : 0 To 2 0.1 1000 m
Equation : $Y = 0 * X^2 + 0.954 * X + 134.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\2022 PAKDL (Feb 22 se)\Bump Integrator 2022\Pakridayal Div Rd Bump\Bump Read SK Builder 12.5.22\Bump
 Name of Customer : M/S S. K. BUILDERS, Name of Work/ Road : Pakhailiya Siwan to Bakhari Main road, Lab Job

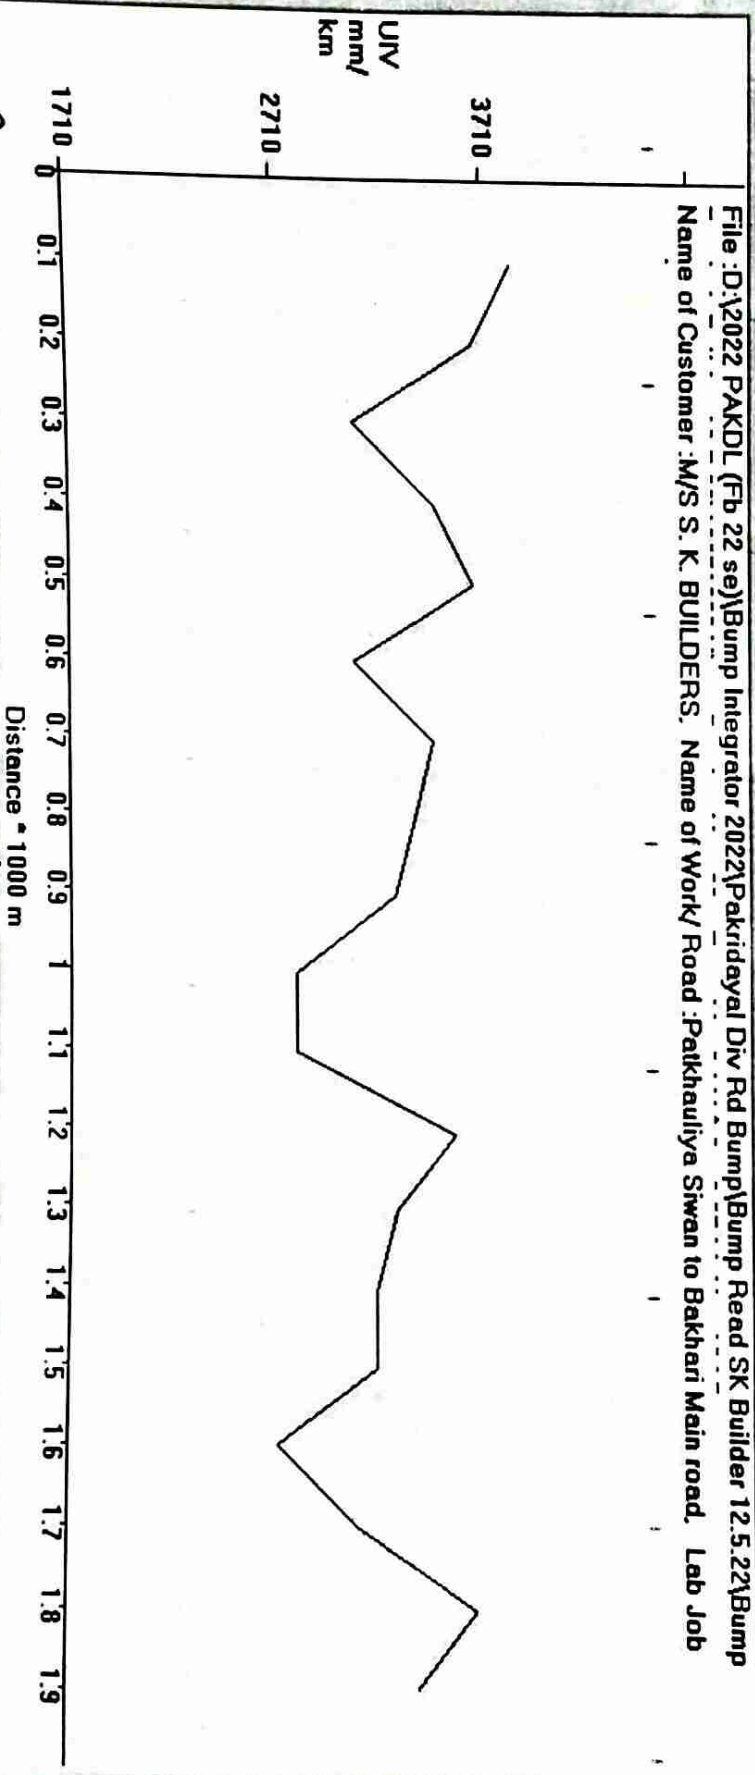

3/6/22
 S.E

3/6/22
 S.E

3/6/22
 S.E
