

**कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल, पूर्वी चम्पारण।**

पत्रांक.....**772 अनु०**

पकड़ीदयाल,

दिनांक **20.6.22**

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA,
बिहार, पटना।

**विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पॉच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।**

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक—मु0अ0—4 (मु0)
3054—04—229 / 2021—2021—1135 अनु0 पटना दिनांक—09.03.2022

महाशय,

उपरोक्त विषयक एवं प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति—2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054 (New Maintenance Policy 2018) के अन्तर्गत MR-N/19-20 Pakridayal/-05 (1). Chaita To Shopur Kundal. (2). Hathial Jharilal Prasad Mandir To Harnathpur Pandey Raut. (3) Mathaba R.E.O Road To Ramnagar Culvert Via Hathiaul. (4) Chorma Chowk To Sirha Village. (5) Hathiaul Sakal Dev Paswan House To R.E.O Road. पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाए। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद उक्त पथों में ए0टी0आर0 लंबित नहीं है।

अनु0 :- यथोक्त।

विश्वासभाजन

(Signature)
20/6/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।
(Signature)

1 Year (2nd Quarter)

Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

From:- Hathiaul Jharial Prasad Mandir To Hmaphur Pandey Raut,
Package No. MR-N/19-20 Pakridayal/-05)

Length of Road :- 0.850 Km

Period :- From:- 24-06-2021 To 23-09-2021

Inspector :- A.E RWD Sub Division : Pakridayal

To:-

Executive Engineer
RWD, Works Division Pakridayal

Date:-

Position :- A.E

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil											Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil											No Crack sealing Found
OM103	Crack Sealing	Lm	Nil											No Loss Of Aggregates (Surface Ravelling) Found
	Surface Treatment													No Bleeding / Flushing Required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil											No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil											No Edge Repair Required
	© Crocodile Cracking	m ²	Nil											
105	Edge Repair	m ²	Nil											
106	Digouts	m ²	N.A											
107	Concrete pavement	m ³	N.A											
	Other activities													
OM200	Shoulder													No Edge Drop-Off Required
	Unsealed Shoulder													Not Required
OM201	(a) Edge Drop-off	Lm	Nil											No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	Nil											Not Required
	(c) Holding water	Lm	Nil											Not Required
OM202	Embankment Repair	M ³	Nil											Not Required
	Other activities (Rain Cuts)													
OM300	Drainage including culverts major													Not Required
OM301	Surface Drains & Verge	Lm	N.A											Not Required
OM302	Culvert Cleaning	No	Nil											Not Required
OM303	Culvert and pit Repair	M ³	Nil											Not Required
	Other activities (Whilw washing)	M ²	Nil											

4

Id Of Work Item	Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
	Vegetation												
	Grass Control												
	a) Roadside- General Tidy	Ha	Nil										Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil										Not Required
	Tree and Shrub Management	No	Nil										Not Required
	Cutting Of Branches Of Trees	No	Nil										Not Required
	Cutting Of Shrubs From Road Way	No	Nil										Not Required
	Other activities (Trimming of Grass)	M ²	Nil										Not Required
OM402	Safety Signage and Road		Nil										Not Required
OM500	Signs Maintenance	No	Nil										Not Required
OM501	Guard Stones	Lm	N.A										Not Required
OM502	Distance Stones	No	N.A										Not Required
OM503	Road Marking	M ²	Nil										Not Required
OM504	Other activities												

Wagwan
20.6.22
DE

Suman
20/6/22
AF

Executive Engineer,
RWD. Works Division, Pakridayal.
20/6/22

Standrad Format For Roads Quarterly Statement (2 nd Quarter)

10 Name:- R.W.D.(W) Division, Pakridayal

1	Name of the Road	Hathiaul Jharilal Prasad Mandir To Hrnathpur Pandey Raut.		
2	Batch No.			
3	Project ID	31708607024		
4	Total Length of Road(in K.M.)	0.85		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	0.85		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	8.71584		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	0.43579		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				0.43579

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

(Signature)

Signature of Person inspecting road

Certify by E/I (Signature) Date

Road :- Hathiaul Jharial Prasad Mandir to Haranathpur Pandey Raut
 Cor Name:- Braj Bihari Singh

Scheme:- MR New Maintenance Policy

Division:- Pakridayal

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	
9/6/22	11:25:12	41	0.1	320	0	3200	3187 G		26.614235	85.122625	Normal	$Y = 0 * X^2 + 0.954 * X + 134.5$
9/6/22	11:26:0	41	0.1	320	20.2	3200	3187 G		26.614795	85.121918	Normal	$X = 11695$
9/6/22	11:26:25	41	0.1	370	30.3	3700	3664 G		26.615257	85.121127	Normal	$Y = 11291$
9/6/22	11:26:25	41	0.1	330	30.3	3300	3282 G		26.61548	85.12013	Normal	
9/6/22	11:27:0	41	0.1	350	10.1	3100	3091 G	(R) RURAL ROAD	26.615607	85.11914	Normal	
9/6/22	11:27:36	41	0.1	340	20.2	3500	3473 G	Good	26.616005	85.118282	Normal	Average
9/6/22	11:28:0	41	0.1	370	30.3	3400	3378 G	Poor	26.61629	85.11749	Normal	<4000
9/6/22	11:28:1	41	0.05	330	30.3	3700	3664 G		26.616215	85.116532	Normal	4001-5000
						3300	3282 G		26.616217	85.116534	Normal	>5001
Total:-							30208					
Avg IRI :-							3356					

Aggaveen
 20.06.22
 DE


Suman
 20/6/22
 AE

h n/y
 22

Name of Customer : Braj Bihari Singh
Name of Work/ Road : Highway No. 1 Prasad Mandir
Lab Job number :
Date : 09-06-2022
Section No. : 41

Test Date : 09-06-2022
Machine No. : 437
Start S No. :
Start E No. :
Weather :
Start Location :
End Location :
Road Name : Sir to Haranathpur Pandey Rout
Road Type : (R) RURAL ROAD
Side :
Interval :
U/V Range : 2031 To 5000 mm/km
Dist Range : 0 To 1 0.1 * 1000 m
Equation : $Y = 0 \cdot X^2 + 0.954 \cdot X + 134.5$

File : D:\2022\Bump Integrator 2022\Pakridayal Div Rd Bump\Braj Bihari 8 Rd Mt 9.5.22\Bump Re
 Name of Customer : Braj Bihari Singh. Name of Work/ Road : Hathiaul Jhalilal Prasad Mandir to Haranathpur Pandey

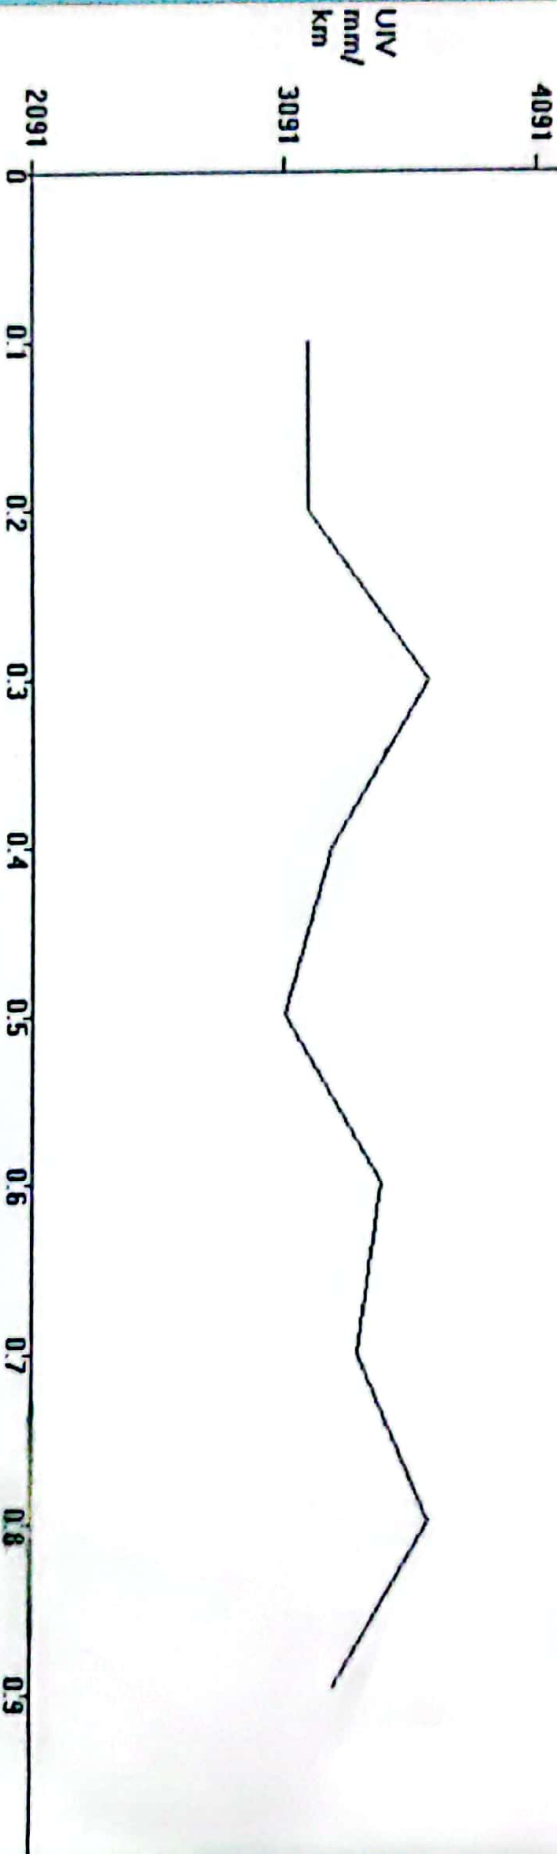

Vagdevan
 20.6.22
 Suman
 20.6.22
 DE
 20.6.22
