

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:— 1017

सासाराम/दिनांक:— 28.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :— शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :— विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :— यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-

Sasaram-1

From 2nd Quarter
From 30/06/2021 to- 29/09/2021

1	Name of the Road	Kargahar Barchari - Reharu		
2	Batch No.	RPI/RO/SAS/19/0004		
3	Project ID	10301002093		
4	Total Length of Road (In Km)	1.52 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	1.52 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	8.23943		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.41197		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	—
II	SHOULDERS AND EMBANKMENTS		10%	—
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	—
IV	SIGNAGE AND ROAD SAFETY		10%	—
V	VEGETATION		5%	—
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		—
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.41197

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Mahesh Prasad Sah
J.E.

Name and Designation of person inspection road

Mahesh Prasad Sah
10-06-22

(Signature)

Date 10/06/22

Mahesh Prasad Sah
10/6/22

Signature of person inspection road

Mahesh Prasad Sah
28/6/20

Certify by E/I [signature] Date:-

Name of Road : KARGAHAR BADAHRI ROAD SE REHADI

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
27/5/22	11: 21: 42	1	0.1	300	20.2	3000	3540	G	25.158603	83.999023	Normal
27/5/22	11: 22: 0	1	0.1	310	30.3	3100	3654	G	25.157708	83.998855	Normal
27/5/22	11: 22: 0	1	0.1	270	30.3	2700	3199	G	25.157055	83.998602	Normal
27/5/22	11: 22: 20	1	0.1	290	40.4	2900	3426	G	25.15611	83.99837	Normal
27/5/22	11: 22: 20	1	0.1	340	30.3	3400	3994	G	25.15611	83.99837	Normal
27/5/22	11: 22: 20	1	0.1	290	30.3	2900	3426	G	25.15611	83.99837	Normal
27/5/22	11: 22: 20	1	0.1	290	40.4	2900	3426	G	25.15611	83.99837	Normal
27/5/22	11: 22: 55	1	0.1	290	30.3	2900	3426	G	25.15611	83.99837	Normal
27/5/22	11: 22: 55	1	0.1	260	30.3	2600	3086	G	25.15611	83.99837	Normal
27/5/22	11: 22: 55	1	0.1	290	30.3	2900	3426	G	25.15611	83.99837	Normal
27/5/22	11: 23: 31	1	0.1	340	10.1	3400	3994	G	25.15611	83.99837	Normal
27/5/22	11: 24: 6	1	0.1	340	10.1	3400	3994	G	25.15611	83.99837	Normal
27/5/22	11: 24: 41	1	0.1	330	20.2	3300	3881	G	25.15611	83.99837	Normal
27/5/22	11: 24: 41	1	0.1	320	20.2	3200	3767	G	25.15611	83.99837	Normal
27/5/22	11: 25: 16	1	0.1	290	30.3	2900	3426	G	25.15611	83.99837	Normal
Average IRI							3578				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD
Good
Average 4001-5000 Poor >5001

10-06-22

5'12

AE

10/06/22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer: NAVAL KISHOR SINGH
Name of Work/Road: KARGAHAR BADAHRI ROAD
Lab Job number: 1
Date: 27-05-2022
Section No.: 1

Test Date: 27-05-2022
Road Name: KARGAHAR BADAHRI ROAD
Machine No.: 391
Road Type: (R) RURAL ROAD
Start S No.: 15
Side: KARGAHAR
Start E No.: 29
Interval:
Weather: NORMAL
UV Range: 2086 To 5000 mm/km
Dist Range: 0 To 0.476 0.028 ~ 1000 m
Start Location: 25.158603
End Location: 25.15611
Equation: $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$


Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\27-5-22\123.Xls, Section No.: 1, Eqn : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : NAVAL KISHOR SINGH, Name of Work/ Road : KARGAHAR BADAHRI ROAD SE REHADL, Lab

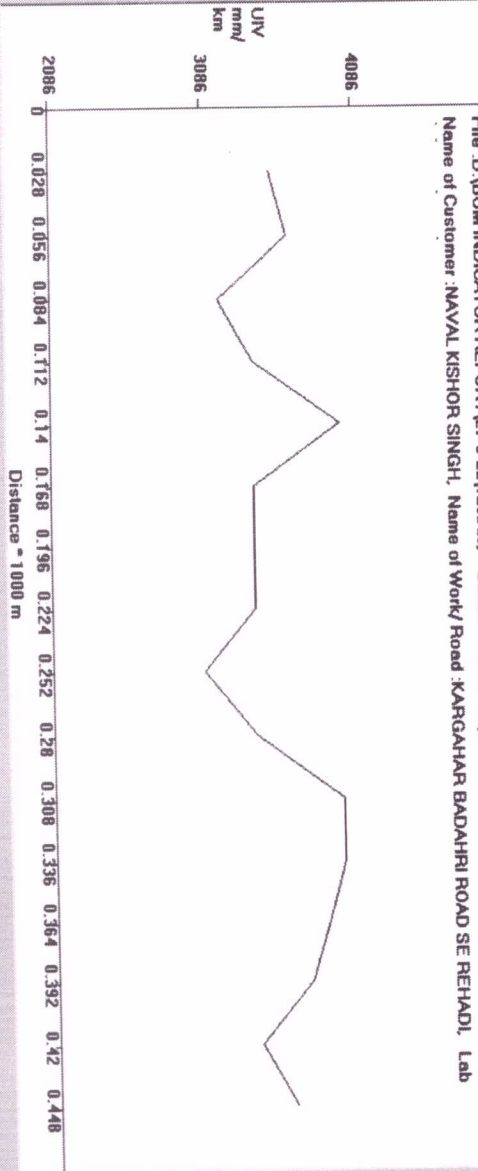

17/05/2022
 10-06-22
 JH

10/6/22
 AG

28/6/22
