

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा (नालन्दा)।
Email:- ee.hilsa.rwd@gmail.com

पत्र संख्या 2037

हिलसा/दिनांक 30.11.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-22 में
व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रू0 10.85625 (रू0 दस लाख पचासी
हजार छः सौ पच्चीस मात्र) रूपये का आवंटन उपलब्ध कराने की कृपा की जा ताकि किये गये
कार्यों का भुगतान किया जा सके।

अनु:- यथोक्त।

विश्वासभाजन

R. 30/11/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

30.11

MAINTENANCE YEAR : 1st

NAME OF THE ROAD : HILSA FATUHA BANWARI ROAD TO KAMTA VILLAGE UPTO TEMPLE

LENGTH OF THE ROAD : 0.350 KM

DIVISION : HILSA

PACKAGE NO. : MR-N/19-20/HILSA/04

BLOCK : HILSA

AGENCY : SUNNY CONTRACTOR AND ENGINEERS PVT LTD

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV mm/km	CATEGORY	IRI	Latitude	Longitude	Event			
3/6/21	9:22:16	91	0.1	280	0	2800	2899	G	3.9	25.335828	85.28313	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
3/6/21	9:23:0	91	0.1	310	30.3	3100	3180	G	4.24	25.3364	85.28367	Normal	$Y = 2337$		
3/6/21	9:23:27	91	0.1	300	30.3	3000	3086	G	4.13	25.337038	85.283737	Normal	(R) RURAL ROAD		
3/6/21	9:23:57	91	0.045	320	30.3	2200	2337	G	3.22	25.336432	85.283802	Normal	Good	Average	Poor
TOTAL			0.345	1210	90.9	11100	11502		15.49	101.345698	341.134339		<4000	4001-5000	>5001
AVERAGE						2775	2875.5		3.8725						


30/11/17

Name of Customer: SUNNY CONTRACTOR AND
 Name of Work/ Road: HILSA FATUHA BANWARI RD
 Lab Job number: 2306-2021
 Date: 23-06-2021
 Section No: 91

Test Date: 03-06-2021
 Machine No:
 Start S No:
 Start E No:
 Weather:
 Start Location:
 End Location:
 Road Name: MTA VILLAGE UPTO TEMPLE
 Road Type: (R) RURAL ROAD
 Side:
 UIV Range: 1337 To 4000 Interval 1000 mm/km
 Dist Range: 0 To 0.5 Interval 0.1 = 1000 m
 Equation: $Y = 0 * X^2 + 0.936 * X + 278.4$

Print Generate Report and Graph Redraw Graph Map View

File C:\Users\SHAZN\Desktop\191 Xs. Section No. 91. Eqn : $Y = 0 * X^2 + 0.936 * X + 278.4$
 Name of Customer: SUNNY CONTRACTOR AND ENGG. Name of Work/ Road: HILSA FATUHA BANWARI ROAD TO

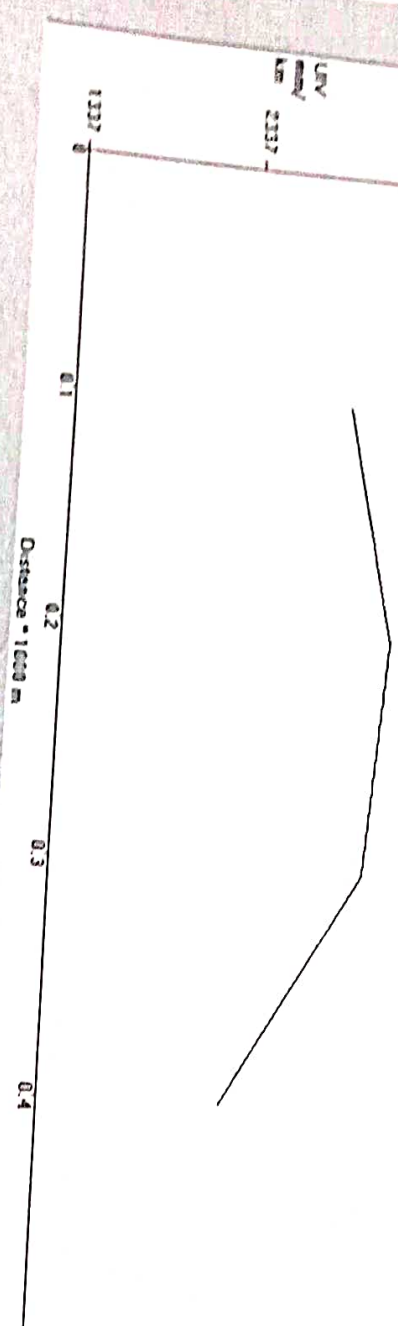

30/11/21

Government of Bihar
OM01

3rd Quarter

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Form

Rural Work Department
Road From : Hilsa fathua banwari road to kamta village
Length of Road : 0.720 Km.
Period:- from 11.7.21 to 10.10.21

To: ... Executive Engineer
RWD, Works Division Hilsa

Date : ...

Inspector :J.E.. RWD Sub Division Ekangarsarai

Position : ..J.E

No.	Name	Work	Unit of work required in each kilometre										Comments					
			1	2	3	4	5	6	7	8	9	10						
OM100	Sealed Pavement																	
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil											No. Pothole found.
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil	Nil	Nil											No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil											No Crack Sealing found
OM104	Surface Treatment																	
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil											No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil											No Bleeding / Flushing Required
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil											No Crocodile Cracking found
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.	N.A.											No Edge Repair Required
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.	N.A.	N.A.											
OM200	Shoulder																	
	Unsealed Shoulder																	
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil											No Edge Drop-off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil											No Roughness, Scouring or Potholes Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil											No Holding water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil											No Embankment Repair Required
OM300	Drainage including culverts major																	
	Other activities		N.A.	N.A.	N.A.	N.A.	N.A.											
OM301	Surface Drains & Verges	Lm	N.A.	N.A.	N.A.	N.A.	N.A.											Not Required
OM302	Culvert Clearing	No.	Nil	Nil	Nil	Nil	Nil											Not Required
OM303	Culvert and pit Repair	M ²	Nil	Nil	Nil	Nil	Nil											Not Required
	Other activities (White Washing)	M ²	Nil	Nil	Nil	Nil	Nil											Not Required

30338

Appendix

Executive Engineer, Works Division

No.	Standard work item Name	Work Units	Unit of work required in each kilometre										Comments									
			1	2	3	4	5	6	7	8	9	10										
OM400	Vegetation																					
	Grass Control																					
OM401	a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil	Nil													Not Required		
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil														Not Required	
OM402	Tree and Shrub Management (Cutting Trees)	No.	Nil	Nil	Nil	Nil	Nil														Not Required	
	(Cutting shrubs)	No.	Nil	Nil	Nil	Nil	Nil														Not Required	
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil	Nil														Not Required	
	Safety Signage and Road																				Not Required	
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil	Nil														Not Required	
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.	N.A.														Not Applicable	
OM503	Distance Stones	No.	N.A.	N.A.	N.A.	N.A.	N.A.														Not Applicable	
OM504	Road marking	M ²	Nil	Nil	Nil	Nil	Nil														Not Required	
	Other activities																					

(Signature of Contractor/Authorized representative) Date

SUNNY CONTRACTORS AND ENGINEERS PVT. LTD Time

[Signature] Place

DIRECTOR

[Signature]

[Signature] *[Signature]*

[Signature] *[Signature]*

Executive Engineer

Rural Works Department

Works Division, NH&S

[Signature]

Note:- Enclose photographs with this report.

No.	Standard work Item Name	Work Units	Unit of work required in each kilometre										Comments					
			1	2	3	4	5	6	7	8	9	10						
OM400	Vegetation																	
	Grass Control																	
	a) Roadside- General Tidy																	
OM401	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Tree and Shrub Management (Cutting Trees)	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	(Cutting shrubs)	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM500	Safety Signage and Road																	
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	Not Required
OM503	Distance Stones	No.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	Not Applicable
OM504	Road marking	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Applicable
	Other activities																	Not Required

(Signature of Contractor/Authorized representative)
SANKU CONTRACTORS AND ENGINEERS PVT. LTD
Sanku
 Date

DIRECTOR

Prasanna
 05.05.2022
 A.E

Rajesh
Executive Engineer
 Rural Works Department
 Works Division, MHS

Note:- Enclose photographs with this report.

Place

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Hilsa fathua banwari road to kamta village		
2	Batch No.	RM/NA/III/19/0006		
3	Project ID	1281033302		
4	Total Length of Road (in km.)	0.720		
5	Length of Road to Meet Required Service Level (Completed Length) (in km) [1]	0.720		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	4th quarter		
7	Ordinary Maintenance Cost as per Shedule (Agreement Amount for Maintenance) in lakh	0.07050		
8	Quarterly Payment:1/20 of Ordinary Mainten ance Cost as per shedule (in Lakh) [2]	0.07050		
Compliance Criteria	Standard job Decription	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.07050

Date of inpection by E/I or his agent
Prepared by contractor's self control unit

Name and Designation of person inspecting road

Signature

Date

Signature of person inspecting road

Ram
05.05.2022
J.B
