

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

पत्रांक..... 1942 अनु० सोनपुर, दिनांक..... 14.11.2022

प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक

पदाधिकारी—सह—सचिव,

बिहार ग्रामीण पथ विकास अभिकरण

(BRRDA)

बिहार, पटना।

विषय:— बिहार ग्रामीण पथ अनुरक्षण निति—2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति—2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 22,56,380.00 (बाईस लाख छप्पन हजार तीन सौ अस्सी) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु०:—Standard Formate for Roads

Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

14/11/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150

Form of Utilization Certificate up to the month of **November-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)		175.42789	Certified that out of Rs 175.42789 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 131.66677 Lakh has been utilized for the purpose of New Maintenance Policy-18 (Maintenance) Scheme as given in the margin for which it was sanctioned and that the balance of Rs 43.76112 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Words have been supervised be Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

D.A.O

R.W.D. Works Division Sonpur.

EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Name of Works Division:- SONPUR																												
Road Details					AA Details		Agreement							Actual Maintenance Expenditure								Current Maintenance Demand					Remarks	
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintena nce Amount (in lakh)	Main Work Amount (in Lakh)	Agre emen t-1	Agree ment-2	Agree ment-3	Agreement-4	Agree ment-5	Total Maintenance	Length h (in KM)	1st. Year Maint enanc e	2nd. Year Mainte nance	3rd. Year Mainte nance	4th Year Mainte nance	5th Year Mainte nance	Total Maint ananc e Expen diture	Length as per Bump Report	IRI As per bump Report	1st QTR Maint enance	2nd QTR Mainte nance	3rd QTR Mainte nance	4 th QTR Mainte nance		Total
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	30	31	
1	Parsa Bankerwa R.E.O. road to babhan garna via marar bazar	RM/SA/SON /19/0001	31306201016	05-06-2020	100.79500	56.02000	95.97828	9.90394	9.90394	9.90394	9.90394	9.90394	49.51970	4.580	0.00000	0.00000	0.00000	0.00000	0.00000	0.000	4.580	2107	2.47599	2.47599	2.47599	2.47599	9.90394	
2	Parsa to Ekdervia Masuria hasanpura	RM/SA/SON /19/0001	31306202161	16-06-2020	183.88900	71.54600	179.07457	12.65986	12.65986	12.65986	12.65986	12.65986	63.29930	5.700	0.00000	0.00000	0.00000	0.00000	0.00000	0.000	5.700	2450	3.16497	3.16497	3.16497	3.16497	12.65986	
Total																											22.56380	


 D.A. 11.10.20
 R.W.D. Works Division
 SONPUR


 Executive Engineer
 R.W.D. Works Division
 SONPUR
 14/11/2022

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Parsa to Ekderwa Masuria hasanpura		
2	Batch No.	RM/SA/SON/19/0001		
3	Project ID	31306202161		
4	Total Length of Road (in Km)	5.700		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	5.700		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	63.29930		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	3.16497		

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				3.16497

Date of inspection by E/1 or his agent Prepared by Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Executive Engineer
Roads & Works Department
Work Division, Sonapatna

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Sonpur

Government of Bihar

OM01

Rural works Department

Road From- Parsa to Ekderwa Masuria hasanpura

Length of Road: 5.700 KM

Period : From.....

Inspector: A.E RWD Sub Division, Parsa

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Sonpur

Date:

Position: A.E

Standard Work item			Work	Units of work required in each kilometre										Comments
S No	Name	Units		1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement														
OM101	Pothole Patching	m2												No. Pothole found.
OM102	Surface Depression and Rut Patching	m2												No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm												No Crack Sealing found
Surface Treatment														
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2												No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2												No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2												No Crocodile Cracking found
OM105	Edge Repair	m2												No Edge Repair Required
OM106	Digouts	m2												
OM107	Concrete Pavement	m3												
	Other activities	Lm												
OM200 Shoulder														
OM201	Unsealed Shoulder	No												No Edge Drop off Required
	(a) Edge Drop off	Lm												Not required
	(b) Roughness, Scouring or Potholes	Lm												
	(c) Holding Water	Lm												No Holding water found
OM202	Embankment Repair	No												No Embankment Repair Required
	Other Activite (Raincut)													Defects rectified within stipulated time.
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm												Not Required
OM302	Culvert Cleaning	Lm												Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2												Not Required

15/01/2022
15/01/2022
15/01/2022

Name of work : Parsa to Ekderwa Masuria hasanpura

Name of customer : Lalan Kumar

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	-Latitude	Direction	Longitude	Direction1	Remarks
13/04/22	13:44:19	25	100	100	31.0 cm	19.5 Km/Hr	3100.0 mm/Km	3073	4.12	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	14:04:16	25	100	200	28.0 cm	15.7 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:04:36	25	100	300	21.0 cm	17.6 Km/Hr	2100.0 mm/Km	2111	2.94	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:04:53	25	100	400	19.0 cm	21.8 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:05:08	25	100	500	20.0 cm	22.8 Km/Hr	2000.0 mm/Km	2015	2.82	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:05:23	25	100	600	17.0 cm	24.0 Km/Hr	1700.0 mm/Km	1726	2.46	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:05:49	25	100	700	16.0 cm	14.4 Km/Hr	1600.0 mm/Km	1630	2.34	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:06:31	25	100	800	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:07:02	25	100	900	24.0 cm	11.4 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:07:20	25	100	1000	24.0 cm	20.2 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:07:40	25	100	1100	23.0 cm	17.8 Km/Hr	2300.0 mm/Km	2304	3.18	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:08:04	25	100	1200	15.0 cm	15.3 Km/Hr	1500.0 mm/Km	1534	2.21	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:08:29	25	100	1300	19.0 cm	14.2 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:08:50	25	100	1400	19.0 cm	16.9 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:09:19	25	100	1500	27.0 cm	12.7 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:09:36	25	100	1600	30.0 cm	18.3 Km/Hr	3000.0 mm/Km	2977	4	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:09:54	25	100	1700	27.0 cm	22.5 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:10:17	25	100	1800	28.0 cm	13.7 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:10:58	25	100	1900	32.0 cm	18.4 Km/Hr	3200.0 mm/Km	3169	4.23	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:11:18	25	100	2000	22.0 cm	18.5 Km/Hr	2200.0 mm/Km	2207	3.06	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:11:38	25	100	2100	26.0 cm	17.2 Km/Hr	2600.0 mm/Km	2592	3.54	Good	25.8480921	N	85.0339670	E	Normal

13/04/22
13/04/22
13/04/22

13/04/22
13/04/22
13/04/22

Executive Engineer
Rural Works Department
Work Division, Sonagur

Name of work : Parsa to Ekderwa Masuria hasanpura

Name of customer : Lalan Kumar

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

13/04/22	14:11:56	25	100	2200	19.0 cm	12.8 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:12:18	25	100	2300	24.0 cm	17.1 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:12:37	25	100	2400	26.0 cm	18.1 Km/Hr	2600.0 mm/Km	2532	3.54	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:13:39	25	100	2500	16.0 cm	15.9 Km/Hr	1600.0 mm/Km	1630	2.34	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:14:45	25	100	2600	27.0 cm	15.4 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:15:21	25	100	2700	38.0 cm	15.0 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:16:08	25	100	2800	30.0 cm	17.6 Km/Hr	3000.0 mm/Km	2977	4	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:16:45	25	100	2900	26.0 cm	9.4 Km/Hr	2600.0 mm/Km	2592	3.54	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:17:18	25	100	3000	29.0 cm	10.6 Km/Hr	2900.0 mm/Km	2881	3.89	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:17:53	25	100	3100	28.0 cm	10.5 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:18:20	25	100	3200	28.0 cm	13.7 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:18:40	25	100	3300	18.0 cm	17.8 Km/Hr	1800.0 mm/Km	1822	2.58	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:18:59	25	100	3400	10.0 cm	19.0 Km/Hr	1000.0 mm/Km	1053	1.58	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:19:33	25	100	3500	27.0 cm	10.8 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:20:09	25	100	3600	27.0 cm	9.9 Km/Hr	2700.0 mm/Km	2688	3.65	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:20:44	25	100	3700	11.0 cm	10.3 Km/Hr	1100.0 mm/Km	1144	1.71	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:21:04	25	100	3800	18.0 cm	16.7 Km/Hr	1800.0 mm/Km	1822	2.58	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:21:28	25	100	3900	28.0 cm	15.4 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:22:07	25	100	4000	14.0 cm	9.0 Km/Hr	1400.0 mm/Km	1438	2.09	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:22:26	25	100	4100	13.0 cm	18.3 Km/Hr	1300.0 mm/Km	1342	1.95	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:22:44	25	100	4200	28.0 cm	20.2 Km/Hr	2800.0 mm/Km	2784	3.77	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:23:01	25	100	4300	14.0 cm	20.6 Km/Hr	1400.0 mm/Km	1438	2.09	Good	25.8480921	N	85.0339670	E	Normal

15/04/22
16/04/22

Kam Arjun
Rural Works Department
Work Division, Sonepur

Name of work : Parsa to Ekderwa Masuria hasanpura

Name of customer : Lalain Kumar

(R) Rural Road			
Good		Average	Poor
< 4000		4001 - 5000	> 5000


13/04/22	14:23:22	25	100	4400	13.0 cm	17.4 Km/Hr	1300.0 mm/Km	1342	1.96	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:23:41	25	100	4500	15.0 cm	18.5 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:24:22	25	100	4600	15.0 cm	18.9 Km/Hr	1500.0 mm/Km	1534	2.21	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:24:49	25	100	4700	23.0 cm	13.2 Km/Hr	2300.0 mm/Km	2304	3.18	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	14:25:04	25	100	4800	21.0 cm	13.2 Km/Hr	2100.0 mm/Km	2111	2.94	Good	25.8480921	N	85.0339670	E	Normal
13/04/22	15:09:26	25	100	4900	27.0 cm	16.3 Km/Hr	2700.0 mm/Km	2888	3.65	Good	25.9353934	N	85.0228205	E	Normal
13/04/22	15:10:07	25	100	5000	19.0 cm	18.8 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.9356204	N	85.0218897	E	Normal
13/04/22	15:10:48	25	100	5100	22.0 cm	18.7 Km/Hr	2200.0 mm/Km	2207	3.06	Good	25.9364672	N	85.0218134	E	Normal
13/04/22	15:11:19	25	100	5200	24.0 cm	11.6 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.9373618	N	85.0219736	E	Normal
13/04/22	15:11:46	25	100	5300	19.0 cm	13.3 Km/Hr	1900.0 mm/Km	1919	2.7	Good	25.9377699	N	85.0212259	E	Normal
13/04/22	15:12:09	25	100	5400	24.0 cm	15.2 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.9384852	N	85.0202799	E	Normal
13/04/22	15:12:31	25	100	5500	20.0 cm	16.6 Km/Hr	2000.0 mm/Km	2015	2.82	Good	25.9389544	N	85.0194864	E	Normal
13/04/22	15:12:54	25	100	5600	24.0 cm	15.6 Km/Hr	2400.0 mm/Km	2400	3.3	Good	25.9389544	N	85.0194864	E	Normal
13/04/22	15:13:25	25	100	5700	11.0 cm	10.8 Km/Hr	1100.0 mm/Km	1149	1.71	Good	25.8480921	N	85.0339670	E	Normal

15/04/22

16/04/22

Executive Engineer
Rural Works Department
Work Division, Sonapur

Name of Customer: Lalan Kumar, Machine no: 19209, Road: Parsa to Ekderwa Masuria hasanpura, Date: 13-04-22, Section No: 25, Equation: $Y = 0.926 X + 90.9$

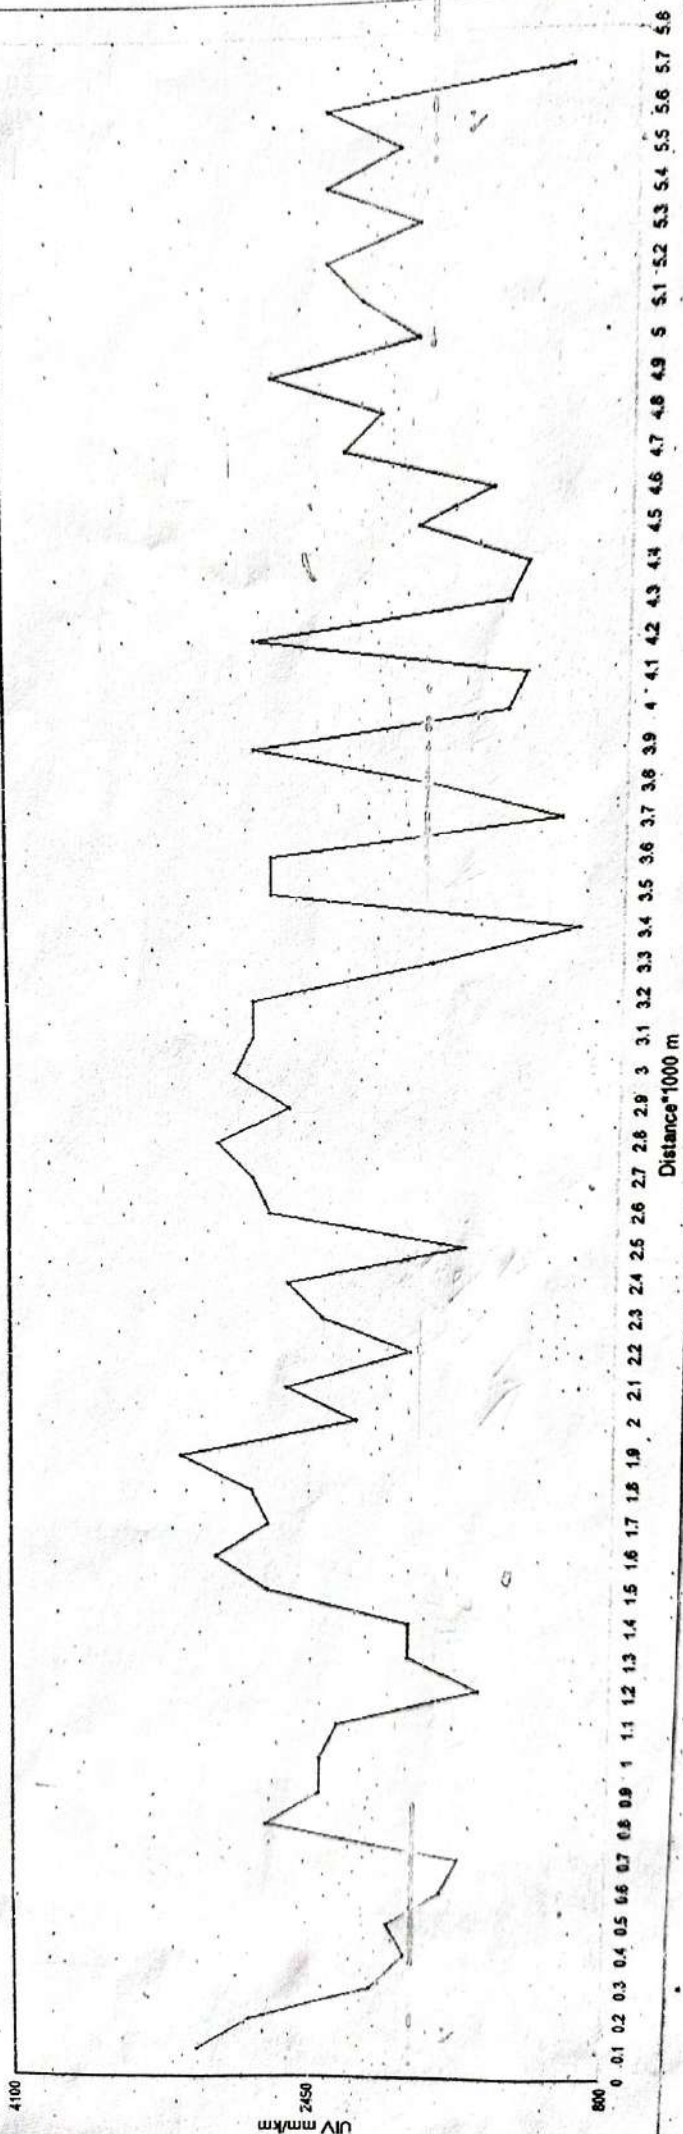

Signature
A.E. 16/12/22

Signature
22/12/22

Signature
Executive Engineer
Rural Works Department
Work Division, Sonapur
