

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, महुआ।

पत्रांक 2063 /

महुआ/दिनांक 30 / 09 / 2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-
सचिव, ब्राडा,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- एम0आर0 (3054) नई अनुरक्षण नीति 2018 (अनुरक्षण मद) योजना अन्तर्गत कराये गए अनुरक्षण कार्य के विरुद्ध अधियाचना के संबंध में।

महाषय,

उपरोक्त विषयक एम0आर0 (3054) नई अनुरक्षण नीति 2018 (अनुरक्षण मद) योजना अन्तर्गत कराये गए अनुरक्षण कार्य के विरुद्ध अधियाचना विहित प्रपत्र में भरकर भेजी जा रही है।

अनु0- (1) अधियाचना विहित प्रपत्र में।

विश्वासभाजन,

[Signature]

29.09.22

कार्यपालक अभियंता,

ग्रामीण कार्य विभाग, कार्य प्रमंडल,

महुआ।

[Signature]
29/09/22

[Signature]
29/09/22

Form GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month- 27 .09.2022


STATE- BIHAR


SL. No	Name of Scheme	Sanction No. & Date With Amount (In Rs. Lacs)	Amount Received (In Rs.Lacs)	Particulars
1	Construction of Rural Roads under MR(3054) New Maintenance Policy 2018	Lt No-27 Dated- 26.08.2022 Amount- Rs- 2.08600	7.02808	Certified that out of Rs.7.02808 Lacs of grants-in-aid sanctioned during the years 14-15 in favour of E-in-C, REO Bihar, Patna a sum of Rs.7.02808 lacs has been utilized for the purpose of MR(3054) New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.NIL lacs remaining unutilized at the end of the period under.
	Total:		7.02808	


- 2 Certified that I have satisfied myself that the conditions on which the gram-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sancticed.

Kind of Checks exercised:-

- Works has been supervised by Executive Engineer/Superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - Construction materials have been tested.
 - Measurements have been recorded in the MBs and test check conducted by the Assistant Executive Engineer
 - All other codal formalities have been observed.
- 3 Physical Progress achieved:-
- Construction of Road Works.
 - Construction of CD Works.


Divisional Account Officer
RWD. Works Division, Mahua




29.09.22
Executive Engineer
RWD. Works Division, Mahua


29/09/22

Name of Works Division :- Mahua

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018


Road Details				AA Details				Agreement					Actual Maintenance Expenditure							Current Maintenance Demand					Remarks				
Sl No.	Name of Work	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in Lakh)	Main Work Amount (in Lakh)	Agreement 1	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maintenance Amt. (in Lakh)	Length (in Km)	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4th Year Maint. Exp.	5th Year Maint. Exp.	Total Maint. Exp.	Length As per Bump Report	ISI As per Bump Report	1st Qtr Maint.	2nd Qtr Maint.		3rd Qtr Maint.	4th Qtr Maint.	5th Qtr Maint.	Total
1	Maksudpur Jogi baba asthan - Narsingpur path via Milkandpur	RM/VA/MAH/19/0010	31507502033	20.08.2021	49.43000	25.57300	41.97800	1.26629	2.39984	6.68424	3.47055	7.16910	20.99002	2.300	0.00000	0.00000	0.00000	0.00000	0.00000	0	2.400	1846	1.04950	0.00000	0.00000	0.00000	0.00000	1.04950	
2	Joathan Chaulk - Permandpur Lal	RM/VA/MAH/19/0010	31507502068	22.08.2021	64.98000	33.59800	55.18000	1.65624	3.15406	8.77398	4.57512	9.46140	27.62080	3.041	0.00000	0.00000	0.00000	0.00000	0.00000	0	3.100	2440	1.38104	0.00000	0.00000	0.00000	0.00000	1.38104	
3	Chahwera Kapur - Jahangirpur Salikhan	RM/VA/MAH/19/0010	NEA220002397	18.08.2021	141.00000	75.40000	119.40800	3.85688	7.24218	19.71339	10.44220	21.26144	62.51609	6.850	0.00000	0.00000	0.00000	0.00000	0.00000	0	6.900	2182	3.12576	0.00000	0.00000	0.00000	0.00000	3.12576	
Total																													5.55630


 EXECUTIVE ENGINEER
 RURAL WORKS DEPARTMENT
 MAHUA
 29.09.22

 DISTRICT ENGINEER
 MAHUA

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Jodhan Chauk - Parmanandpur Lal		
2	Batch No.	RM/VA/MAH/19/0010		
3	Project ID	31507502068		
4	Total Length of Road (in Km)	3.041		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.041		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	27.62080		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.38104		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.38104

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit


29.09.22

Name and Designation of person inspecting road
(Signature)

Date


29.09.22
Signature of person inspecting road

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name of Works Division :- Mahua													
Government of Bihar OM01 Road works Department			SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT										
Road From----- Jordan Chank - Parmanandpur Lal			To: Executive Engineer RWD Works Division Mahua Date										
Length of Road- 3.041 KM													
Period ----- From													
Inspector ----- A E RWD Sub Division, 0			Position: A.E.										
S No	Standard Work item Name	Work Units	Units of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No Pothole found
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Dipsouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m2	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	1%	1%	Nil							Defects rectified within stipulated time
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activities (Raincut)		1%	1%	2%	1%							Defects rectified within stipulated time
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
OM 400 Vegetation													
OM401	Grass Control												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Trees and shrub management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

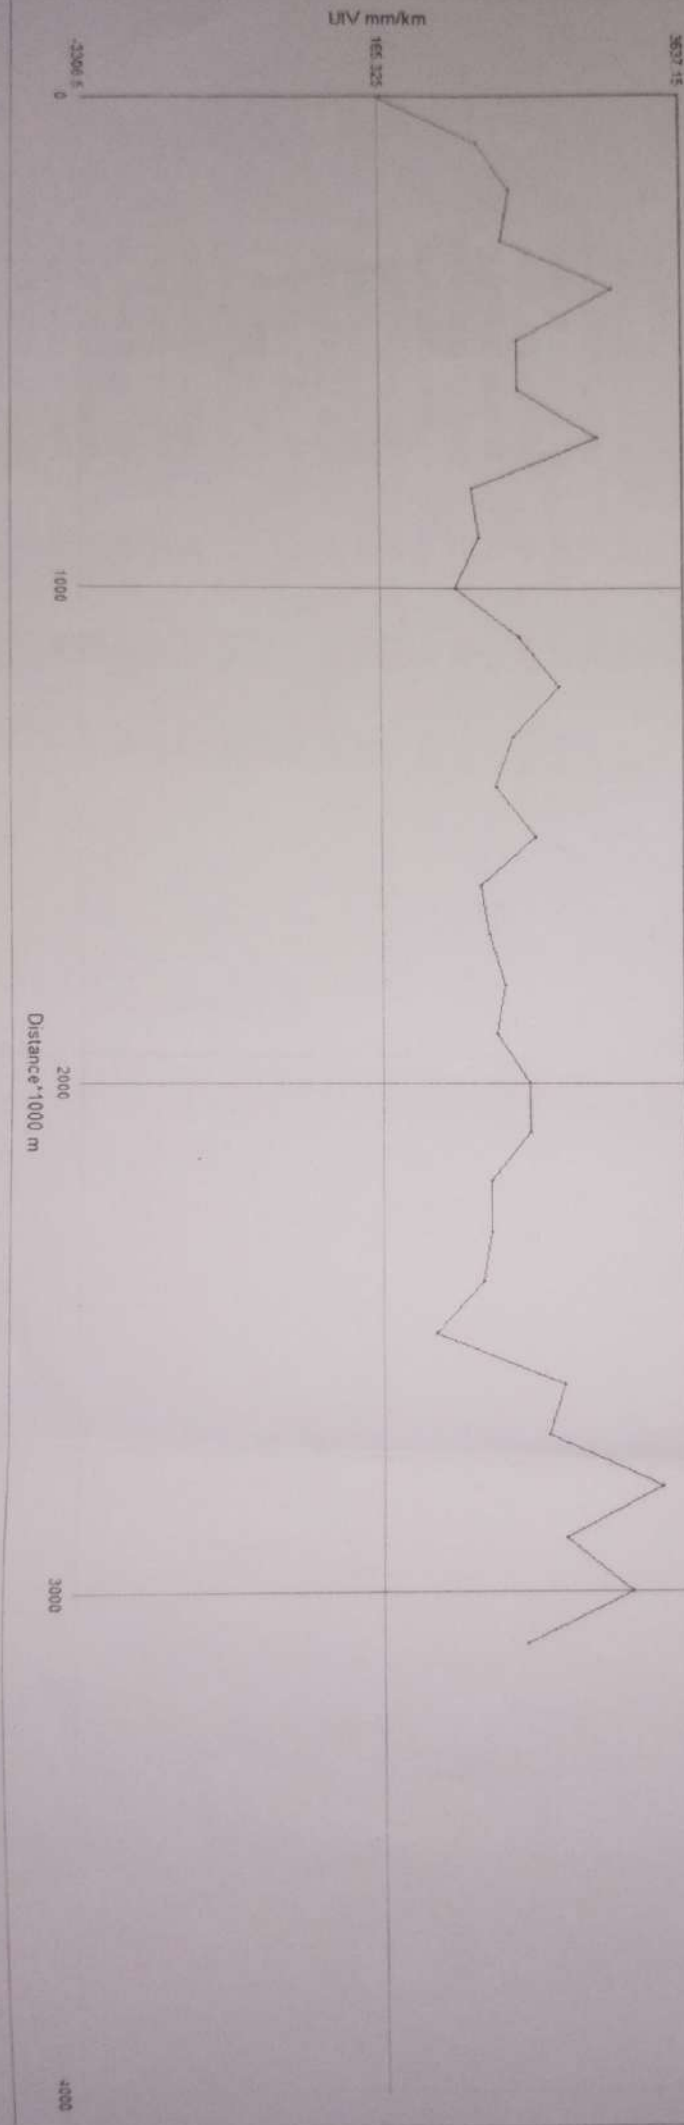
Bidder

Appendix

Executive Engineer, Rural Work Department,
Work Division, Mahua

28/09/22
08

Name of Customer: E.A.P Construction Pvt. Ltd, Machine no: 19190, Road: Jodhan Chowk to Parmanandpur Lal, Date: 04-06-22, Section No: 20, Equation: $Y=0.909X+125.0$



Signature
29-08-22

Signature
29-08-22

Name of the work: Jodhan Chowk to Parmanandpur Lal

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMPLE (m)	Speed (km/Hr)	U (mm/Km)	Corrected U (mm/km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
04-06-2022	17:24:57	20	0	0	0.0 cm	19.6 Km/Hr	0.0 mm/Km	125	0.236	Good	25.8727141 N		85.3943033 E		Normal
04-06-2022	11:42:59	20	100	100	13.0 cm	6.3 Km/Hr	1300.0 mm/Km	1306.7	1.918	Good	25.8727141 N		85.3943033 E		Normal
04-06-2022	11:43:19	20	100	200	17.0 cm	17.6 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8727141 N		85.3943033 E		Normal
04-06-2022	11:43:38	20	100	300	16.0 cm	19.6 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8727141 N		85.3943033 E		Normal
04-06-2022	11:43:58	20	100	400	30.0 cm	17.8 Km/Hr	3000.0 mm/Km	2852	3.851	Good	25.8727141 N		85.3943033 E		Normal
04-06-2022	11:44:22	20	100	500	18.0 cm	15.1 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.781991 N		85.4290705 E		Normal
04-06-2022	11:44:43	20	100	600	18.0 cm	17.0 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.781991 N		85.4290705 E		Normal
04-06-2022	11:45:05	20	100	700	28.0 cm	16.0 Km/Hr	2800.0 mm/Km	2670.2	3.631	Good	25.781924 N		85.4318552 E		Normal
04-06-2022	11:45:28	20	100	800	12.0 cm	15.8 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.7816095 N		85.4322596 E		Normal
04-06-2022	11:45:49	20	100	900	13.0 cm	17.0 Km/Hr	1300.0 mm/Km	1306.7	1.918	Good	25.7814226 N		85.4338083 E		Normal
04-06-2022	11:47:17	20	100	1000	10.0 cm	4.1 Km/Hr	1000.0 mm/Km	1034	1.556	Good	25.781146 N		85.434701 E		Normal
04-06-2022	11:47:39	20	100	1100	18.0 cm	16.5 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.781146 N		85.434701 E		Normal
04-06-2022	11:48:00	20	100	1200	23.0 cm	16.9 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.781146 N		85.434701 E		Normal
04-06-2022	11:48:21	20	100	1300	17.0 cm	16.8 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.781146 N		85.434701 E		Normal
04-06-2022	11:48:42	20	100	1400	15.0 cm	17.2 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.781146 N		85.434701 E		Normal
04-06-2022	11:49:03	20	100	1500	20.0 cm	17.1 Km/Hr	2000.0 mm/Km	1943	2.734	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:49:22	20	100	1600	13.0 cm	18.6 Km/Hr	1300.0 mm/Km	1306.7	1.918	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:49:40	20	100	1700	14.0 cm	20.6 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:49:57	20	100	1800	16.0 cm	20.6 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:50:15	20	100	1900	15.0 cm	20.6 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:50:34	20	100	2000	19.0 cm	19.0 Km/Hr	1900.0 mm/Km	1852.1	2.619	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:50:53	20	100	2100	19.0 cm	18.1 Km/Hr	1900.0 mm/Km	1852.1	2.619	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:51:12	20	100	2200	14.0 cm	20.0 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:51:31	20	100	2300	14.0 cm	18.5 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:51:51	20	100	2400	13.0 cm	18.1 Km/Hr	1300.0 mm/Km	1306.7	1.918	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:52:11	20	100	2500	7.0 cm	18.2 Km/Hr	700.0 mm/Km	761.3	1.184	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:52:31	20	100	2600	23.0 cm	17.8 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.7803469 N		85.4391413 E		Normal
04-06-2022	11:52:51	20	100	2700	21.0 cm	17.6 Km/Hr	2100.0 mm/Km	2033.9	2.847	Good	25.7817888 N		85.4496927 E		Normal
04-06-2022	11:53:10	20	100	2800	35.0 cm	19.4 Km/Hr	3500.0 mm/Km	3306.5	4.394	Good	25.7826433 N		85.450036 E		Normal
04-06-2022	11:53:36	20	100	2900	23.0 cm	13.5 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.7826433 N		85.450036 E		Normal
04-06-2022	11:54:00	20	100	3000	31.0 cm	15.0 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.7826433 N		85.450036 E		Normal
04-06-2022	11:54:30	20	100	3100	18.0 cm	12.3 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.7826433 N		85.450036 E		Normal

[Signature]
DB

[Signature]
29.09.21

IRI Value 2440
Machine No 19190
