

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल सासाराम-2

पत्रांक1037 अगुठ..... सासाराम/ दिनांक 20/10/22

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सासाराम-2।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार - पटना।

विषय :- MR (3054) New Maintenance Policy.2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक- मु0अ0 04(मु0)3054-04-229/2021-1135 (अनु0)/ पटना, दिनांक- 09.03.2022 एवं पत्रांक- 97 दिनांक- 07.01.2022

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निदेश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR (3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। उक्त कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- Standard Format for Roads
Quarterly Statement

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सासाराम-2
20/10/22

STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (1st Quarter)

PIU NAME :- Rural Works Department Works Division Sasaram-2

1	Name Of Road	Construction of road from Nokha Buxer Cainal to isharpura Village		
2	Batch No.	RM/RO/SAS/20/0002		
3	Project ID	10301101057		
4	Total Length Of Road(in Km)	0.900		
5	Lenth Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	0.900		
6	NO. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	8.71341		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.43567		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.43567

date of Inpection by E/I Or His Agent
Prepared by Contractor's Self Control Unit

Name and Designation of person inspecting road

date

20/10/22
26

(Signature)

Certify by E/I [Signature] date

Signature of person inspecting road

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Sasaram-2

1 Year (1st Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-Construction of road from Nokha Buxer Caimal to Isharpura Village
(Package No.RM/RO/SAS/20/0002)
Length of Road :- 0.900 Km
Inspector :- J.E RWD Sub Division :Nokha

To:-

Executive Engineer
RWD, Works Division Sasaram-2

Date:-

Position :- J.E.

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil										No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil										Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil										No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil										No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil										No Bleeding/ Flushing Required
	@ Crocodile Cracking	m ²	Nil										No Crocodile Cracking Found
105	Edge Repair	m ²	Nil										No Edge Repair Required
106	Digouts	m ²	N.A										No Edge Repair Required
107	Concrete pavement	m ³	N.A										N/A
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil										No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil										Not Required
	(c) Holding water	Lm	Nil										No Holding Water Found
OM202	Embankment Repair	m ³	Nil										Not Required
	Other activities (Rain Cuts)		Nil										N/A
OM300	Drainage Including culverts major												
OM301	Surface Drains & Verge	Lm	N.A										N/A
OM302	Culvert Cleaning	No	Nil										Not Required
OM303	Culvert and pit Repair	m ³	Nil										Not Required
	Other activities(Whirlw washing)	m ²	Nil										Not Required

22/10/22

2E

No	standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil										Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil										Not Required
	Tree and Shrub Management	No	Nil										Not Required
	Cutting Of Branches Of Trees	No	Nil										Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil										Not Required
	Other activities (Trimming of Grass)	M ²	Nil										Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil										Not Required
OM502	Guard Stones	Lm	N.A										Not Required
OM503	Distance Stones	No	N.A										Not Required
OM504	Road Marking	M ²	Nil										N/A
	Other activities												

Bidder

Appendix

Executive Engineer, Works Division, Sasaram-2

20/10/22
20/10/22
JE

20/10/22
20/10/22

Name of Road : Const. Road Nokha - Buxar Canal to isharpura village

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
19/9/22	14:1:0	65	0.1	120	33.2	1200	1615	G	25.45293	84.9606	Normal
19/9/22	14:1:30	65	0.1	120	10.1	1600	2215	G	25.45128	84.97037	Normal
19/9/22	14:2:5	65	0.1	150	10.1	1500	1915	G	25.44758	84.97945	Normal
19/9/22	14:2:40	65	0.1	210	10.1	2100	2515	G	25.44315	84.9877	Normal
19/9/22	14:3:0	65	0.1	190	10.1	1900	2315	G	25.44005	84.9973	Normal
19/9/22	14:3:15	65	0.1	130	10.1	1300	1715	G	25.43795	84.10069	Normal
19/9/22	14:4:0	65	0.1	210	10.1	2400	2815	G	25.43647	84.10165	Normal
19/9/22	14:6:12	65	0.1	220	13.2	2200	2615	G	25.43097	84.10236	Normal
19/9/22	14:6:47	65	0.1	260	10.1	2100	2515	G	25.42882	84.10332	Normal
Total			0.9								

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 2000$$

$$Y = 2415$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Plead
29/10/22
7E

20/10/22
E/E

Name of Customer : NAVEEN KUMAR SINGH
 Name of Work/ Road : Canal Road Nohla - Boxer Ca
 Lab Job number : 65
 Date : 19/09/2022
 Section No. : 65


Test Date : 19-09-2022
 Machine No : 391
 Road Type : (R) RURAL ROAD
 Side :
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 UIV Range : 215 To 4000 Interval
 Dist Range : 0 To 10.1
 Elevation : $Y = 0 \cdot X^2 + 1,000 \cdot X + 415.2$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BUMF\mavm\1303154111.xls, Section No. : 65, Egn : $Y = 0 \cdot X^2 + 1,000 \cdot X + 415.2$
 Name of Customer : NAVEEN KUMAR SINGH, Name of Work/ Road : Canal Road Nohla - Boxer Canal to Ishapur

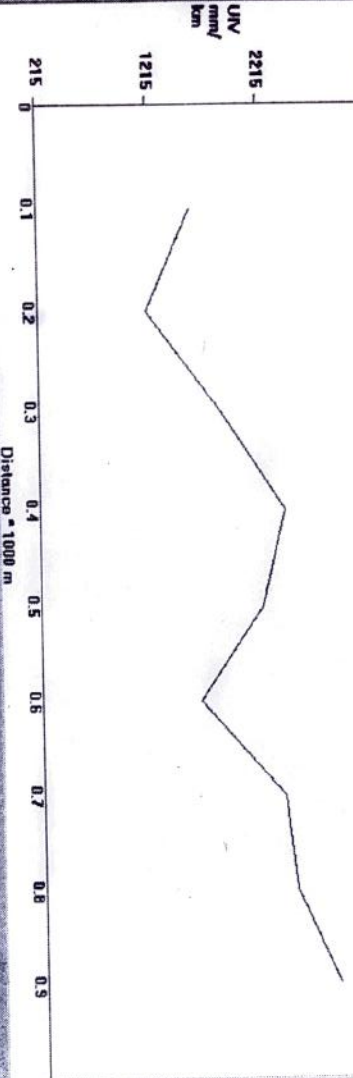

Recd
 20/10/22
 >E

20/10/22
 >E
