

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल गोपालगंज-1

पत्रांक:- 1578 ~~34~~ / गोपालगंज दिनांक:- 10/09/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल गोपालगंज-1

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय:- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सुचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0-यथोक्त।

विश्वासभाजन


10/9/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : Executive Engineer, R.W.D. Works Division, Gopalganj-1

1st Year
3rd Quarter

1	Name of the Road	Harakhua Khawasepur to Odipur Road		
2	Batch No.	RM/610/610P/19/0007		
3	Project ID	31407001015		
	Total Length of Road (in Km)	1.580 Km		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	1.580 Km		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	15.44057		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.77203		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATAION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.77203

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

(Signature)

Certify by E/I [signature] Date:-
Executive Engineer
R.W.D. Works Division
Gopalganj-1

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Harakhuwa Khawajepur to Oilpur Road
 (Package No.M/R-N/19-20 Gopalganj-1/07
 Length of Road :- 1.580 Km
 Inspector :- J.E RWD Sub Division : Gopalganj

To:-
 Executive Engineer
 RWD, Works Division Gopalganj-1
 Date:-

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N/A	N/A	N/A	N/A							
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major	Lm	N/A	N/A	N/A	N/A							Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil	Nil							Not Required
OM302	Culvert Cleaning	m ³	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	m ²	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whirl washing)												

7/12/2022
 J.E.

6/10/2022
 J.E.

(Signature)
 10/9/22
 Executive Engineer
 R.W.D. Works Division
 Gopalganj-1

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

10/6/2022
A.E

10/6/22
R.D

M's hrs
10/6/22
Executive Engineer
R.W.D. Works Division
Gopetgani-1

Name Of Road :-Harakuwa Khawajapur to Olipur Road

Date	Time	Section	Length	Bumps	Speed	OR	ATEGOR	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	ROAD				
15/8/22	11:25:53	72	0.1	340	10.1	3400	G	3379	26.46411	84.48438	Curve
15/8/22	11:26:0	72	0.1	390	10.1	3900	G	3810	26.4648	84.485	Normal
15/8/22	11:26:28	72	0.1	270	20.2	2700	G	2775	26.46555	84.48551	Normal
15/8/22	11:26:28	72	0.1	260	20.2	2600	G	2689	26.46628	84.48594	Normal
15/8/22	11:26:28	72	0.1	300	20.2	3000	G	3034	26.46628	84.48594	Normal
15/8/22	11:26:28	72	0.1	300	10.1	3000	G	3034	26.46628	84.48594	Normal
15/8/22	11:27:4	72	0.1	290	10.1	2900	G	2948	26.46628	84.48594	Normal
15/8/22	11:27:39	72	0.1	300	10.1	3000	G	3034	26.46628	84.48594	Normal
15/8/22	11:27:39	72	0.1	370	10.1	3700	G	3637	26.47049	84.48685	Normal
15/8/22	11:28:14	72	0.1	380	10.1	3800	G	3724	26.47049	84.48685	Normal
15/8/22	11:28:49	72	0.1	320	20.2	3200	G	3206	26.47049	84.48685	Normal
15/8/22	11:28:49	72	0.1	340	10.1	3400	G	3379	26.47049	84.48685	Normal
15/8/22	11:29:25	72	0.1	370	10.1	3700	G	3637	26.47049	84.48685	Normal
15/8/22	11:30:0	72	0.1	370	20.2	3700	G	3637	26.47049	84.48685	Normal
15/8/22	11:30:35	72	0.1	390	10.1	3900	G	3810	26.47049	84.48685	Speed Breaker

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 3900$$

$$Y = 3810$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001


7/9/2022
J.E
Harpal

10/9/22
R.W.D.

10/9/22
Executive Engineer
R.W.D. Works Division
Gopalganj-1

File : E:\STECO-USB-GPS V1_1\15081344.Xls, Section No. : 72, Eqn : $Y = 0 * X^2 + 0.862 * X + 448.5$

Name of Customer : M/S Sri Krishna Construction Company, Name of Work/ Road : Harakuwa Khawajepur to Olipur

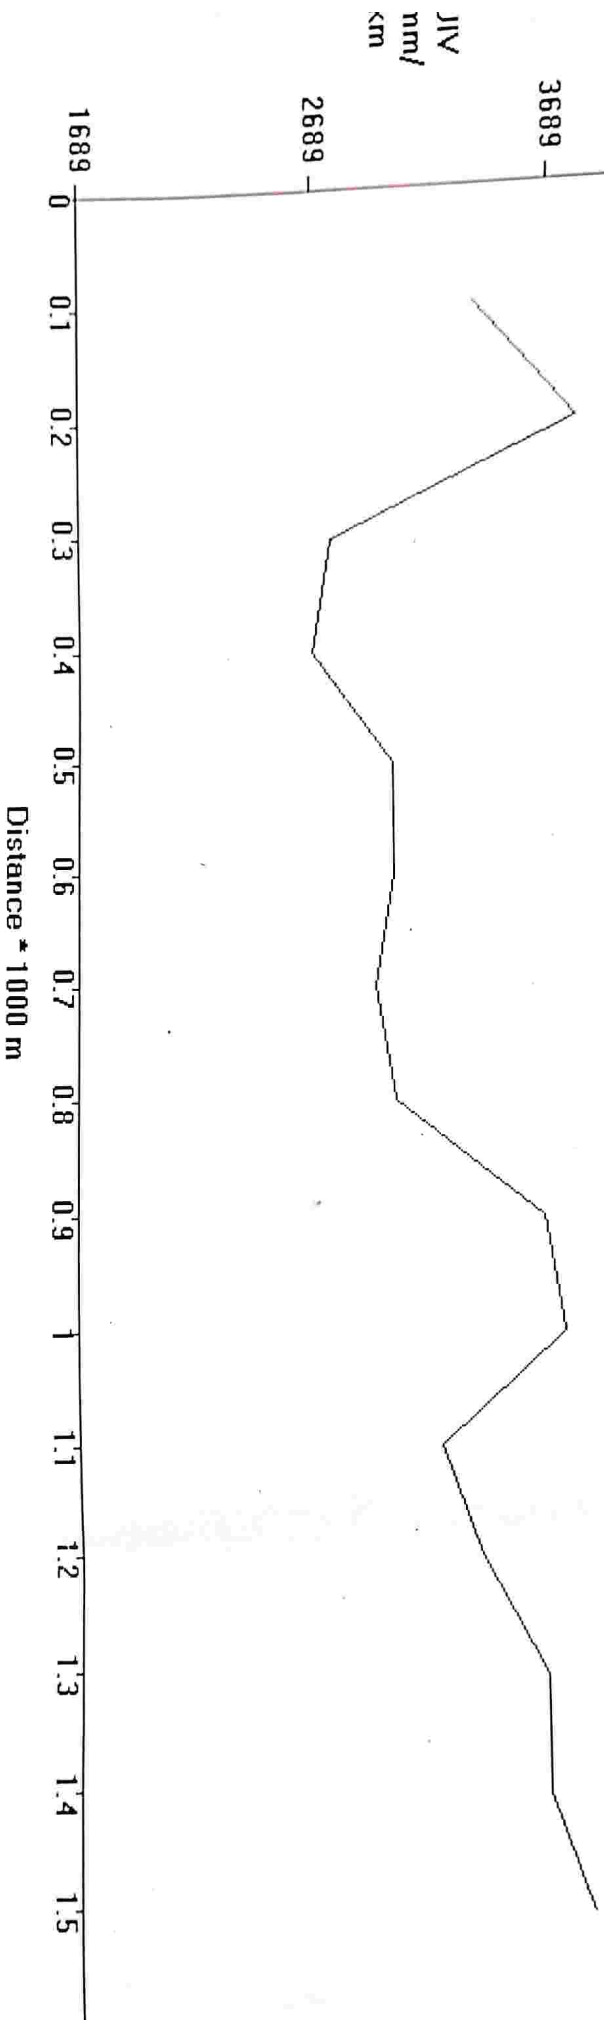

[Signature]
10/9/2022
J.E.

[Signature]
10/9/22

[Signature]
10/9/22
Executive Engineer
R.W.D. WORKS DIVISION
Gopaldham-1
