

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्यप्रमंडल, चकिया, (पूर्वी चम्पारण),

पत्रांक: 759/अनु0/ चकिया, दिनांक: 28/06/2022

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई अनुरक्षण नीति-2018 M.R (3054) योजना के अन्तर्गत पंचवर्षीय अनुरक्षण कार्य के लिए निधि उपलब्ध कराने के संबंध में।

प्रसंग- अभियंता प्रमुख, ग्रा0का0वि0, बिहार, पटना के पत्रांक-मु0अ0-4(मु0)
3054-04-229/2021-1135 (अनु0)/पटना, दिनांक-09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः M.R (3054) नई अनुरक्षण नीति-2018 (Package No.RM/EA/CHA/20/0010) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दशाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया, कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- 1. अधियाचना प्रपत्र।

2. Signed Hard Copy and of recorded IRI is enclosed
3. Standard Format for Roads Quarterly Statement

विश्वासभाजन,

[Signature]
28/06-22

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT (4th Quarter)

PIU Name :- RWD, WD, CHAKIA

1	Name of the Road -	Puranl Mehsl to motnata Village(Barharba)		
2	Batch No. -	RM/EA/CHA/20/0010		
3	Project ID -	31708202186		
4	Total Length of Road (in KM) -	1.013		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	1.013		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	14.33649		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (In Lakh) [2]	0.71682		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUATRER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.71682

Date of Inpection by E/ I or his agent
Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date

04/05/22

04/05/22

Signature of Person inspecting road

(Signature)
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमोद, चकीया
Certify [Signature] Date:-

Requestion Formet for Scheme Head-MR-43054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (4th Quarter)

RWD, Works Division Chakia
Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From - Purant Mehshi to Motnata Village (Barharba)
(Package No RMEACHA200010)

Length of Road - 1.013 Km
Period - From:- 02.09.2021 To 01.12.2021
Inspector - A.E RWD Sub Division : Mehshi

To :-
Executive Engineer
RWD, Works Division Chakia

Position :- A.E

Date:-

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil									No Pot Hole Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil									Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil									No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil									No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil									No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil									No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil									No Edge Repair Required
106	Digouts	m ²	Nil	Nil									
107	Concrete pavement	m ³	N.A	N.A									
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil									No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil									Not Required
	(c) Holding water	Lm	Nil	Nil									No Holding Water Found
OM202	Embankment Repair	M ³	13.64	Nil									Not Required
	Other activities (Ran Cuts)		N.A	N.A									Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A									Not Required
OM302	Culvert Cleaning	No	Nil	Nil									Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil									Not Required
	Other activities (Whitewashing)	M ²	Nil	Nil									Not Required

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	No	Nil	Nil									Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil									Not Required
OM500	Cutting Of Shrubs From Road Way	No	Nil	Nil									Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil									Not Required
OM501	Safety Signage and Road												Not Required
OM502	Signs Maintenance	No	Nil	Nil									Not Required
OM503	Guard Stones	Lm	Nil	Nil									Not Required
OM504	Distance Stones	No	Nil	Nil									Not Required
	Road Marking	M ²	Nil	Nil									Not Required
	Other activities												

Executive Engineer,
Works Division, Chakia

Bidder
Appendix

Signature
22/05/22

Signature
04/5/22

Signature
04/5/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकोया


Name of Customer : VIJAY GIRI
 Name of Work/ Road : TNATA VILLAGE (BARHARBA)
 Lab Job number :
 Date : 24-04-2022
 Section No. : 24

Test Date : 24-04-2022
 Machine No : 406
 Start S No :
 Start E No :
 Weather :
 Start Location : IRANI MEHSI
 End Location : (BARHARBA)
 Road Name : TNATA VILLAGE (BARHARBA)
 Road Type : (R) RURAL ROAD
 Side :
 UV Range : 1057 To 4000
 Dist Range : 0 To 1013
 Interval : 1000
 Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

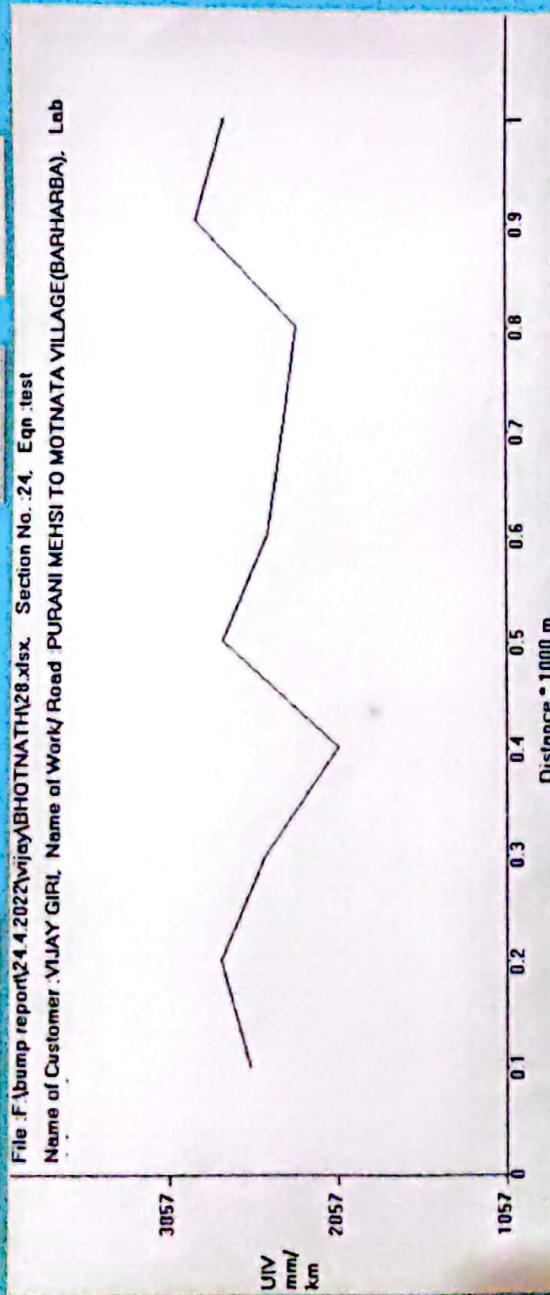

Signature

Signature
 24/4/22

Signature
 कार्यपालक अभियंता
 ग्रामीण कार्य विभाग
 कार्य प्रमण्डल, चकीया

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI,TEGORY ROAD	Latitude ongitude	Event
ROAD NAME- PURANI MESHI TO MOTNATA VILLAGE (BARHARBA)									
24/ 4/ 22	14: 42: 12	24	0.1	270	20.2	2700	2579 G	26.3615	85.14051 Normal
24/ 4/ 22	14: 43: 0	24	0.1	290	20.2	2900	2752 G	26.36112	85.13963 Normal
24/ 4/ 22	14: 43: 0	24	0.1	260	20.2	2600	2492 G	26.36076	85.1387 Normal
24/ 4/ 22	14: 43: 22	24	0.1	210	20.2	2100	2057 G	26.36056	85.13776 Normal
24/ 4/ 22	14: 43: 22	24	0.1	290	20.2	2900	2752 G	26.36038	85.13678 Normal
24/ 4/ 22	14: 44: 0	24	0.1	260	20.2	2600	2492 G	26.36019	85.13574 Normal
24/ 4/ 22	14: 44: 0	24	0.1	250	20.2	2500	2405 G	26.36001	85.13481 Normal
24/ 4/ 22	14: 44: 0	24	0.1	240	20.2	2400	2318 G	26.35982	85.13382 Normal
24/ 4/ 22	14: 44: 33	24	0.1	310	20.2	3100	2926 G	26.35945	85.13291 Normal
24/ 4/ 22	14: 44: 33	24	0.1	290	20.2	2900	2752 G	26.35902	85.13199 Normal
TOTAL							25525		
AVERAGE							2552.5		

**कायदपुण्डलक अस्पताल
कायदपुण्डल, चक्रिया**

24/4/22
Dhyan

Zul
