

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 481(3054) / बिहारशरीफ, दिनांक 18-4-23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०—यथोक्त।

विश्वासभाजन


18/4/23


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
18/04/23

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bihar Sharif

1 Year (2nd Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- NH-82 Soyba pachetan road to village srichandpur
(Package No.RM/NA/BIH/19/0002)
Length of Road :- 0.58Km
Inspector :- J.E RWD Sub Division : Asthwan

To:-

Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

standard Of Work Item		Work Unit	Unit Of Required in each Kilometer										Comments
No	Name		1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

18/12/21

18/12/21

18/12/21

Executive Engineer
Rural Work Department
Work Division Bihar Sharif

18/12/21

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	
2	Batch No.-	NH-82 Soyba pachetan road to village srichandpur
3	Project ID -	RM/NA/BIH/19/0002
4	Total Length of Road (in Km)	10200701033
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	0.58
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	0.58
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	20
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	5.56004
		0.27800

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.00000
				0.27800

Date of inspection by E/1 or his agent


Date

Name and Designation of person inspecting road

Signature of person inspecting road

Certify by E/1 (signature) Date

File : E:\Bump Machine\Bump Reading\Maa Tara Construction\01051720.xls, Section No. : 85, Egn : $Y = 0 - X^2 +$
 Name of Customer : Maa Tara Construction, Name of Work/ Road : NH-82 Soyba pachetan road to village

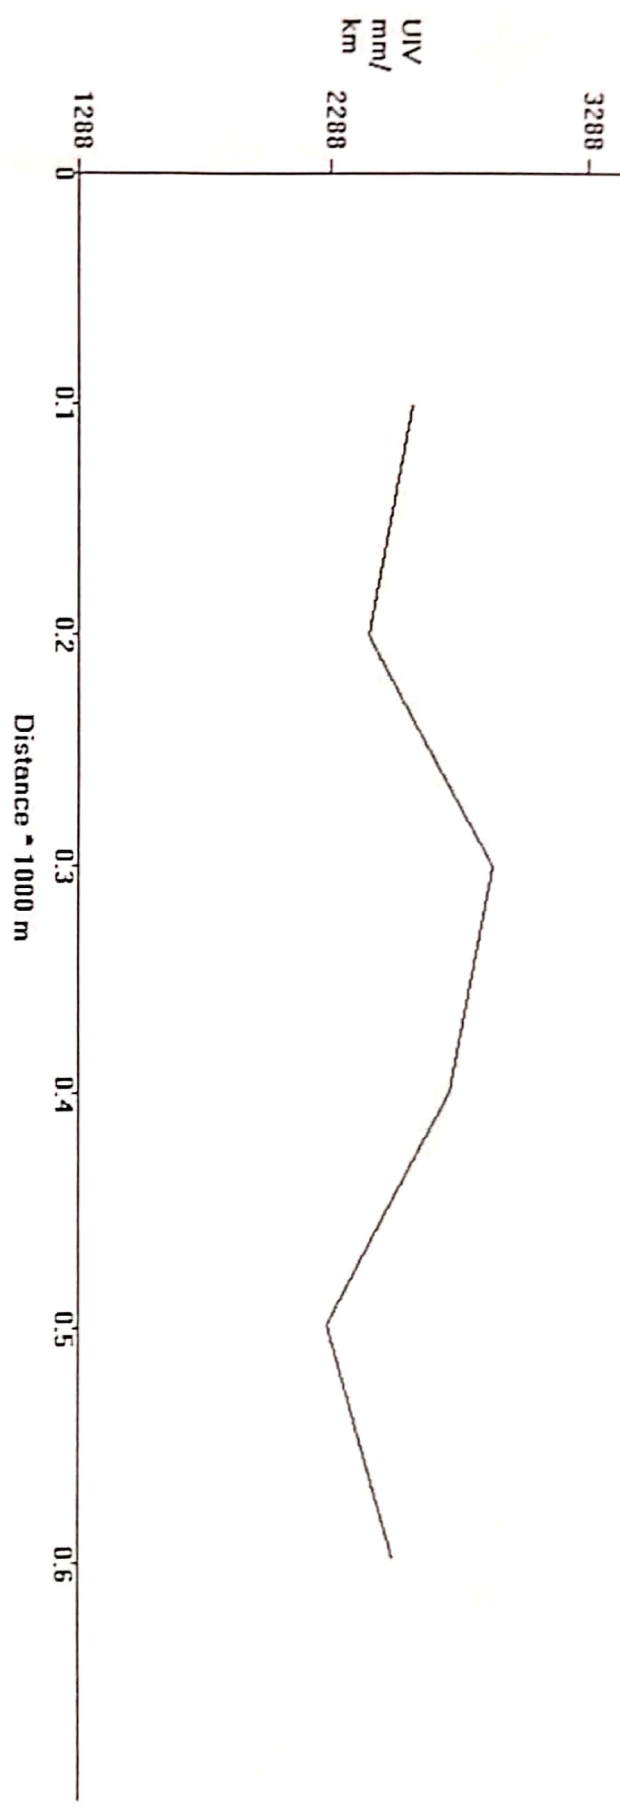

⑪
 2/9/2022

2/9/2022

Scheme-NEW MR
Road Name-NH-82 soywa pachetan road se srichandanpur
Contractor-Maa Tara Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event						
1/5/22	14:42:22	85	0.1	290	0	2900	2615	G	25.230103	85.613047	Normal	$Y = 0 * X^2 + 0.816 * X + 249$					
1/5/22	14:43:00	85	0.1	270	30.3	2700	2452	G	25.230243	85.614107	Normal				X = 3100		
1/5/22	14:43:33	85	0.1	330	10.1	3300	2941	G	25.230457	85.6151	Normal	(R) RURAL ROAD			Y = 2778		
1/5/22	14:43:33	85	0.1	310	10.1	3100	2778	G	25.23056	85.616178	Normal						
1/5/22	14:44:44	85	0.1	250	10.1	2500	2288	G	25.230688	85.616178	Normal				Good	Average	Poor
1/5/22	14:45:00	85	0.1	280	10.1	2800	2533	G	25.230453	85.615302	Normal				<4000	4001-5000	>5001
							Total										
							IRI Value	2601									

①
 2/5/22
 14:42

2/5/22
 14:42
