

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 481(305) / बिहारशरीफ, दिनांक 18-4-23.

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०-यथोक्त।

विश्वासभाजन


18/4/23


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
18/04/23

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bihar Sharif

1 Year (2nd Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-Nauranga Bridge - Ishwarchak
(Package No.RM/NA/BIH/19/0003)

Length of Road :- 3.312 Km

Inspector :- J.E RWD Sub Division : Blind

To:-

Executive Engineer
RWD, Works Division Bihar Sharif

Date:-

Position :- J.E

No	standard Of Work Item	Work	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil	Nil							Not Required

Standard Of Work Item		Work	Unit Of Required in each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Handwritten signature

Handwritten signature

Handwritten signature

Handwritten signature

Executive Engineer
Rural Work Department
Work Division Bihar Sharif

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	
2	Batch No.-	Nauranga Bridge - Ishwarchak
3	Project ID -	RM/NA/BIH/19/0003
4	Total Length of Road (in Km)	10200702010
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	3.312
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	3.312
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	20
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	30.79100
		1.53955

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.53955

Date of inspection by E/1 or his agent


Name and Designation of person inspecting road

Date

Signature of person inspecting road

Certify by E/1 (signature) Date

File : E:\Bump Machine\Bump Reading\Maa Tara Construction\01051720.Xls, Section No. :84, Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Maa Tara Construction, Name of Work/ Road : Nauranga Bridge - Ishwarchak, Lab Job number

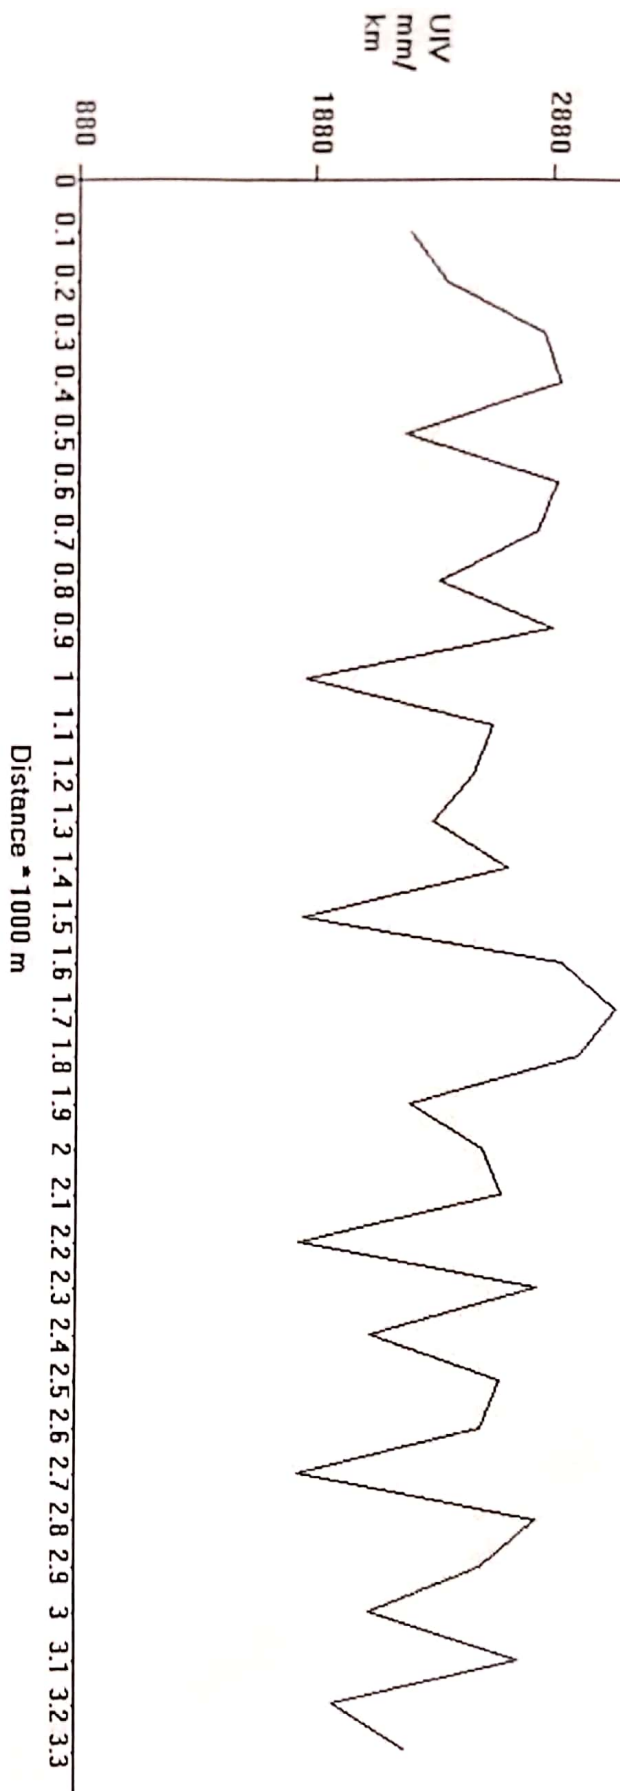

[Handwritten signature]
15/05/22

[Handwritten signature]
15/05/22
me

Scheme-NEW IIR
Road Name-Nauranga Bridge se Ishwar Chak
Contractor-Maa Tara Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event						
1/5/22	10:23:0	84	0.1	250	0	2500	2288	G	25.32788	85.69515	Normal						
1/5/22	10:23:10	84	0.1	270	10.1	2700	2452	G	25.328278	85.694292	Normal						
1/5/22	10:23:10	84	0.1	320	10.1	3200	2860	G	25.328827	85.693535	Normal						
1/5/22	10:23:10	84	0.1	330	10.1	3300	2941	G	25.329125	85.692608	Normal						
1/5/22	10:23:45	84	0.1	250	10.1	2500	2288	G	25.329323	85.691497	Curve						
1/5/22	10:23:45	84	0.1	330	10.1	3300	2941	G	25.32846	85.69111	Normal						
1/5/22	10:24:0	84	0.1	320	10.1	3200	2860	G	25.327612	85.69074	Normal						
1/5/22	10:24:0	84	0.1	270	10.1	2700	2452	G	25.32677	85.690487	Normal						
1/5/22	10:24:21	84	0.1	330	10.1	3300	2941	G	25.325903	85.690505	Normal						
1/5/22	10:24:21	84	0.1	200	10.1	2000	1880	G	25.324915	85.690572	Normal						
1/5/22	10:24:21	84	0.1	300	10.1	3000	2656	G	25.324442	85.689713	Curve						
1/5/22	10:24:56	84	0.1	290	10.1	2900	2615	G	25.323547	85.689578	Normal						
1/5/22	10:25:0	84	0.1	270	10.1	2700	2452	G	25.32269	85.689477	Normal						
1/5/22	10:25:0	84	0.1	310	10.1	3100	2778	G	25.321705	85.689427	Normal						
1/5/22	10:25:0	84	0.1	200	10.1	2000	1880	G	25.320853	85.689208	Normal						
1/5/22	10:25:31	84	0.1	340	10.1	3400	3023	G	25.319945	85.68914	Normal						
1/5/22	10:25:31	84	0.1	370	10.1	3700	3268	G	25.319125	85.688618	Normal						
1/5/22	10:25:31	84	0.1	350	10.1	3500	3104	G	25.31872	85.687827	Normal						
1/5/22	10:26:0	84	0.1	260	10.1	2600	2370	G	25.318745	85.68678	Normal						
1/5/22	10:26:7	84	0.1	300	10.1	3000	2656	G	25.31882	85.685673	Normal						
1/5/22	10:26:7	84	0.1	310	10.1	3100	2778	G	25.318915	85.684747	Normal						
1/5/22	10:26:7	84	0.1	200	10.1	2000	1880	G	25.31899	85.683687	Normal						
1/5/22	10:26:7	84	0.1	330	10.1	3300	2941	G	25.318978	85.682677	Normal						
1/5/22	10:26:42	84	0.1	240	10.1	2400	2207	G	25.319073	85.681615	Normal						
1/5/22	10:26:42	84	0.1	310	10.1	3100	2778	G	25.31918	85.680605	Normal						
1/5/22	10:27:0	84	0.1	300	10.1	3000	2656	G	25.31935	85.679528	Curve						
1/5/22	10:27:0	84	0.1	200	10.1	2000	1880	G	25.318677	85.679175	Normal						
1/5/22	10:27:16	84	0.1	330	10.1	3300	2941	G	25.317747	85.678955	Normal						
1/5/22	10:27:16	84	0.1	300	10.1	3000	2696	G	25.316865	85.678787	Normal						
1/5/22	10:27:16	84	0.1	240	10.1	2400	2207	G	25.316275	85.678198	Normal						
1/5/22	10:28:27	84	0.1	320	10.1	3200	2860	G	25.316503	85.677272	Normal						
1/5/22	10:30:13	84	0.1	220	10.1	2200	2044	G	25.31628	85.677727	Normal						
1/5/22	10:30:13	84	0.1	260	10.1	2600	2370	G	25.316385	85.67872	Normal						
						Total	85063										
						IRI Value	2578										

[Signature]
 15/05/22

[Signature]
 21/5/22
 MC
