

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1563

/नरकटियागंज, दिनांक 19.8.23

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ:-

1. Jhumka se Dukhi Chhapar

का कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज

15/8/23

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative Approval(AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	MR-N/19-20 NARKATIAGANJ/ 12	Jhumka se Dukhi Chhapar	318891031927	3350 01.08.2019	4.000	173.06600	187.01035	36.20968	2020-21 26.05.2020	25.05.2021	28.03.2022	2799	SDBC-25mm	5%	126.19918	126.19918	46.81117	Complete

Hin
19/8/2023
J.C

Re
19/08/23
AE

Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

19/8/23

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Jhumka se Dukhi Chhapar

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- AKHTAR IMAM

Length of Road :- 4.000 KM

Project ID :- 318891031927

Package No. :- MR-N/19-20 NARKATIAGANJ/12

Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me

Hin
19/08/2023
J.E.

Certified that all item wise 50% measurement has been verified by me

Revan
19/08/23
AE

Certified that all item wise 10% measurement has been verified by me

M. S. B.
19/08/23

Name of Road - Jhumka se Dukhi Chhapar (Sec-83)


Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
2/8/23	17:16:0	83	0.1	260	20.3	2600	2645	G	26.96202	84.62771	Normal
2/8/23	17:17:0	83	0.1	230	20.3	2300	2341	G	26.962	84.628652	Normal
2/8/23	17:17:0	83	0.1	220	20.3	2200	2237	G	26.96258	84.629242	Normal
2/8/23	17:17:28	83	0.1	260	20.3	2600	2627	G	26.963402	84.629662	Culvert
2/8/23	17:18:0	83	0.1	300	20.3	3000	3033	G	26.964207	84.63002	Culvert
2/8/23	17:18:3	83	0.1	250	20.3	2500	2563	G	26.965008	84.630318	Normal
2/8/23	17:18:38	83	0.1	230	20.3	2300	2349	G	26.96592	84.630555	Normal
2/8/23	17:19:0	83	0.1	310	20.4	3100	3103	G	26.966555	84.631178	Normal
2/8/23	17:19:14	83	0.1	300	20.1	3000	3028	G	26.96743	84.631195	Curve
2/8/23	17:19:14	83	0.1	230	20.2	2300	2327	G	26.96825	84.631582	Normal
2/8/23	17:20:0	83	0.1	270	20.3	2700	2734	G	26.969043	84.631968	Normal
2/8/23	17:20:0	83	0.1	270	21.3	2700	2748	G	26.969842	84.63234	Normal
2/8/23	17:20:24	83	0.1	250	21.3	2500	2567	G	26.970707	84.632625	Normal
2/8/23	17:20:24	83	0.1	300	22.3	3000	3032	G	26.971547	84.632912	Normal
2/8/23	17:20:24	83	0.1	250	20.2	2500	2554	G	26.972335	84.63337	Normal
2/8/23	17:21:0	83	0.1	310	30.3	3100	3180	G	26.97311	84.633838	Normal
2/8/23	17:21:0	83	0.1	270	20.2	2700	2741	G	26.97388	84.634208	Normal
2/8/23	17:21:0	83	0.1	260	20.1	2600	2643	G	26.974732	84.634578	Normal
2/8/23	17:21:35	83	0.1	230	20.2	2300	2357	G	26.97542	84.63515	Normal
2/8/23	17:21:35	83	0.1	250	20.3	2500	2553	G	26.976195	84.63574	Normal
2/8/23	17:22:0	83	0.1	290	20.1	2900	2947	G	26.976838	84.636328	Normal
2/8/23	17:22:10	83	0.1	270	20.1	2700	2783	G	26.977677	84.636582	Normal
2/8/23	17:22:10	83	0.1	270	21.2	2700	2765	G	26.978597	84.63678	Normal
2/8/23	17:22:45	83	0.1	330	22.2	3300	3300	G	26.97941	84.637188	Normal
2/8/23	17:23:0	83	0.1	310	20.2	3100	3180	G	26.980163	84.637592	Normal
2/8/23	17:23:0	83	0.1	270	22.3	2700	2712	G	26.980902	84.63813	Normal
2/8/23	17:23:21	83	0.1	270	23.3	2700	2736	G	26.981443	84.638972	Normal
2/8/23	17:24:0	83	0.1	330	20.2	3300	3367	G	26.98178	84.639898	Curve
2/8/23	17:24:0	83	0.1	310	24.3	3100	3180	G	26.982427	84.640522	Normal
2/8/23	17:25:6	83	0.1	280	23.3	2800	2805	G	26.98327	84.64079	Normal
2/8/23	17:26:0	83	0.1	280	24.3	2800	2835	G	26.984135	84.640875	Normal
2/8/23	17:26:17	83	0.1	300	24.3	3000	3086	G	26.985015	84.641027	Normal
2/8/23	17:26:52	83	0.1	260	20.2	2600	2648	G	26.985798	84.641347	Normal
2/8/23	17:27:0	83	0.1	260	26.3	2600	2618	G	26.986675	84.641648	Normal

Name of Road - Jhumka se Dukhi Chhapar (Sec-83)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
2/8/23	17:27:27	83	0.1	320	23.3	3200	3273	G	26.987527	84.641952	Normal
2/8/23	17:27:27	83	0.1	320	20.2	3200	3209	G	26.988322	84.64234	Normal
2/8/23	17:28:2	83	0.1	260	22.3	2600	2648	G	26.989123	84.642777	Normal
2/8/23	17:28:2	83	0.1	300	22.6	3000	3086	G	26.989887	84.643282	Normal
2/8/23	17:30:23	83	0.1	250	23.4	2500	2593	G	26.990113	84.64342	Normal
2/8/23	17:35:5	83	0.1	280	26.2	2800	2812	G	26.989848	84.643282	Normal
Average IRI Value=							2799				

Hin
19/8/2023
J.C.

Peru
19/08/23
AE


Executive Engineer
Rural Works Department
 Work Division, Narkatiyagani

 19/8/23

Name of Customer : Akhtar Imam
 Name of Work/ Road : Jhumka se Dukhi Chhapar
 Lab Job number :
 Date : 04-08-2023
 Section No. : 83


Test Date : 04-08-2023 Road Name : Jhumka se Dukhi Chhapar
 Machine No : 402 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 1237 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 4.1 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

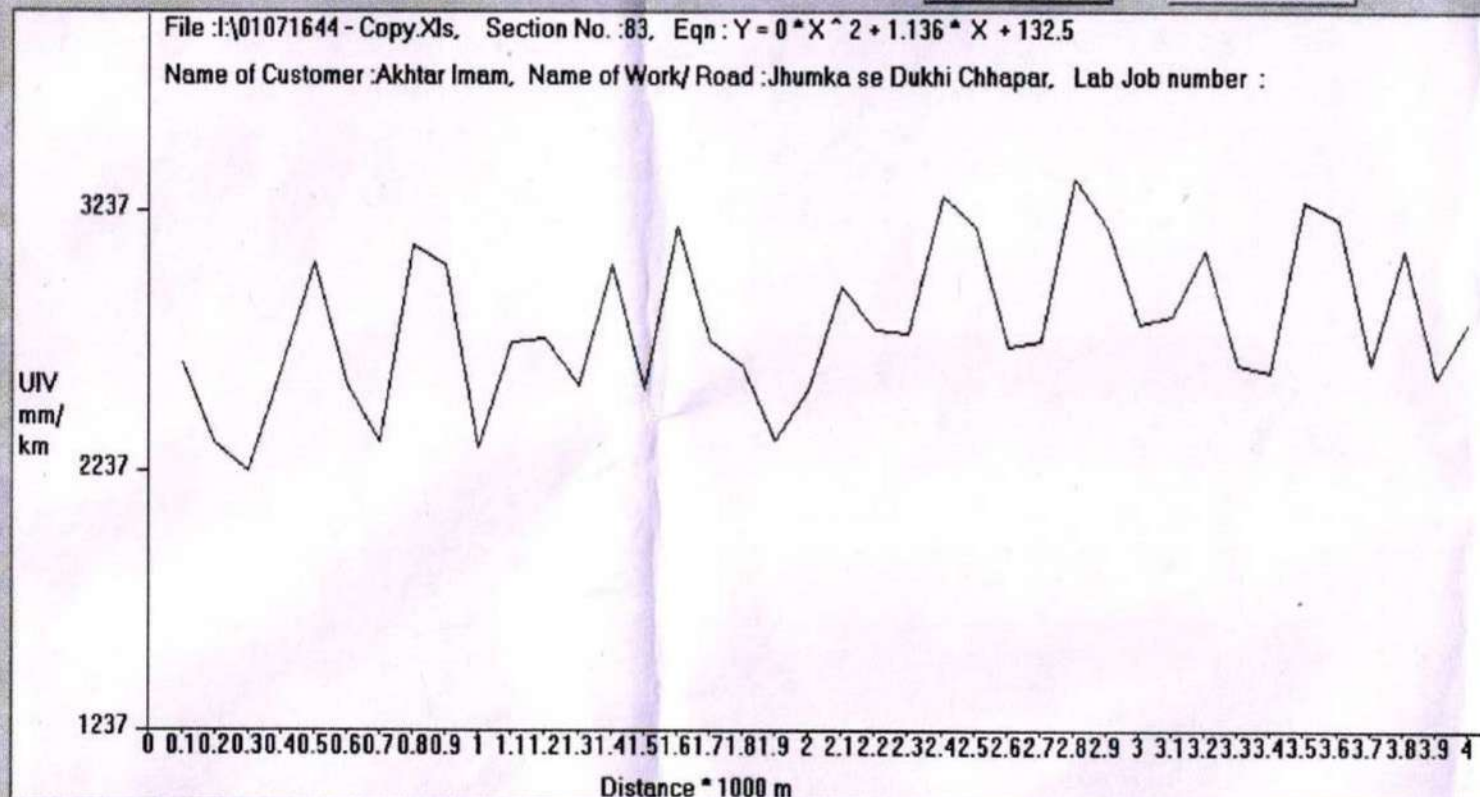

Hin
19/8/2023
J.E.

Re
19/08/23
AE

Executive Engineer
 Rural Works Department
 Work Division, Narkatiyaganj

19/8/23
