

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

पत्रांक :- १५९ (उसु)

पटना / दिनांक :- 6/2/23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना ।

सेवा में,

सचिव, ब्राडा (बी.आर.आर.डी.ए.),
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 योजना अन्तर्गत
अनुरक्षण मद में आवंटन का अध्याचना के संबंध में ।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ
नई अनुरक्षण नीति-2018 योजना अन्तर्गत अनुरक्षण मद में निम्नांकित पथों का आवंटन का
अध्याचना का मांग (Yearly Quarter wise) तैयार कर आवश्यक कार्रवाई हेतु समर्पित किया
जाता है, जो निम्न प्रकार है :-

Sl. No.	Name of Road	Yearly Quarter wise	Amount (in Lakh)
1.	Panapur to Nakta (Package No.- MR-N/2019-20/PATNA/10)	1 st Year-1 st Quarter	0.96908
		1 st Year-2 nd Quarter	0.96908
		1 st year-3 rd Quarter	0.96908
		1 st year-4 th Quarter	0.96908
		2 nd year-1 st Quarter	0.96908
		2 nd year-2 nd Quarter	0.96908

अतः अनुरोध है कि उक्त योजना अन्तर्गत अनुरक्षण मद में आवंटन उपलब्ध कराने
की कृपा की जाय, ताकि संवेदक का भुगतान किया जा सके ।

अनु०:- यथोक्त ।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road -	Panapur to Nakta		
2	Batch No. -	RMPA/PAT/19/0010		
3	Project ID -	10103556		
4	Total Length of Road (in Km)	3.2		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.174		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	19.38154		
8	Quarterly Payment 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.96908		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGETATION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.96908
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				

Date of inspection by E/1 or his agent

Name and Designation of person inspecting road

Date

Certify by E/1 (signature) Date

Signature of person inspecting road

Sabita
28/12/22

JE

Wdson
28/12/22
AE

Requisition Form for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Patna

2 Year (6th Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTNANCE INSPECTION REPORT

Road From:- Panapur to Naktia
(Package No. MR-N/2019-2020/PATNA/10)
Length of Road > 3.200 Km
Inspector > JE RWD Sub Division : Patna Sader

To:-

Executive Engineer
RWD, Works Division Patna

Date:

Position :- JE

No	Name	Work	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Toss Of Aggregates (Surface Ravelling) Found
	Surface Treatment	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
OM104	(a) Loss of Agregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							N/A
106	Di-cours	m ²	N/A	N/A	N/A	N/A							
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							
	Other activities												No Edge Drop-Off Required
OM200	Shoulder												Not Required
	Unsealed Shoulder	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Not Required
	(b) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							N/A
	(c) Roughness, Scouring or Pot-holes	Lm	Nil	Nil	Nil	Nil							
	(d) Holding water	M ³	Nil	Nil	Nil	Nil							
OM202	Embankment Repair		Nil	Nil	Nil	Nil							N/A
	Other activities (Rain Cuts)												Not Required
OM300	Drainage including culverts major	Lm	N/A	N/A	N/A	N/A							Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil	Nil							Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (with mix washing)	M ³	Nil	Nil	Nil	Nil							

Sobhan
28/12/22
JE

Signature
Sobhan
JE

Signature
Sobhan
JE

No	Standard Of Work Item	Work Unit	Unit Of Required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
	Name												
OM400	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside - General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							N/A
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							
	Other activities												

Executive Engineer
Rural Work Department
Work Division Patna

(Signature)

Sabite
28/12/22

28/12/22
28/12/22

JE

Name of The Road : Panapur to Nakta

Length : 3.174 Km

Package No. : M/R-N/2019-2020/PATNA/10

Division : Patna

Block : Patna Sadar

Contractor Name : SHUBHAMMANA FOUNDATION CONSTRUCTION PVT.LTD

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event		
15/08/2022	12:58:50	74	0.1	280	0	2800	2899	ROAD	25.66412	85.5771	Normal	$y = 0 \cdot x^2 + 0.936 \cdot x + 2.716.4$	
15/08/2022	12:59:0	74	0.1	230	20.2	2300	2431	G	25.664858	85.8673	Normal		
15/08/2022	12:59:25	74	0.1	350	30.3	3800	3835	G	25.664963	85.85757	Normal	$x = 35.00$	
15/08/2022	12:59:25	74	0.1	360	30.3	3600	3648	G	25.664895	85.8483	Normal	$y = 35.54$	
15/08/2022	13:0:0	74	0.1	260	20.2	2600	2599	G	25.664958	85.83832	Normal		
15/08/2022	13:0:36	74	0.1	260	20.2	2600	2150	G	25.665597	85.82945	Normal	(R)Rural Road	
15/08/2022	13:1:11	74	0.1	200	30.3	3300	3554	G	25.665937	85.82037	Normal	Average	
15/08/2022	13:1:46	74	0.1	350	30.3	3500	3554	G	25.665958	85.81077	Normal	4001-5001	
15/08/2022	13:2:0	74	0.1	230	20.2	3300	2431	G	25.665845	85.8012	Normal		
15/08/2022	13:2:21	74	0.1	330	30.3	3200	2337	G	25.665402	85.78298	Normal		
15/08/2022	13:3:0	74	0.1	260	30.3	2600	2712	G	25.665127	85.77407	Normal		
15/08/2022	13:4:36	74	0.1	290	30.3	2900	2992	G	25.664707	85.76565	Normal		
15/08/2022	13:5:0	74	0.1	250	30.3	2500	2712	G	25.66452	85.75588	Normal		
15/08/2022	13:5:11	74	0.1	280	30.3	2800	2818	G	25.664329	85.74645	Normal		
15/08/2022	13:5:11	74	0.1	280	30.3	2800	2899	G	25.664535	85.7367	Normal		
15/08/2022	13:5:11	74	0.1	270	30.3	2700	2805	G	25.665802	85.7275	Normal		
15/08/2022	13:6:22	74	0.1	210	20.2	2100	2244	G	25.665213	85.7079	Normal		
15/08/2022	13:6:22	74	0.1	290	10.1	2900	2992	G	25.665347	85.69848	Normal		
15/08/2022	13:10:22	74	0.1	320	20.2	3200	3273	G	25.665562	85.68872	Normal		
15/08/2022	13:10:58	74	0.1	220	30.3	2200	2337	G	25.665561	85.67978	Normal		
15/08/2022	13:11:0	74	0.1	280	30.3	2800	2899	G	25.665147	85.67053	Normal		
15/08/2022	13:11:0	74	0.1	260	30.3	2600	2712	G	25.665005	85.66127	Normal		
15/08/2022	13:22:25	74	0.1	280	30.3	2800	2899	G	25.664765	85.65185	Normal		
15/08/2022	13:22:25	74	0.1	340	30.3	3400	3460	G	25.664325	85.64377	Normal		
15/08/2022	13:35:20	74	0.1	360	30.3	3600	3648	G	25.664022	85.6345	Normal		
15/08/2022	13:38:12	74	0.1	330	30.3	3300	3367	G	25.66377	85.6249	Normal		
15/08/2022	13:38:12	74	0.1	360	30.3	3600	3648	G	25.663353	85.61532	Normal		
15/08/2022	13:41:00	74	0.1	310	30.3	3100	3180	G	25.663273	85.605572	Normal		
15/08/2022	13:43:02	74	0.1	320	20.2	3200	3273	G	25.662838	85.5978	Normal		
15/08/2022	13:43:02	74	0.074	350	30.3	3500	3554	G	25.6624	85.59073	Normal		
Total			3.174	9240	848.4	92400	95386		821.271581	2743.130312			
Average						2887.5	2580.812						

Sadek
 28/11/22
 5E
 Mubinn
 28/11/22
 5E
 35/11/22
 5E

Name of Customer : SHUBHAMANA FOUNDATION
 Name of Work/Road : Panpur to Naha
 Lab Job number :
 Date : 15/09/2022
 Section No. : 74


Test Date : 15/09/2022
 Road Name : Panpur to Naha
 Machine No : 374
 Road Type : (R) RURAL ROAD
 Start S No :
 Start E No :
 Side :
 Interval :
 Weather :
 UIV Range : 1150 To 5000 mm/km
 Start Location :
 Dist Range : 0 To 33 0.1 • 1000 m
 End Location :
 Equation : $Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BPRD\23OneDrive\Desktop\13031750.xls, Section No. : 74, Equ : $Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$
 Name of Customer : SHUBHAMANA FOUNDATION CONSTRUCTION PVT.LTD, Name of Work/Road : Panpur to

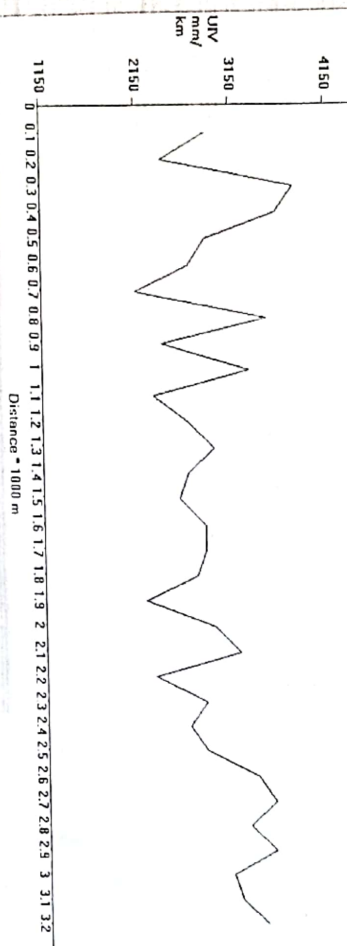

Sabir
28/11/22
SE

15/09/2022
SABIR

SABIR
28/11/22
