

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग कार्य प्रमंडल बांका-1

पत्रांक : ..1103...../ बांका

दिनांक : 26.06.2023

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल बांका-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण पटना।

विषय:- शीर्ष-MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत पंचवर्षीय
अनुरक्षण कार्य के तहत अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ
अनुरक्षण नीति-2018 योजनान्तर्गत पंचवर्षीय अनुरक्षण कार्य के तहत कराये गये निर्माण कार्य
में भुगतान हेतु राशि उपलब्ध कराने की कृपा की जाए। इस पत्र के साथ विहित प्रपत्र में
अधियाचित राशि समर्पित की जा रही है।

अनु०:- 1. अधियाचना प्रपत्र

विश्वासभाजन

26/6/23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग
कार्य प्रमंडल बांका-1

26/06/2023

Rural Works Department

Requisition Format for Scheme Head-MIR(3054) under Bihar Rural Road Maintenance Policy-2018 (5 years Quarterly Maintenance)

Name of Division :- **BANKA-1**
 Scheme Head:- **Scheme Head-MIR(3054) under Bihar Rural Road Maintenance Policy-2018- 5year Quarterly maintenance**

Sr. No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction			Agreement amount (in Lakhs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Requisition Against Work done (In Lakh)					Total Amount	Remarks
				Ltr No & Date	Length (in Km)	Amounts (in Lakhs)	Initial Rectification with Surface Renewal	Maintenance				1st Year						
												1st Qtr (Amt)	2nd Qtr (Amt)	3rd Qtr (Amt)	4th Qtr (Amt)			
1	RM/BA/ BAN/19/ 0005	Kurma More (Shambhuganj Asarganj RCD Road) to Goyara Lakhampur	20703501017	1836 24 06-2019	5.300	198.04450	118.47000	47.70550	SBD-10/ 2019-20 06.11.2019	05-08-2022	19-09-2020	2.35150	2.30650	1.96900	1.86100	8.48800		
2	RM/BA/ BAN/19/ 0005	Chhathar to Khajuri	20703502217	1836 24 06-2019	3.000	97.66000	60.13100	24.91702	SBD-10/ 2019-20 06.11.2019	05-08-2022	19-09-2020	1.17320	1.07970	1.00710	0.91990	4.17990		
3	RM/BA/ BAN/19/ 0005	Bhumihara More to Bharatshila Village	NEA22000402	1836 24 06-2019	1.380	49.22600	27.68900	11.78954	SBD-10/ 2019-20 06.11.2019	05-08-2022	19-09-2020	0.55740	0.46770	0.38660	0.42930	1.84100		
4	RM/BA/ BAN/19/ 0005	Mitrapur- Kirampur Road Pahalampur via Pararia	NEA22000416	1836 24 06-2019	4.650	155.76000	99.01700	36.96535	SBD-10/ 2019-20 06.11.2019	05-08-2022	19-09-2020	1.81850	1.73500	1.48060	1.38520	6.41930		
																	20.92820	

Sr. Div. Actg. Officer
 RWD (Works Division), Banka-1

Executive Engineer
 RWD (Works Division), Banka-1

26/06/2023

26/06/2023

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- R.W.D. BANKA-1

1	Name of the Road	Chhathar to Khajuri		
2	Batch No	RM/BA/BAN/19/0005		
3	Project ID	20703502217		
4	Total Length of Road (in Km)	3.000		
5	Length of Road to Meet Required Service level [Completed length] (in Km) [1]	3.000		
6	No. of total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement amount of Maintenance] (in Lakh)	24.91702		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.24585		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weightage Value for Payment Reduction % [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.0000
II	SHOULDERS AND EMBANKMENT	4.1	10%	0.1703
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	2	15%	0.1246
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.0000
V	VEGETATION	1.5	5%	0.0311
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.3260
TO BE PAID FOR QUARTER/DEMAND (in Lakh) [6]				0.9199

Jamit
20/06/23
J.E

Pritam
20.06.23
A.E

26/6/23

Lab Job number :168			
Date :17-06-2023			
Name of Customer :Prince Construction			
Name of Work/ Road :Chhathar To Khajuri			
Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.1	2571	G
2	0.2	3163	G
3	0.3	2977	G
4	0.4	3564	G
5	0.5	2575	G
6	0.6	2973	G
7	0.7	2555	G
8	0.8	2562	G
9	0.9	2571	G
10	1	2542	G
11	1.1	2576	G
12	1.2	2371	G
13	1.3	2356	G
14	1.4	2547	G
15	1.5	2758	G
16	1.6	2353	G
17	1.7	2491	G
18	1.8	2551	G
19	1.9	2737	G
20	2	2543	G
21	2.1	3347	G
22	2.2	3467	G
23	2.3	3438	G
24	2.4	3457	G
25	2.5	3155	G
26	2.6	3175	G
27	2.7	3681	G
28	2.8	3296	G
29	2.9	3129	G
30	3.00	3540	G

Samir
20/06/23
J.E

Pritham
20/06/23
H.E

Star
20/6/23

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
17-06-2023	08:53:00	158	0.1	280	20.2	2800	2571	G	3.77	25.077092	86.673353	Normal
17-06-2023	08:54:31	158	0.1	320	20.2	3200	3163	G	4.23	25.076907	86.674113	Normal
17-06-2023	08:55:45	158	0.1	300	30.3	3000	2977	G	4	25.076723	86.674872	Normal
17-06-2023	08:56:06	158	0.1	360	20.2	3600	3564	G	4.69	25.076538	86.675632	Normal
17-06-2023	08:56:58	158	0.1	280	10.1	2800	2575	G	3.77	25.076354	86.676391	Normal
17-06-2023	08:57:32	158	0.1	300	30.3	3000	2973	G	4.03	25.076169	86.677151	Normal
17-06-2023	08:58:14	158	0.1	280	30.3	2800	2555	G	3.77	25.075984	86.677911	Normal
17-06-2023	08:59:39	158	0.1	280	20.2	2800	2562	G	4.7	25.075800	86.678670	Normal
17-06-2023	09:00:32	158	0.1	280	20.2	2800	2571	G	3.77	25.075615	86.679430	Normal
17-06-2023	09:03:34	158	0.1	280	20.2	2800	2542	G	2.82	25.075431	86.680189	Normal
17-06-2023	09:04:09	158	0.1	280	20.2	2800	2576	G	3.06	25.075246	86.680949	Normal
17-06-2023	09:04:57	158	0.1	240	20.2	2400	2371	G	3.3	25.075061	86.681709	Normal
17-06-2023	09:05:16	158	0.1	240	30.3	2400	2356	G	3.3	25.074877	86.682468	Curve
17-06-2023	09:05:56	158	0.1	280	10.1	2800	2547	G	2.57	25.074692	86.683228	Normal
17-06-2023	09:06:09	158	0.1	290	10.1	2900	2758	G	2.94	25.074508	86.683987	Normal
17-06-2023	09:06:48	158	0.1	240	10.1	2400	2353	G	3.3	25.074323	86.684747	Normal
17-06-2023	09:07:28	158	0.1	250	20.2	2500	2491	G	3.42	25.074138	86.685507	Normal
17-06-2023	09:07:57	158	0.1	270	20.2	2700	2551	G	2.45	25.073954	86.686266	Normal
17-06-2023	09:08:0	158	0.1	290	10.1	2900	2737	G	2.94	25.073769	86.687026	Normal
17-06-2023	09:08:35	158	0.1	250	30.3	2500	2543	G	2.2	25.073585	86.687785	Normal
17-06-2023	09:09:19	158	0.1	340	20.2	3400	3347	G	4.17	25.073400	86.688545	Normal
17-06-2023	09:10:21	158	0.1	350	20.2	3500	3467	G	3.17	25.073215	86.689305	Normal
17-06-2023	09:11:07	158	0.1	360	10.1	3500	3438	G	3.33	25.073031	86.690064	Curve
17-06-2023	09:13:38	158	0.1	380	10.1	3500	3457	G	3.63	25.072846	86.690824	Normal
17-06-2023	09:14:16	158	0.1	320	10.1	3200	3155	G	3.83	25.072662	86.691583	Normal
17-06-2023	09:15:12	158	0.1	320	10.1	3200	3175	G	3.37	25.072477	86.692343	Normal
17-06-2023	09:16:30	158	0.1	370	30.3	3700	3681	G	3.09	25.072292	86.693103	Normal
17-06-2023	09:17:23	158	0.1	370	20.2	3300	3296	G	3.38	25.072108	86.693862	Normal
17-06-2023	09:18:24	158	0.1	320	20.2	3200	3129	G	3.37	25.071923	86.694622	Normal
17-06-2023	09:19:31	158	0.1	380	20.2	3800	3540	G	3.39	25.071695	86.695031	Normal

Sumit
20/06/23
A/E

Pitkm
20/06/23
A/E


25/6/23

Name of Customer: Prince Construction
 Name of Work/ Road: Chhatra To Khajuri
 Lab Job number: 158
 Date: 17-06-2023
 Section No.: 158

Test Date: 17-06-2023
 Machine No.: 407
 Start S No.: 1st
 Start E No.: Khajuri
 Weather:
 Start Location: 487556283545
 End Location: 789524322588
 Road Name: Chhatra To Khajuri
 Road Type: (R) RURAL ROAD
 Side:
 UIV Range: 1353 To 5000 Interval 1000 mm/km
 Dist Range: 0 To 31 0.1 ~ 1000 m
 Equation: test

Print Generate Report and Graph Redraw Graph Map View

File: G:\Banka 19-06-2023\42316511.Xls, Section No.: 158, Egn test
 Name of Customer: Prince Construction, Name of Work/ Road: Chhatra To Khajuri, Lab Job number: 158

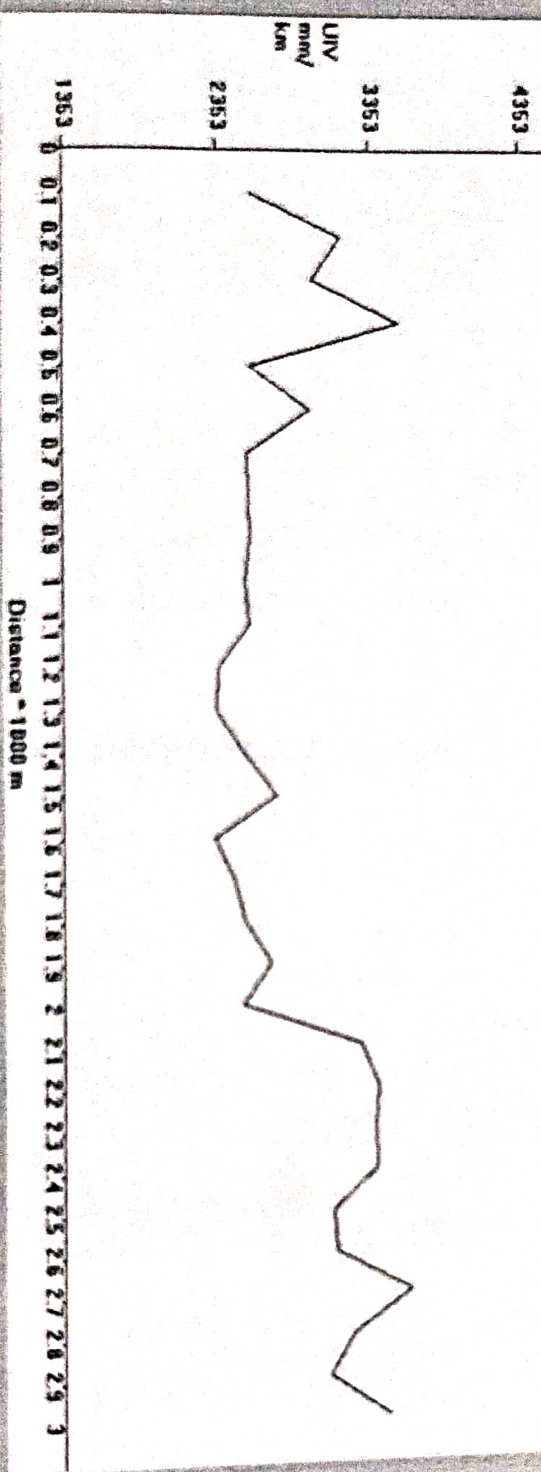


Samir
 20/06/23
 A.C

Pritham
 20/06/23
 A.C

20/06/23

File :G:\Banka 19-06-2023\42316511.Xls. Section No.:168, Eqn :est

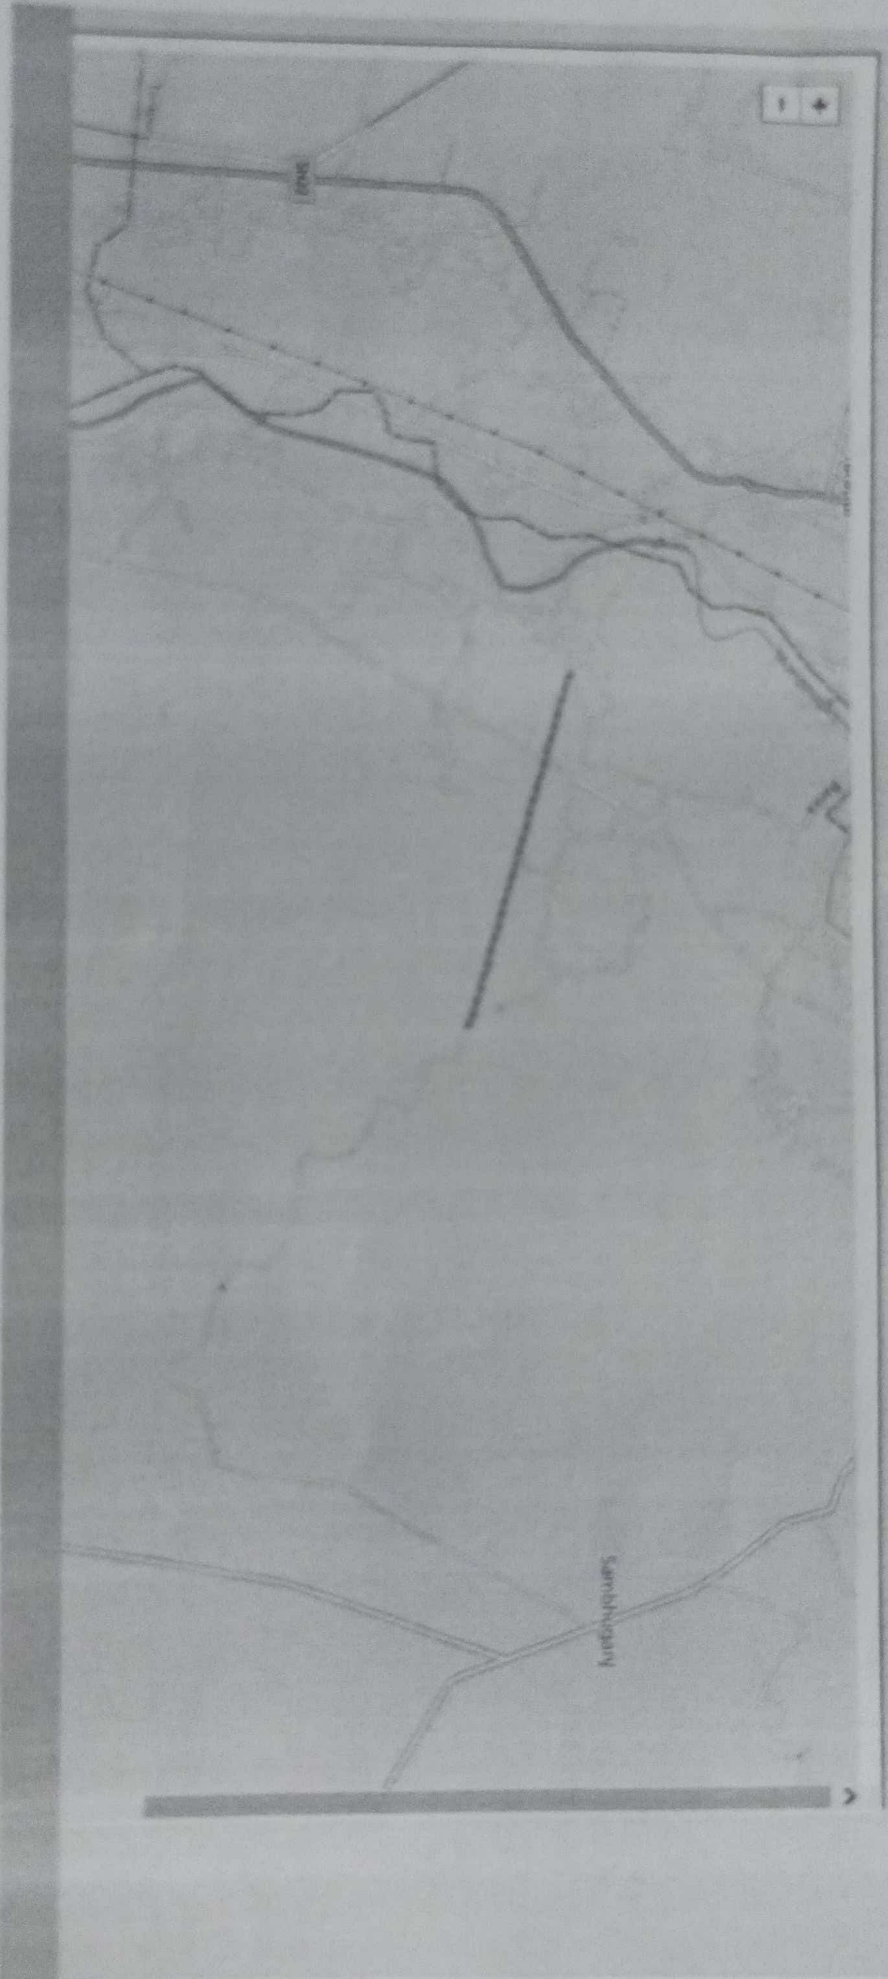

Samir
20/06/23
J.F

Priya
20.06.23
ME

20/06/23

Requisition Format for Scheme Read- MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Government of Bihar
 OM01
 Rural works Department

Name of Works Division:- BANKA-1
 SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Chhathar to Khajuri
 Length of Road - 3.000 KM
 Period: From - 4th Quarter
 Inspector - A.E RWD Sub Division, Belhar

To: Executive Engineer
 RWD Works Division, Banka-1
 Position: AE
 Date -

Standard Work item			Work	Units of work required in each kilometre										Comments
S. No.	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m2	NIL	NIL	NIL									
OM102	Surface Depression and Rut Patching	m2	NIL	NIL	NIL									
OM103	Crack Sealing	Lm	NIL	NIL	NIL									
OM104	Surface Treatment	m2	NIL	NIL	NIL									
	(a) Loss of Azorgse (Surface Ravelling)	m2	NIL	NIL	NIL									
	(b) Bleeding/Fanhing	m2	NIL	NIL	NIL									
	(c) Crocodile Cracking	m2	NIL	NIL	NIL									
OM105	Edge Repair	m2	NIL	NIL	NIL									
OM106	Digouts	m2	NIL	NIL	NIL									
OM107	Concrete Pavement	m2	NIL	NIL	NIL									
	Other activit	Lm	NIL	NIL	NIL									
	OM200 Shoulder		NIL	NIL	NIL									
OM201	Unscaled Shoulder	No	NIL	NIL	NIL									
	(a) Edge Drop off	Lm	NIL	NIL	NIL									
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL									
	(c) Holding Water	Lm	NIL	NIL	NIL									
OM202	Embankment Repair	No	NIL	NIL	NIL									
	Other Activite (Raincut)		NIL	NIL	NIL									

