

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक- 1104(अनु०)

दिनांक- 14/06/2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण
नीति 2018" योजनान्तर्गत पथ:-

1. SIKTA - BHERIHARWA

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना
विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल नरकटियागंज



Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

SL No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WENAR/22-0006	SIKTA - BHERIHARWA	3160001127	105 03.06.2022	5.100	309.83000	190.86021	10.24455	6322/23 20.03.2023	19.12.2023		2478	100% - 25mm	5%	0.00000	0.00000	190.86021	Surface Complete


Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

19/12/2023

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- SIKTA - BHERIHARWA

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Deepak Kumar


Length of Road :- 5.100 KM

Project ID :- 31808902127


Package No. :- RM/WE/NAR/22/0036

Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


JE

Certified that all item wise 50% measurement has been verified by me


AE

Certified that all item wise 10% measurement has been verified by me


EE

Name of Road - SIKTA - BHERIHARWA (Sec-99)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
13/ 6/ 23	15: 29: 9	99	0.1	270	20.2	2700	2745	G	26.99361	84.740538	Normal
13/ 6/ 23	15: 30: 0	99	0.1	220	20.2	2200	2235	G	26.9931	84.741347	Normal
13/ 6/ 23	15: 30: 16	99	0.1	220	10.1	2200	2256	G	26.99266	84.742305	Normal
13/ 6/ 23	15: 30: 51	99	0.1	240	10.1	2400	2460	G	26.99241	84.743315	Normal
13/ 6/ 23	15: 31: 0	99	0.1	250	20.2	2500	2520	G	26.99218	84.744258	Normal
13/ 6/ 23	15: 31: 26	99	0.1	300	20.2	3000	3031	G	26.99196	84.745268	Normal
13/ 6/ 23	15: 31: 26	99	0.1	300	20.2	3000	3031	G	26.99175	84.746245	Normal
13/ 6/ 23	15: 32: 2	99	0.1	290	20.2	2900	2929	G	26.99153	84.747238	Normal
13/ 6/ 23	15: 32: 37	99	0.1	240	20.2	2400	2481	G	26.99129	84.748265	Normal
13/ 6/ 23	15: 33: 12	99	0.1	210	20.2	2100	2115	G	26.99109	84.749208	Normal
13/ 6/ 23	15: 33: 12	99	0.1	200	20.2	2000	2052	G	26.99087	84.750202	Normal
13/ 6/ 23	15: 33: 47	99	0.1	290	20.2	2900	2950	G	26.99067	84.751195	Normal
13/ 6/ 23	15: 40: 0	99	0.1	270	20.2	2700	2745	G	26.99048	84.752188	Normal
13/ 6/ 23	15: 40: 14	99	0.1	210	20.2	2100	2133	G	26.99019	84.753147	Normal
13/ 6/ 23	15: 43: 11	99	0.1	240	20.2	2400	2439	G	26.99001	84.75409	Normal
13/ 6/ 23	15: 43: 11	99	0.1	280	20.2	2800	2848	G	26.98974	84.75507	Normal
13/ 6/ 23	15: 43: 46	99	0.1	290	20.2	2900	2950	G	26.98944	84.75601	Normal
13/ 6/ 23	15: 44: 0	99	0.1	250	20.2	2500	2541	G	26.98915	84.756918	Normal
13/ 6/ 23	15: 44: 0	99	0.1	290	20.2	2900	2929	G	26.98884	84.757912	Normal
13/ 6/ 23	15: 44: 21	99	0.1	220	10.1	2200	2256	G	26.98852	84.758905	Normal
13/ 6/ 23	15: 44: 21	99	0.1	260	10.1	2600	2664	G	26.98823	84.759865	Normal
13/ 6/ 23	15: 44: 21	99	0.1	240	20.2	2400	2460	G	26.98792	84.760773	Normal
13/ 6/ 23	15: 45: 11	99	0.1	290	20.2	2900	2950	G	26.99146	84.74739	Normal
13/ 6/ 23	15: 45: 11	99	0.1	290	21.3	2900	2950	G	26.99167	84.746397	Normal
13/ 6/ 23	15: 45: 11	99	0.1	260	22.6	2600	2635	G	26.96741	84.741003	Normal
13/ 6/ 23	15: 45: 11	99	0.1	320	25.1	3200	3256	G	26.96795	84.74182	Normal
13/ 6/ 23	15: 46: 18	99	0.1	230	20.2	2300	2376	G	26.96873	84.74234	Normal
13/ 6/ 23	15: 46: 18	99	0.1	220	20.1	2200	2274	G	26.96954	84.742464	Normal
13/ 6/ 23	15: 46: 18	99	0.1	230	20.2	2300	2376	G	26.97041	84.742671	Normal
13/ 6/ 23	15: 46: 18	99	0.1	220	20.2	2200	2274	G	26.97128	84.742917	Normal

14/6/23
P.C.

Name of Road - SIKTA - BHERIHARWA (Sec-99)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
13/6/23	15:48:7	99	0.1	210	20.2	2100	2172	G	26.97201	84.743497	Normal
13/6/23	15:48:7	99	0.1	210	20.2	2100	2172	G	26.97288	84.743755	Normal
13/6/23	15:48:7	99	0.1	230	20.2	2300	2370	G	26.97378	84.743821	Normal
13/6/23	15:48:7	99	0.1	220	20.2	2200	2274	G	26.97467	84.743922	Normal
13/6/23	15:49:23	99	0.1	210	20.4	2100	2170	G	26.97556	84.744065	Normal
13/6/23	15:49:23	99	0.1	220	20.3	2200	2274	G	26.97643	84.744326	Normal
13/6/23	15:49:23	99	0.1	250	20.3	2500	2596	G	26.97729	84.744596	Normal
13/6/23	15:49:23	99	0.1	220	20.3	2200	2274	G	26.97817	84.744818	Normal
13/6/23	15:50:21	99	0.1	220	20.2	2200	2274	G	26.97905	84.744615	Normal
13/6/23	15:50:21	99	0.1	210	20.2	2100	2156	G	26.97994	84.74457	Normal
13/6/23	15:50:21	99	0.1	210	20.2	2100	2172	G	26.98084	84.744559	Normal
13/6/23	15:50:21	99	0.1	230	20.2	2300	2376	G	26.98174	84.74458	Normal
13/6/23	15:51:11	99	0.1	240	20.2	2400	2421	G	26.98262	84.744776	Normal
13/6/23	15:51:11	99	0.1	230	20.2	2300	2356	G	26.98344	84.745175	Normal
13/6/23	15:51:11	99	0.1	250	20.2	2500	2531	G	26.98422	84.745659	Normal
13/6/23	15:51:11	99	0.1	210	20.2	2100	2162	G	26.98505	84.746047	Normal
13/6/23	15:52:19	99	0.1	230	20.2	2300	2352	G	26.98595	84.746087	Normal
13/6/23	15:52:28	99	0.1	250	20.2	2500	2536	G	26.98681	84.746301	Normal
13/6/23	15:52:41	99	0.1	230	20.2	2300	2362	G	26.98764	84.746661	Normal
13/6/23	15:52:52	99	0.1	230	20.2	2300	2365	G	26.98843	84.747147	Normal
13/6/23	15:53:9	99	0.1	210	20.2	2100	2162	G	26.98923	84.747539	Normal
Average IRI Value=							2478				

14/6/23
JG

14/06/23
AE

Executive Engineer
Kural Works Department
Works Division, Narkattiyaga
14/6/23

Name of Customer : Deepak Kumar
 Name of Work/ Road : SIKTA - BHERIHARWA
 Lab Job number :
 Date : 13-06-2023
 Section No. : 99

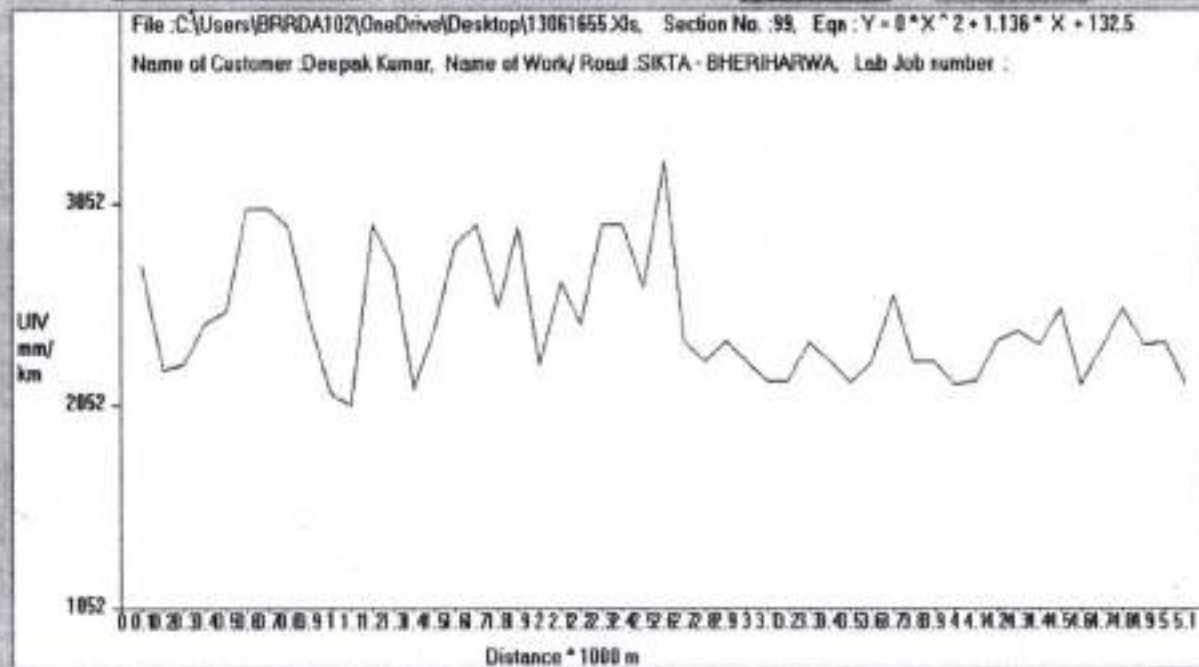
Test Date : 13-06-2023 Road Name : SIKTA - BHERIHARWA
 Machine No : 402 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UV Range : 1052 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 5.2 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View



14/06/2023
 2.0

14/06/23
 AE

Executive Engineer
 Rural Works Department
 Works Division, Narsatiyaga
