

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिमरी बख्तियारपुर।

Email ID :- ee.simribakhtiyarpur@gmail.com (Mob-8986915464)

पत्रांक.....595/3736
प्रेषक,

सिमरी बख्तियारपुर, दिनांक- 15/03/2023

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल सिमरी बख्तियारपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक मु०अ०-4 (मु०) 3054-04-229/229/2021- 2021- 1135 अनु०, दिनांक 09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054(New Maintenance Policy 2018) के अन्तर्गत (RM/SA/SIM/0007)

1. "Sakhori - Tulsipur" (RM/SA/SIM/0001) 1. "Dumar Sonbarsa Road - Sirahi" 2. "Dumra to Lagma via Baltora Ghat Tariyama" 3. "Biratpur - Soha" पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए०टी०आर० लंबित नहीं है।

अनु० :- यथोक्त।

विश्वासभाजन,

15/03/23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिमरी बख्तियारपुर।
15.03.2023

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtiyarpur 2nd Quarter (19-03-2021 to 18-06-2021)

1	Name of the Road	Biratpur - Soha		
2	Batch No / Package no	Rm/SA/Sim/19/0001		
3	Project ID	20904302025		
4	Total Length of Road (in Km)	4.606 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	4.606 km		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	46.81990 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.34100 Lakh		
Compliance ceriteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non - Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.34100

Maa Jwala Enterprises

Date of inspection by E / I his agent prepared by Contractor's self Control unit

RAM KUMAR.
Name and Designation of person inspecting road

Signature of person inspecting road

Certify by E / I [signature] Date:-

Government of Bihar OM01 Rural Works Department			ORDINARY MAINTENANCE INSPECTION REPORT Form OM01										
Road From: Bihatpur - Soha Length of Road: 4.606 km Period: 2nd Quarter (19-03-2021 to 18-06-2021) Inspector: J.E. RWD, Sub Division Sonbaria			To: EXECUTIVE ENGINEER, RWD, Works Division, Simri Bakhtiyarpur Position: J.E.										
Standard work item			Unit of work required in each kilometre										
No.	Name	Work Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil						No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil						No Surface Depression and Rut Patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil						No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate	m2	Nil	Nil	Nil	Nil	Nil						No Loss of Aggregate (Surface)
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil						No Bleeding/Flushing required.
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil						No Crocodile cracking found.
OM106	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil						No Edge Repair required.
OM108	Digouts	m2	N.A.	N.A.	N.A.	N.A.	N.A.						
OM107	Concrete Pavement	m3	N.A.	N.A.	N.A.	N.A.	N.A.						
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-Off	Lm	Nil	Nil	Nil	Nil	Nil						No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil						No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil						No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil	Nil	Nil	Nil						No Embankment Repair required.
	Other activities												
OM 300	Drainage including culverts major and minor br												
OM301	Surface Drains & Verges	Lm	N.A.	N.A.	N.A.	N.A.	N.A.						Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil	Nil						Not required.
OM303	Culvert and Pile Repair	m3	Nil	Nil	Nil	Nil	Nil						Not required.
	Other activities	m2	Nil	Nil	Nil	Nil	Nil						

Maa Jwala Enterprises
 Bidder
 23/11/22
 Proprietor

23/11/22
 Executive Engineer, Work Division

Standard work item			Work Units	Units of work required in each kilometre										Comments
No.	Name			1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation														
Grass Control														
OM401	a) Roadside - General Tidy		Ha	Nil	Nil	Nil	Nil	Nil						Not required
	b) Clear near safety signs, kilometre posts and roadside furniture		Ha	Nil	Nil	Nil	Nil	Nil						Not required
OM402	Tree and Shrub Management													
	Cutting Tree		No	Nil	Nil	Nil	Nil	Nil						Not required
	Cutting Shrubs		No	Nil	Nil	Nil	Nil	Nil						Not required
	Other activities													
OM500 Safety Signage and Road														
OM501	Signs Maintenance		No	Nil	Nil	Nil	Nil	Nil						Not required
OM502	Guard stones		Lm	N.A	N.A	N.A	N.A	N.A						Not required
OM503	Distance stones		No	N.A	N.A	N.A	N.A	N.A						Not required
OM504	Road markings		m2	Nil	Nil	Nil	Nil	Nil						Not required
	Other activities													

Waa Joon Enterprises

26/01/2022

Signature of Contractor/ Authorized representative

Time

Place

Maa Juma Enterprises

Director

[Signature]

Signature of Contractor/ Authorized representative

Date Time Place

Name of work : Biratpur - Soha

Name of customer : MAA JAWALA ENTERPRISES

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMF(cm)	Speed(Km/Hr)	U/mn/Km	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
08/02/23	19:02:43	110	0	0	0.0 cm	27.3 Km/Hr	0.0 mm/Km	88	0.17	Good	25.7261190	N	86.8023158	E	Normal
08/02/23	19:32:09	110	100	100	31.0 cm	25.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7331552	N	86.7531443	E	Normal
08/02/23	19:32:37	110	100	200	16.0 cm	12.8 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7338991	N	86.7541971	E	Normal
08/02/23	19:32:58	110	100	300	15.0 cm	15.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7348070	N	86.7547235	E	Normal
08/02/23	19:33:23	110	100	400	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2610	3.56	Good	25.7348070	N	86.7547235	E	Normal
08/02/23	19:33:35	110	100	500	17.0 cm	28.8 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7364588	N	86.7547541	E	Normal
08/02/23	19:33:45	110	100	600	15.0 cm	37.0 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7375612	N	86.7549829	E	Normal
08/02/23	19:34:04	110	100	700	18.0 cm	19.6 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7380953	N	86.7554712	E	Normal
08/02/23	19:34:23	110	100	800	31.0 cm	19.2 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7384825	N	86.7559061	E	Normal
08/02/23	19:34:36	110	100	900	16.0 cm	28.2 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7389326	N	86.7558298	E	Normal
08/02/23	19:34:50	110	100	1000	14.0 cm	25.9 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7401781	N	86.7551432	E	Normal
08/02/23	19:35:11	110	100	1100	20.0 cm	17.0 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7410574	N	86.7549829	E	Normal
08/02/23	19:35:29	110	100	1200	16.0 cm	20.0 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7412443	N	86.7549295	E	Normal
08/02/23	19:35:50	110	100	1300	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.7427587	N	86.7545099	E	Normal
08/02/23	19:36:03	110	100	1400	21.0 cm	25.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7432222	N	86.7546549	E	Normal
08/02/23	19:36:18	110	100	1500	10.0 cm	24.1 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7432222	N	86.7546549	E	Normal
08/02/23	19:36:49	110	100	1600	31.0 cm	25.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7446413	N	86.7558955	E	Normal
08/02/23	19:37:00	110	100	1700	9.0 cm	32.7 Km/Hr	900.0 mm/Km	929	1.41	Good	25.7458143	N	86.7562799	E	Normal
08/02/23	19:37:12	110	100	1800	10.0 cm	30.0 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7458467	N	86.7569056	E	Normal
08/02/23	19:37:20	110	100	1900	25.0 cm	41.8 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.7458754	N	86.7575541	E	Normal
08/02/23	19:37:31	110	101	2001	10.0 cm	35.4 Km/Hr	990.0 mm/Km	1013	1.53	Good	25.7459726	N	86.7589655	E	Normal

MAA JAWALA ENTERPRISES
15/03/2023
ASL

15/03/2023

15/3/23
66

Name of work : Biratpur - Soha

Name of customer : MAA JAWALA ENTERPRISES

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

08/02/23	19:37:41	110	100	2101	12.0 cm	36.4 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7468386	N	86.7593622	E	Normal
08/02/23	19:37:49	110	100	2201	7.0 cm	42.4 Km/Hr	700.0 mm/Km	742	1.16	Good	25.7473593	N	86.7597361	E	Normal
08/02/23	19:38:03	110	100	2301	31.0 cm	25.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7484026	N	86.7603540	E	Normal
08/02/23	19:38:13	110	100	2401	20.0 cm	32.7 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7484026	N	86.7603540	E	Normal
08/02/23	19:38:22	110	100	2501	9.0 cm	40.9 Km/Hr	900.0 mm/Km	929	1.41	Good	25.7500296	N	86.7608118	E	Normal
08/02/23	19:38:37	110	100	2601	31.0 cm	25.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7511816	N	86.7614298	E	Normal
08/02/23	19:38:49	110	100	2701	14.0 cm	29.1 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7520227	N	86.7616892	E	Normal
08/02/23	19:38:59	110	100	2801	11.0 cm	34.8 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7528216	N	86.7617884	E	Normal
08/02/23	19:39:27	110	100	2901	12.0 cm	13.1 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7537775	N	86.7618952	E	Normal
08/02/23	19:39:54	110	100	3001	20.0 cm	12.4 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7543840	N	86.7622232	E	Normal
08/02/23	19:40:09	110	100	3101	20.0 cm	23.1 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7545996	N	86.7625971	E	Normal
08/02/23	19:40:19	110	100	3201	11.0 cm	39.1 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7556887	N	86.7636270	E	Normal
08/02/23	19:40:27	110	100	3301	19.0 cm	43.2 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7563372	N	86.7636881	E	Normal
08/02/23	19:40:47	110	100	3401	14.0 cm	18.0 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7577772	N	86.7637033	E	Normal
08/02/23	19:41:01	110	100	3501	7.0 cm	24.6 Km/Hr	700.0 mm/Km	742	1.16	Good	25.7580080	N	86.7637033	E	Normal
08/02/23	19:41:10	110	100	3601	9.0 cm	37.4 Km/Hr	900.0 mm/Km	929	1.41	Good	25.7580080	N	86.7637033	E	Normal
08/02/23	19:41:19	110	100	3701	12.0 cm	40.3 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7599745	N	86.7640924	E	Normal
08/02/23	19:41:47	110	100	3801	17.0 cm	13.8 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7612200	N	86.7638712	E	Normal
08/02/23	19:42:08	110	100	3901	11.0 cm	15.0 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7616625	N	86.7639017	E	Normal
08/02/23	19:42:19	110	100	4001	8.0 cm	33.3 Km/Hr	800.0 mm/Km	836	1.29	Good	25.7616625	N	86.7639017	E	Normal
08/02/23	19:42:28	110	100	4101	14.0 cm	37.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7628546	N	86.7654963	E	Normal
08/02/23	19:42:37	110	100	4201	18.0 cm	41.4 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7638483	N	86.7659006	E	Normal

15/03/2023

15/03/23

15/3/23

;	Biratpur - Soha
---	-----------------

MAA JAWALA ENTERPRISES

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


				≤ 4000											
08/02/23	19.42.48	110	100	4301	5.0 cm	35.2 Km/Hr	500.0 mm/Km	555	0.89	Good	25.7647924	N	86.7661142	E	Normal
08/02/23	19.43.17	110	100	4401	15.0 cm	12.1 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7654104	N	86.7654810	E	Normal
08/02/23	19.44.11	110	100	4501	20.0 cm	17.0 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7610574	N	86.7649829	E	Normal
08/02/23	19.45.29	110	100	4601	16.0 cm	20.0 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7612443	N	86.7649295	E	Normal

15.03.2023

15/03/23

22/5/15

Name of Customer: MAA JAWALA ENTERPRISES, Machine no: 19215, Road: Biralpur - Soha, Date: 15/03/23, Section No: 110, Equation: $Y=0.930X+08.4$

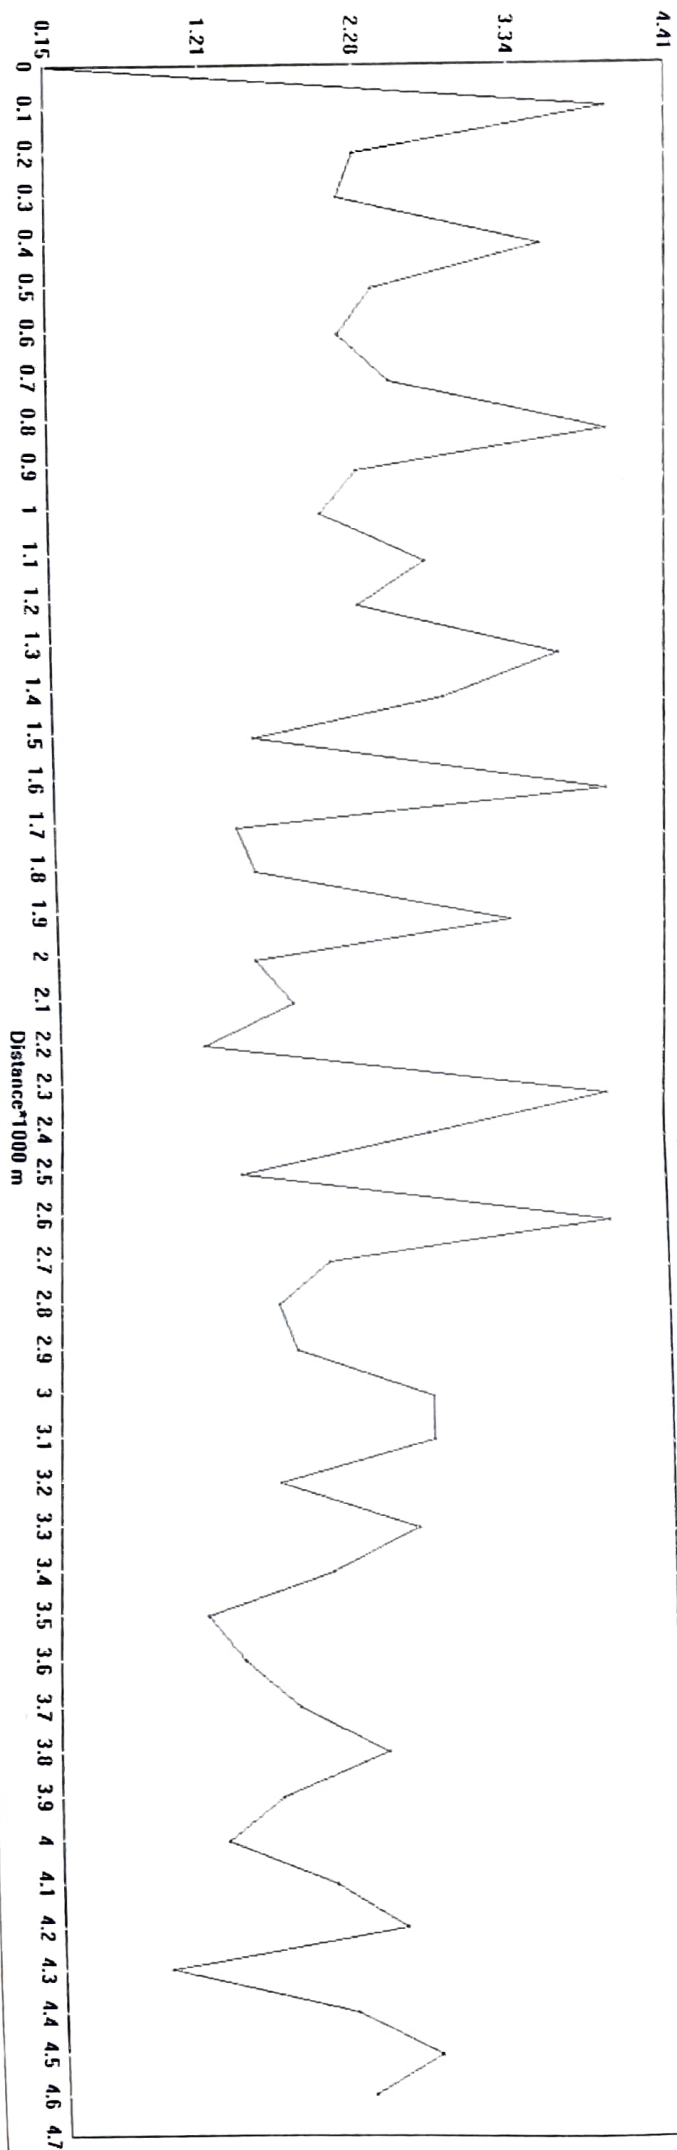

15/03/23

15/03/23

15/3/23
