

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिमरी बख्तियारपुर।

Email ID :- ee.simribakhtiyarpur@gmail.com (Mob-8986915464)

पत्रांक 595/3736
प्रेषक,

सिमरी बख्तियारपुर, दिनांक- 15/03/2023

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल सिमरी बख्तियारपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक मु०अ०-4 (मु०) 3054-04-229/229/2021- 2021- 1135 अनु०, दिनांक 09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054(New Maintenance Policy 2018) के अन्तर्गत (RM/SA/SIM/0007)

1. "Sakhori - Tulsipur" (RM/SA/SIM/0001) 1. "Dumar Sonbarsa Road - Sirahi" 2. "Dumra to Lagma via Baltora Ghat Tariyama" 3. "Biratpur - Soha" पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए०टी०आर० लंबित नहीं है।

अनु० :- यथोक्त।

विश्वासभाजन,

15/03/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिमरी बख्तियारपुर।
15.03.2023

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtigar Pur 2nd Quarter (13-06-2021 to 12-09-2021)

1	Name of the Road	Dumra to Lagma via Baltora Chhat Tariyama		
2	Batch No / Package no	Rm/SA/Sim/15/0001		
3	Project ID	20904301010		
4	Total Length of Road (in Km)	1.500 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	1.500 km		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	16.68355 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.83418 Lakh		
Compliance criteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY,	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.83418

Maa Jwala Enterprises

Date of inspection by E / I his agent prepared by
Contractor's self Control unit

RAM KUMAR.
Name and Designation of person inspecting
road
Signature of person inspecting road

Certify by E / I [signature] Date:-

ORDINARY MAINTENANCE INSPECTION REPORT

Form OM01

Government of Bihar

OM01

Rural Works Department

Road From: Dumra to Lagma via Bultara Chhat Tarigum

Length of Road: 1.500 km

Period: 2nd Quarter (13-06-2021 to 12-09-2021)

Inspector: J.E., RWD, Sub Division Sonbaria

Date:

To: EXECUTIVE ENGINEER,
RWD, Works Division, Simri Bakhtiyarpur
Position: J.E.

No.	Standard work item	Work Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil									No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil									No Surface Depression and Rut Patching found.
OM103	Crack Sealing	Lm	Nil	Nil									No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate	m2	Nil	Nil									No Loss of Aggregate (Surface)
	(b) Bleeding/Flushing	m2	Nil	Nil									No Bleeding/Flushing required.
	(c) Crocodile Cracking	m2	Nil	Nil									No Crocodile cracking found.
OM105	Edge Repair	m2	Nil	Nil									No Edge Repair required.
OM106	Digouts	m2	N.A	N.A									
OM107	Concrete Pavement	m3	N.A	N.A									
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-Off	Lm	Nil	Nil									No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil									No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil									No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil									No Embankment Repair required.
	Other activities												
OM300	Drainage including culverts major and minor br												
OM301	Surface Drains & Verge	Lm	N.A	N.A									Not required.
OM302	Culvert Cleaning	No.	Nil	Nil									Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil									Not required.
	Other activities	m2	Nil	Nil									

[Signature]
29/11/21

Maa Jwala Enterprises

2/12/21 to 5/12/21

Bidder

Proprietor

Executive Engineer, Work Division

Standard work item		Work	Units of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
Grass Control													
OM401	a) Roadside - General Tidy	Ha	Nil	Nil									Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil									Not required
Tree and Shrub Management													
OM402	Cutting Tree	No	Nil	Nil									Not required
	Cutting Shrubs	No	Nil	Nil									Not required
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil									Not required
OM502	Guard stones	Lm	N.A	N.A									Not required
OM503	Distance stones	No	N.A	N.A									Not required
OM504	Road markings	m2	Nil	Nil									Not required
	Other activities												

Maa Jwala Enterprises
b/c 24-5 E m r

Signature of Contractor/ Authorized representative

Date

Time

Place

Maa Jwala Enterprises

by Mr

[Signature of Contractor/ Authorized representative]

Signature

Date

Time

Place

Name of work : Dumra to Lagma via Bailora Ghat Tanyama

Name of customer : MAA JAWALA ENTERPRISES

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BURR(cm)	Speed(Km/Hr)	Ultimate(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction I	Remarks
06/02/23	21:12:44	112	0	0	0.0 cm	21.5 Km/Hr	0.0 mm/Km	88	0.17	Good	25.7511282	N	86.6865040	E	Normal
06/02/23	21:17:36	112	100	100	10.0 cm	9.5 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7593832	N	86.6822250	E	Normal
06/02/23	21:17:42	112	100	200	9.0 cm	22.0 Km/Hr	900.0 mm/Km	929	1.41	Good	25.7593832	N	86.6822250	E	Normal
06/02/23	21:18:16	112	100	300	25.0 cm	15.7 Km/Hr	2500.0 mm/Km	2423	3.33	Good	25.7587576	N	86.6813288	E	Normal
06/02/23	21:18:31	112	100	400	13.0 cm	24.0 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:18:43	112	100	500	12.0 cm	30.6 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:19:03	112	100	600	15.0 cm	17.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:19:16	112	100	700	15.0 cm	26.1 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:19:28	112	100	800	14.0 cm	31.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:19:43	112	100	900	10.0 cm	24.3 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:19:54	112	100	1000	9.0 cm	30.9 Km/Hr	900.0 mm/Km	929	1.41	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:20:11	112	100	1100	24.0 cm	22.6 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:20:27	112	100	1200	15.0 cm	21.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:20:36	112	100	1300	10.0 cm	40.0 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:20:52	112	100	1400	14.0 cm	23.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7588911	N	86.6805048	E	Normal
06/02/23	21:20:52	112	100	1500	24.0 cm	22.6 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.7588911	N	86.6805048	E	Normal

MAA JAWALA ENTERPRISES

15/09/23

15/9/23

Name of Customer: MAA JAWALA ENTERPRISES, Machine no: 19215, Road: Daura to Laguna via Badora Chat Taryama, Date: 15/03/23, Section No: 112, Equation: $Y = 0.934X - 93.4$

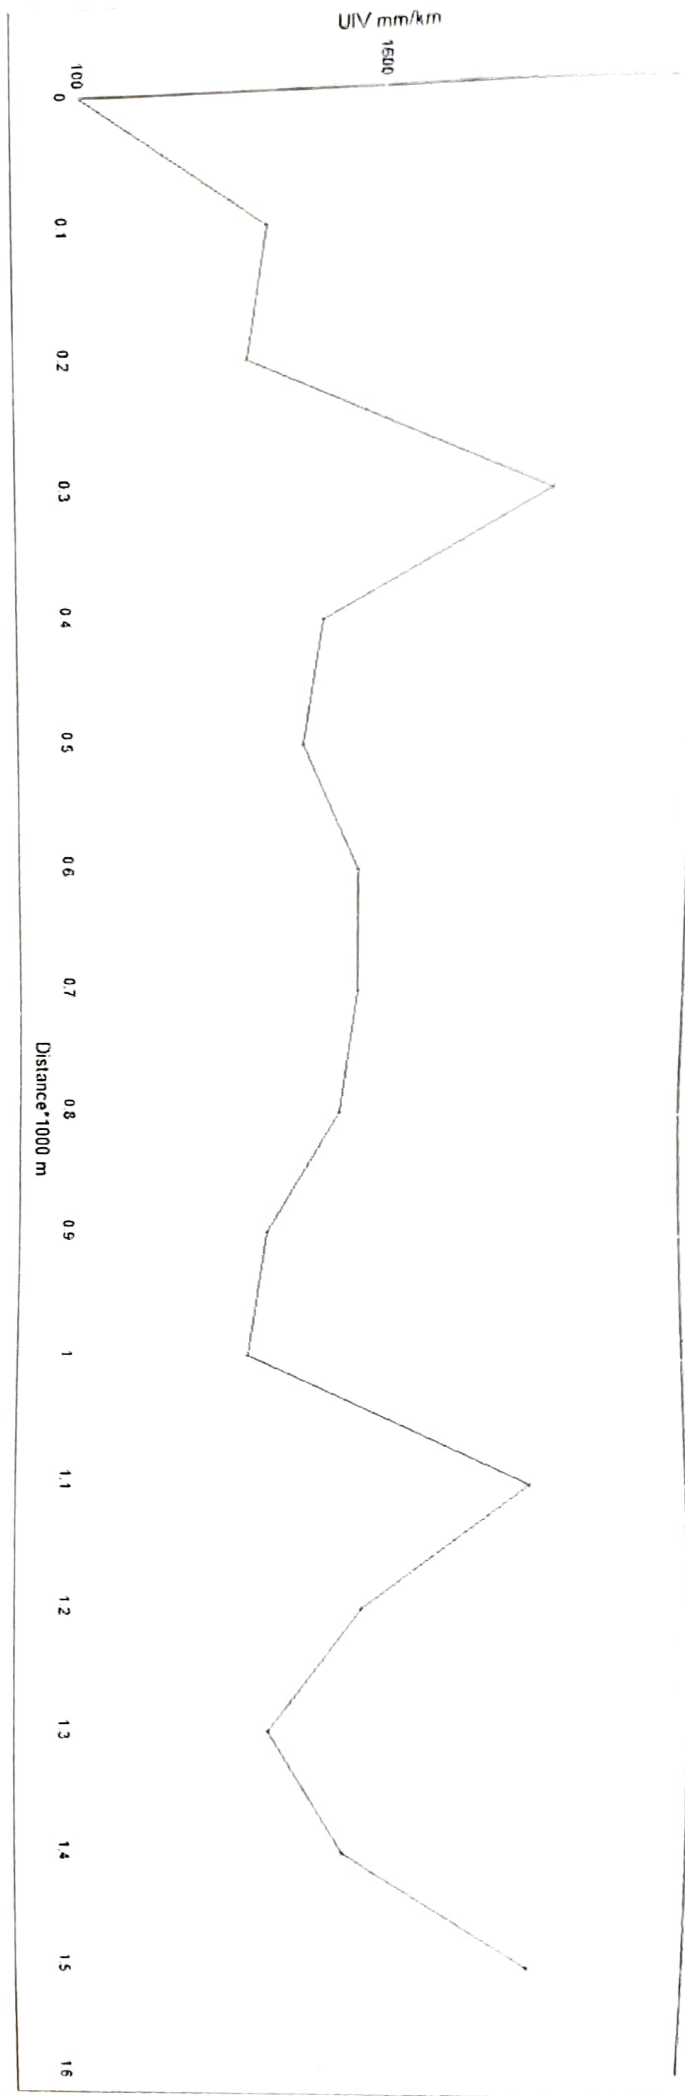

Me
15/03/2023

Ok
15/03/23

80
15/3/23
EC
