

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक- 966

दिनांक- 22/05/2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण
नीति 2018" योजनान्तर्गत पथ:-


1. BETTIAH SE MAINATAND TAK JANE BALI MUKHYA PATH ME
JHUMKA PAKRI MORE SE JHUMKA HOTE HUE SIRISIYA BAZAR
TAK PATH NIRMAN.
2. Rampur L024 to Berwa Barauli (VR74)
3. T02 to Ausanpur (VR39)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना
विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।


विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/22/0037	BETTIAH SE MAINATAND TAK JANE BALI MUKHYA PATH ME JHUMKA PAKRI MORE SE JHUMKA HOTE HUE SIRISIYA BAZAR TAK PATH NIRMAN.	31808901004	105 03.06.2022	4.800	258.20000	176.87014	43.21695	54/22-23 10.02.2023	09.11.2023		2984	SDBC-25mm	5%	46.47115	46.47115	130.39899	Surface Complete
2	RM/WE/NAR/22/0026	Rampur L024 to Berwa Barauli (VR74)	31808902216	105 03.06.2022	2.622	267.04000	204.32939	25.96010	56/22-23 17.02.2023	16.11.2023		2991	SDBC-25mm	5%	89.18862	89.18862	115.14077	Surface Complete
3	RM/WE/NAR/22/0027	T02 to Ausanpur (VR39)	31808902150	105 03.06.2023	2.687	198.21000	152.51486	25.98535	57/22-23 10.02.2024	09.11.2023		2872	SDBC-25mm	5%	42.26928	42.26928	110.24558	Surface Complete


 Executive Engineer
 Rural Works Department
 Work(s) Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road **BETTIAH SE MAINATAND TAK JANE BALI MUKHYA PATH**
 :- ME JHUMKA PAKRI MORE SE JHUMKA HOTE HUE SIRISIYA
 BAZAR TAK

Name of Scheme **:- MR 3054 New Maintenance Policy 2018**

Name of Contractor **:- Khurshid Alam**

Length of Road **:- 4.800 KM**

Project ID **:- 31808901004**

Package No. **:- RM/WE/NAR/22/0037**

Name of Block **:- Sikta**

Certified that all item wise 100% measurement has been taken by me


JE

Certified that all item wise 50% measurement has been verified by me


AE

Certified that all item wise 10% measurement has been verified by me


EE

**Name of Road - BETTIAH SE MAINATAND TAK JANE BALI MUKHYA PATH ME JHUMKA PAKRI MORE SE JHUMKA HOTE HUE
SIRISIYA BAZAR TAK PATH NIRMAN (Sec-77)**

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
13/3/23	12:7:26	77	0.1	280	0	2800	2793	G	26.999463	84.629898	Normal
13/3/23	12:7:26	77	0.1	270	21.5	2700	2735	G	26.998615	84.62968	Normal
13/3/23	12:8:0	77	0.1	280	21.5	2800	2809	G	26.997897	84.629325	Normal
13/3/23	12:8:2	77	0.1	320	31.6	3200	3209	G	26.99702	84.629057	Normal
13/3/23	12:8:2	77	0.1	290	21.5	2900	2874	G	26.996168	84.628703	Normal
13/3/23	12:8:37	77	0.1	290	21.5	2900	2862	G	26.996263	84.629697	Normal
13/3/23	12:8:37	77	0.1	280	21.5	2800	2770	G	26.996287	84.630638	Normal
13/3/23	12:9:0	77	0.1	340	11.4	3400	3398	G	26.996127	84.631665	Normal
13/3/23	12:9:12	77	0.1	300	21.5	3000	2979	G	26.995893	84.632625	Normal
13/3/23	12:9:47	77	0.1	290	21.5	2900	2874	G	26.995697	84.633585	Normal
13/3/23	12:10:0	77	0.1	350	21.5	3500	3503	G	26.995547	84.634545	Normal
13/3/23	12:10:23	77	0.1	340	11.4	3400	3398	G	26.99526	84.635453	Normal
13/3/23	12:10:23	77	0.1	300	21.5	3000	2979	G	26.994927	84.63643	Normal
13/3/23	12:11:0	77	0.1	290	21.5	2900	2874	G	26.99452	84.637255	Normal
13/3/23	12:11:33	77	0.1	260	24.5	2600	2607	G	26.99418	84.638163	Normal
13/3/23	12:12:0	77	0.1	330	26.4	3300	3293	G	26.993713	84.638972	Normal
13/3/23	12:12:9	77	0.1	260	24.7	2600	2600	G	26.99288	84.639007	Normal
13/3/23	12:13:0	77	0.1	300	24.9	3000	2972	G	26.992582	84.639948	Normal
13/3/23	12:13:19	77	0.1	270	24.4	2700	2705	G	26.992638	84.640925	Normal
13/3/23	12:13:19	77	0.1	330	24.4	3300	3293	G	26.9928	84.641852	Normal
13/3/23	12:14:0	77	0.1	320	31.6	3200	3249	G	26.993313	84.642693	Normal
13/3/23	12:14:30	77	0.1	320	31.6	3200	3247	G	26.99323	84.643635	Normal
13/3/23	12:15:5	77	0.1	290	22.7	2900	2916	G	26.99287	84.644512	Normal
13/3/23	12:15:40	77	0.1	320	31.6	3200	3161	G	26.992193	84.645168	Normal
13/3/23	12:16:0	77	0.1	300	31.6	3000	3033	G	26.991458	84.64547	Normal
13/3/23	12:16:16	77	0.1	300	24.8	3000	3043	G	26.990632	84.645555	Normal
13/3/23	12:17:0	77	0.1	330	24.8	3300	3349	G	26.990177	84.646328	Normal
13/3/23	12:17:25	77	0.1	310	24.8	3100	3061	G	26.989315	84.646515	Normal

Hiy
22/5/2023
J.G.

Shameer
22/5/23
J.G.

High
22/5/23
J.G.

**Name of Road - BETTIAH SE MAINATAND TAK JANE BALI MUKHYA PATH ME JHUMKA PAKRI MORE SE JHUMKA HOTE HUE
SIRISIYA BAZAR TAK PATH NIRMAN (Sec-77)**

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
13/3/23	12:18:0	77	0.1	320	24.8	3200	3187	G	26.988662	84.647188	Normal
13/3/23	12:18:36	77	0.1	320	24.8	3200	3247	G	26.988197	84.648013	Normal
13/3/23	12:19:0	77	0.1	280	31.6	2800	2847	G	26.98783	84.648872	Normal
13/3/23	12:19:11	77	0.1	310	24.8	3100	3062	G	26.987463	84.649763	Normal
13/3/23	12:19:11	77	0.1	270	31.6	2700	2738	G	26.987355	84.650773	Normal
13/3/23	12:20:0	77	0.1	270	21.6	2700	2749	G	26.987598	84.651515	Normal
13/3/23	12:20:21	77	0.1	260	22.6	2600	2645	G	26.98768	84.65239	Normal
13/3/23	12:21:0	77	0.1	240	22.6	2400	2449	G	26.987518	84.65338	Normal
13/3/23	12:21:32	77	0.1	270	22.6	2700	2749	G	26.987563	84.65441	Normal
13/3/23	12:21:32	77	0.1	320	22.6	3200	3247	G	26.98701	84.65512	Normal
13/3/23	12:22:7	77	0.1	280	22.6	2800	2758	G	26.986402	84.655505	Normal
13/3/23	12:22:43	77	0.1	290	22.6	2900	2940	G	26.985485	84.655522	Normal
13/3/23	12:23:0	77	0.1	310	22.6	3100	3145	G	26.984568	84.655555	Normal
13/3/23	12:23:18	77	0.1	310	22.6	3100	3131	G	26.983728	84.655437	Normal
13/3/23	12:23:53	77	0.1	290	22.6	2900	2880	G	26.982837	84.655555	Normal
13/3/23	12:24:0	77	0.1	320	22.6	3200	3187	G	26.98213	84.65606	Normal
13/3/23	12:25:0	77	0.1	290	23.8	2900	2859	G	26.981653	84.656868	Normal
13/3/23	12:25:4	77	0.1	300	23.8	3000	2961	G	26.982065	84.657357	Normal
13/3/23	12:25:39	77	0.1	310	23.8	3100	3085	G	26.982827	84.657895	Normal
13/3/23	12:26:14	77	0.1	280	23.8	2800	2758	G	26.983648	84.658163	Normal
Average IRI Value=							2984				

H/A
22/5/2023
J.G.

Sanam
22/5/23
AE

Prish
22/5/23

Name of Customer : Khurshid Alam
 Name of Work/ Road : BETTIAH SE MAINATAND TAI
 Lab Job number :
 Date : 13-03-2023
 Section No. : 77

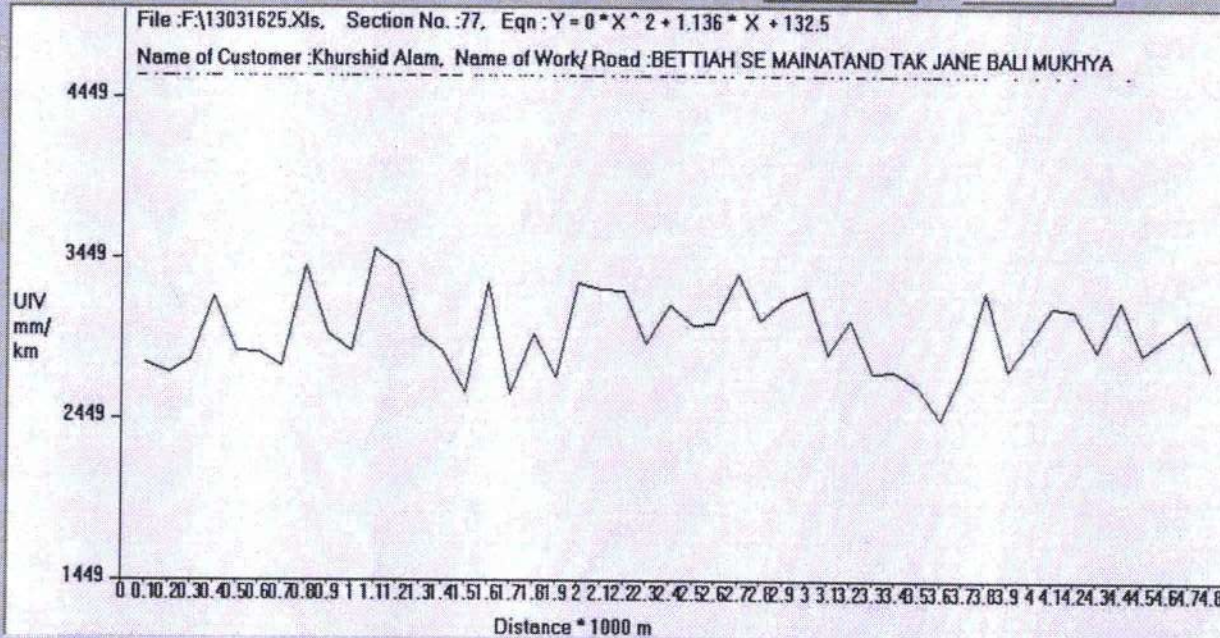
Test Date : 13-03-2023 Road Name : BETTIAH SE MAINATAND TA
 Machine No : 402 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 1449 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 4.9 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View



Hiy
 22/5/2023
 J-G
 E. Amad
 22/5/23
 AC

Quah
 22/5/23
