

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1979(अनु०)

/नरकटियागंज, दिनांक 31/10/2023

प्रेषक,

ई० मुकेश कुमार सिंह,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ:-


1. Done Canal – Serpur
2. BELSANDI PANCHYAT KE BELSANDI SE BAHARWA, SERWA MASJIDWA HOTE HUE MATEARIYA SONBERSA TAK SADAK NIRMAN
3. PWD ROAD - DHAMOURA

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



ई० मुकेश कुमार सिंह

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज

31/10/2023

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/21/0002	Done Canal - Serpur	31808802079	1099 31.03.2021	5.670	253.26500	218.32536	55.56075	27/22-23 23.09.2022	22.06.2023		2824	SDBC-25mm	5%	0.00000	0.00000	130.00000	Surface Complete
2	RM/WE/NAR/21/0002	BELSANDI PANCHYAT KE BELSANDI SE BAHARWA, SERWA MASJIDWA HOTE HUE MATEARIYA SONBERSA TAK SADAK NIRMAN.	31808901008	1099 31.03.2021	8.820	396.22700	292.75988	68.88645	27/22-23 23.09.2022	22.06.2023		2983	SDBC-25mm	5%	0.00000	0.00000	273.64825	Surface Complete
3	RM/WE/NAR/22/0013	PWD ROAD - DHAMOURA	31808802110	105 03.06.2022	1.800	168.62000	132.47557	20.24890	55/22-23 02.02.2023	01.11.2023		2993	SDBC-25mm	5%	0.00000	0.00000	120.00000	Surface Complete

Pranav
31-10-23
JC

Pranav
31.10.23
AE

[Signature]
Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj
[Signature]
21/10/2023

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- PWD ROAD - DHAMOURA

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- RAJAN KUMAR

Length of Road :- 1.800 KM

Project ID :- 31808802110

Package No. :- RM/WE/NAR/22/0013

Name of Block :- Gaunaha

Certified that all item wise 100% measurement has been taken by me

Ruma
31/10/23
JE

Certified that all item wise 50% measurement has been verified by me

Dee
31/10/23
AE

Certified that all item wise 10% measurement has been verified by me

EE *[Signature]*
31/10/23

Name of Road - PWD ROAD - DHAMOURA (Sec-34)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
31/10/23	9:20:6	34	0.1	300	25.2	3000	2976	G	27.25214	84.42099	Normal
31/10/23	9:20:26	34	0.1	290	25.3	2900	2918	G	27.25223	84.42000	Normal
31/10/23	9:20:36	34	0.1	300	25.3	3000	2992	G	27.25202	84.41905	Normal
31/10/23	9:20:46	34	0.1	340	35.4	3400	3392	G	27.25235	84.41818	Normal
31/10/23	9:21:5	34	0.1	310	25.3	3100	3057	G	27.25311	84.41765	Normal
31/10/23	9:21:18	34	0.1	300	25.3	3000	3045	G	27.25385	84.41709	Normal
31/10/23	9:21:27	34	0.1	300	25.3	3000	2953	G	27.25473	84.41692	Normal
31/10/23	9:21:36	34	0.1	300	15.2	3000	3032	G	27.25536	84.41628	Normal
31/10/23	9:21:48	34	0.1	320	25.3	3200	3162	G	27.25582	84.41541	Normal
31/10/23	9:21:57	34	0.1	310	25.3	3100	3057	G	27.25645	84.41468	Normal
31/10/23	9:22:4	34	0.1	270	25.3	2700	2686	G	27.25692	84.41379	Normal
31/10/23	9:22:15	34	0.1	260	15.2	2600	2581	G	27.25695	84.41293	Normal
31/10/23	9:22:26	34	0.1	320	25.3	3200	3162	G	27.25716	84.41197	Normal
31/10/23	9:22:37	34	0.1	310	25.3	3100	3057	G	27.25748	84.41102	Normal
31/10/23	9:22:58	34	0.1	280	28.3	2800	2790	G	27.25837	84.41095	Normal
31/10/23	9:23:9	34	0.1	310	30.2	3100	3076	G	27.25923	84.41060	Normal
31/10/23	9:23:20	34	0.1	280	28.5	2800	2783	G	27.25996	84.41012	Normal
31/10/23	9:23:31	34	0.1	320	28.7	3200	3155	G	27.26065	84.40944	Normal
Average IRI Value=							2993				

Pruman
31-10-23
(J.D)


De
31.10.23
AE

[Signature]
Executive Engineer
Rural Works Department
Work Division, Narkatiyaganj
[Signature]
31/10/2023

Name of Customer : RAJAN KUMAR
Name of Work/ Road : PWD ROAD - DHAMOURA
Lab Job number :
Date : 31-10-2023
Section No. : 34

Test Date : 31-10-2023 Road Name : PWD ROAD - DHAMOURA
Machine No : 402 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1581 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 1.9 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 1.047 * X - 63.36$

Print Generate Report and Graph Redraw Graph Map View

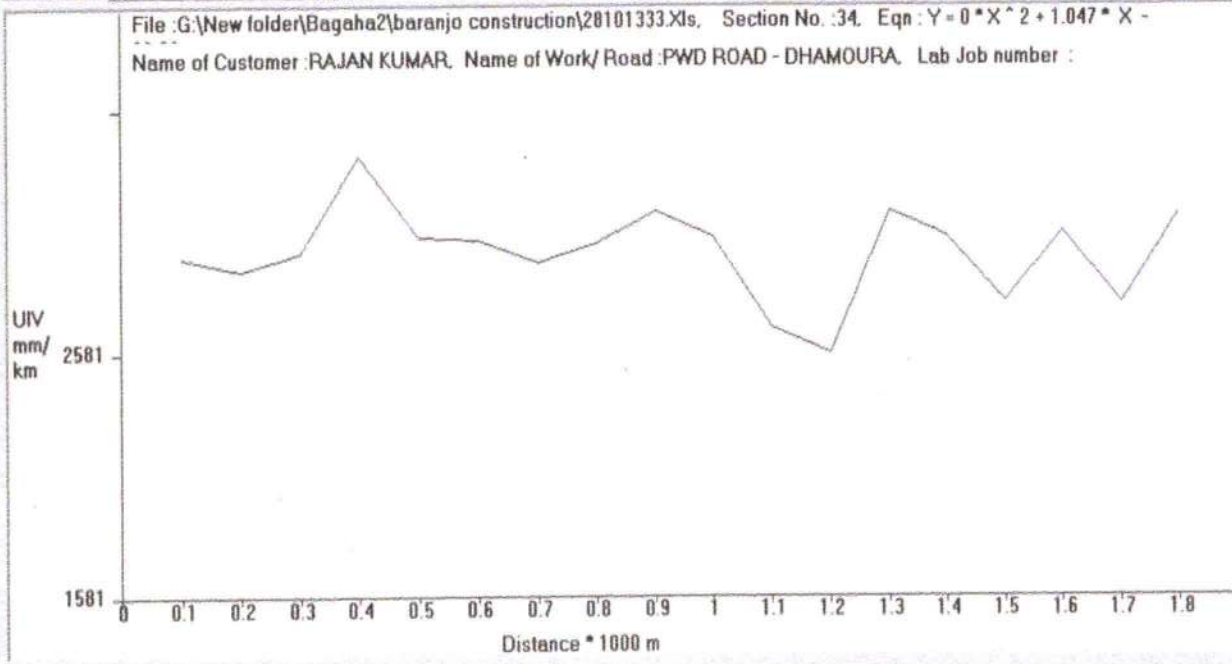

Pruman
31-10-23
(J-E)

Pruman
31.10.23
KE

Executive Engineer
Rural Works Department
Work Division, Narkatiyaganj
31/10/2023
