

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2126.....

/नरकटियागंज, दिनांक 16/11/2023

प्रेषक,

ई0 मुकेश कुमार सिंह,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ:-

1. Hardiya - Majharia
2. REO Road - Mahuabhusa
3. T04 to Poharwa (VR42)
4. Pakri bishauli se amolawa

का कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0:-यथोक्त।

विश्वासभाजस



ई0 मुकेश कुमार सिंह
कार्यपालक अभियन्ता

ग्रा0का0वि0, का0प्र0 नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/22/0004	Hardiya - Majharia	31808802083	1419 26.03.2022	1.910	76.35000	64.48073	20.30635	49/22-23 29.11.2022	28.08.2023	19/8/2023	2902	SDBC-25mm	5%	63.94765	63.94765	0.19631	Complete
2	RM/WE/NAR/22/0004	REO Road - Mahuabhusa	31808802114	1419 26.03.2022	2.550	181.62000	172.89371	25.77805	49/22-23 29.11.2022	28.08.2023	25/10/2023	2982	SDBC-25mm	5%	150.43256	150.43256	4.07061	Complete
3	RM/WE/NAR/22/0004	Pakri bishauli se amolawa	31808908056	1419 26.03.2022	3.500	179.72000	163.08491	35.60055	49/22-23 29.11.2022	28.08.2023	12/9/2023	2849	SDBC-25mm	5%	116.05464	116.05464	41.78751	Complete
4	RM/WE/NAR/22/0004	T04 to Poharwa (VR42)	31808902154	1419 26.03.2022	3.200	139.08000	112.91129	35.93600	49/22-23 29.11.2022	28.08.2023	25/10/2023	2880	SDBC-25mm	5%	96.84085	96.84085	13.95737	Complete

Pruman
16-11-2023
J. B

16.11.23
AE

Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Pakri bishauli se amolawa

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Sg Piling And Construction Private Limited


Length of Road :- 3.500 KM

Project ID :- 31808908056

Package No. :- RM/WE/NAR/22/0004

Name of Block :- Gaunaha

Certified that all item wise 100% measurement has been taken by me


16-11-2023

JE

Certified that all item wise 50% measurement has been verified by me


16-11-23

AE

Certified that all item wise 10% measurement has been verified by me


16-11-23

EE

Name of Road - Pakri bishauli se amolawa (Sec-7)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/6/23	16:37:38	7	0.1	270	22.9	2700	2650	G	27.21025	84.47234	Normal
24/6/23	16:38:15	7	0.1	250	22.9	2500	2454	G	27.20989	84.47350	Normal
24/6/23	16:39:24	7	0.1	280	22.9	2800	2754	G	27.20898	84.47626	Normal
24/6/23	16:40:0	7	0.1	280	22.9	2800	2784	G	27.20863	84.47714	Normal
24/6/23	16:40:35	7	0.1	280	22.9	2800	2763	G	27.20794	84.47732	Normal
24/6/23	16:41:0	7	0.1	290	22.9	2900	2945	G	27.20700	84.47714	Curve
24/6/23	16:41:10	7	0.1	320	22.9	3200	3150	G	27.20752	84.47749	Normal
24/6/23	16:41:45	7	0.1	310	22.9	3100	3136	G	27.20844	84.47766	Curve
24/6/23	16:42:21	7	0.1	290	22.9	2900	2885	G	27.20875	84.47859	Normal
24/6/23	16:42:21	7	0.1	320	22.9	3200	3192	G	27.20839	84.47955	Normal
24/6/23	16:43:0	7	0.1	290	24.1	2900	2864	G	27.20790	84.48037	Normal
24/6/23	16:43:0	7	0.1	300	24.1	3000	2966	G	27.20743	84.48126	Normal
24/6/23	16:43:31	7	0.1	310	24.1	3100	3090	G	27.20710	84.48222	Normal
24/6/23	16:44:0	7	0.1	280	24.1	2800	2763	G	27.20673	84.48308	Normal
24/6/23	16:44:6	7	0.1	290	24.1	2900	2870	G	27.20654	84.48402	Normal
24/6/23	16:44:6	7	0.1	320	24.1	3200	3171	G	27.20652	84.48500	Normal
24/6/23	16:44:42	7	0.1	280	24.1	2800	2754	G	27.20592	84.48576	Normal
24/6/23	16:45:0	7	0.1	280	24.1	2800	2783	G	27.20582	84.48673	Normal
24/6/23	16:45:17	7	0.1	290	24.1	2900	2856	G	27.20588	84.48776	Normal
24/6/23	16:45:17	7	0.1	250	24.1	2500	2477	G	27.20588	84.48875	Normal
24/6/23	16:45:17	7	0.1	310	24.1	3100	3069	G	27.20534	84.48946	Normal
24/6/23	16:46:0	7	0.1	260	24.1	2600	2558	G	27.20446	84.48934	Normal
24/6/23	16:46:0	7	0.1	250	24.1	2500	2456	G	27.20382	84.49002	Normal
24/6/23	16:46:27	7	0.1	300	24.1	3000	2966	G	27.20366	84.49098	Curve
24/6/23	16:46:27	7	0.1	330	25	3300	3252	G	27.20426	84.49163	Normal
24/6/23	16:47:3	7	0.1	300	25	3000	2966	G	27.20428	84.49258	Normal
24/6/23	16:47:3	7	0.1	280	25	2800	2762	G	27.20396	84.49348	Normal
24/6/23	16:47:3	7	0.1	250	25	2500	2456	G	27.20332	84.49428	Normal
24/6/23	16:47:3	7	0.1	300	25	3000	3048	G	27.20268	84.49503	Normal
24/6/23	16:47:38	7	0.1	270	25	2700	2657	G	27.20222	84.49588	Normal

Prunex
16-11-2023
(J.E)

Prunex
16.11.23

M. S. D.
16/11/23

Name of Road - Pakri bishauli se amolawa (Sec-7)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
24/ 6/ 23	16: 53: 2	7	0.1	310	25	3100	3086	G	27.20253	84.49522	Normal
24/ 6/ 23	16: 53: 37	7	0.1	280	25	2800	2754	G	27.20320	84.49449	Normal
24/ 6/ 23	16: 53: 37	7	0.1	260	25	2600	2586	G	27.20374	84.49369	Normal
24/ 6/ 23	16: 54: 0	7	0.1	270	25	2700	2736	G	27.20423	84.49291	Normal
24/ 6/ 23	16: 54: 12	7	0.1	310	25	3100	3068	G	27.20427	84.49189	Normal
Average IRI Value=							2849				

Praveen
16-11-2023
(JE)

Praveen
16.11.23
AE

Praveen
16/11/23

Name of Customer : Sg Piling And Construction Privi
Name of Work/ Road : Pakri bishauli se amolawa
Lab Job number :
Date : 24-06-2023
Section No. : 7


Test Date : 24-06-2023 Road Name : Pakri bishauli se amolawa
Machine No : 402 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1454 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 3.6 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

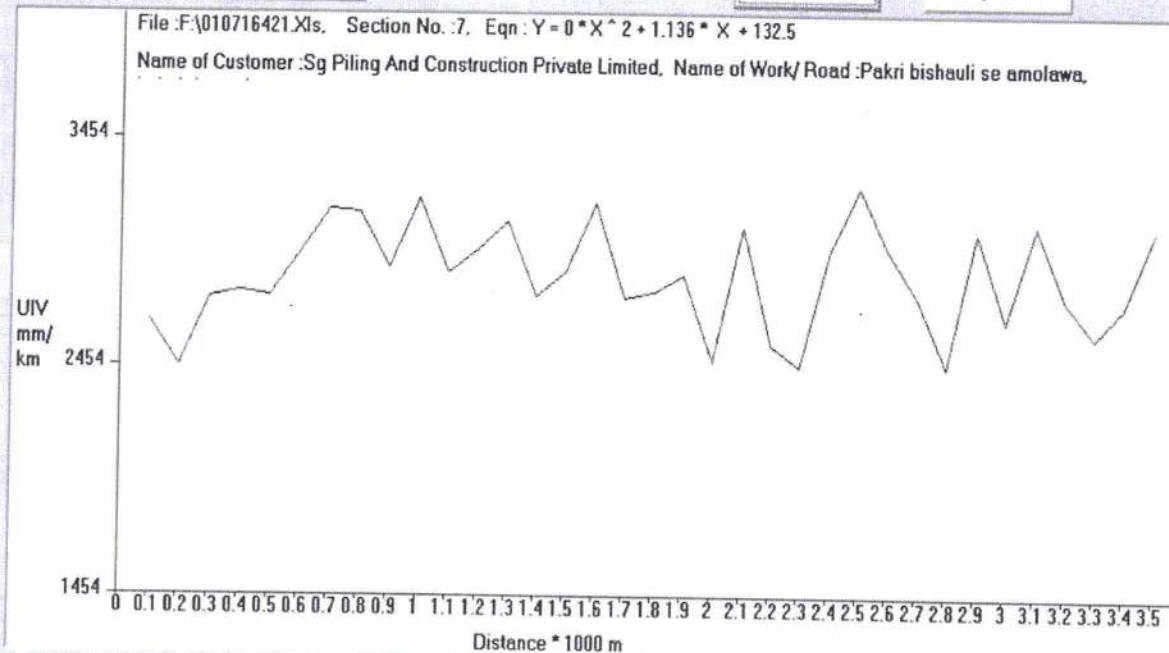

16-11-2023
(S.E)

16/11/23

16.11.23
