

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

पत्रांक :- 18.49.(2030)

पटना/दिनांक :- 04/10/23

प्रेषक,

ई0 राजेश कुमार चौधरी,
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना ।

सेवा में,

नोडल पदाधिकारी-3054,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 योजना अन्तर्गत
अनुरक्षण मद में आवंटन का अधियाचना के संबंध में ।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-3054 (एम.आर.) बिहार ग्रामीण
पथ नई अनुरक्षण नीति-2018 योजना अन्तर्गत अनुरक्षण मद में निम्नलिखित पथ का आवंटन
का अधियाचना का मांग (Yearly Quarter wise) तैयार कर आवश्यक कार्रवाई हेतु समर्पित
किया जाता है, जो निम्न प्रकार है :-

Sl. No.	Name of Road	Yearly Quarter wise	Amount (in Lakh)
1.	SAIDPUR CHANDASI ROD - SAHORA VILLAGE ROAD (Package No.-RM/PA/PAT/19/0005)	1 st Year- 1 st Quarter	0.54673
2.	SAIDPUR CHANDASI ROD - SAHORA VILLAGE ROAD (Package No.-RM/PA/PAT/19/0005)	1 st Year- 2 nd Quarter	0.54673
3.	SAIDPUR CHANDASI ROD - SAHORA VILLAGE ROAD (Package No.-RM/PA/PAT/19/0005)	1 st Year- 3 rd Quarter	0.54673

अतः अनुरोध है कि उक्त योजना अन्तर्गत अनुरक्षण मद में आवंटन उपलब्ध कराने
की कृपा की जाय, ताकि संवेदक का भुगतान किया जा सके ।

अनु०:- यथोक्त ।

विश्वासभाजन



(ई0 राजेश कुमार चौधरी)
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना



STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	SAIDPUR CHANDASI ROAD - SAHORA VILLAGE ROAD		
2	Batch No -	RM/PA/PA1/19/0005		
3	Project ID -	10100102261		
4	Total Length of Road (in Km)	1.2		
5	Length of Road to meet required service level [Completed length] (in Km) (1)	1.2		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	10.93469		
8	Quarterly Payment 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.54673		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND SIGNAGE AND ROAD SAFETY	0	15%	0.00000
IV		0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.54673
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				

Date of inspection by E/I or his agent

Date

Signature of person inspecting road

Name and Designation of person inspecting road

Certify by E/I (signature) Date

John P.
22/09/23
J.E.

Harj
22.09.23
JE

Raj
22/09/23

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (3rd Quarter)

RWD, Works Division Patna

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- SAIDPUR CHANDASI ROAD - SAHORA VILLAGE ROAD
(Package No. RM/PA/PAT/19/0005)
Length of Road :- 1.2 Km
Inspector :- J.E RWD Sub Division : Fatuha

To:-

Executive Engineer
RWD, Works Division Patna

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
OM104	Surface Treatment												No Bleeding/ Flushing Required
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
105	Edge Repair	m ²	N.A	N.A	N.A	N.A							N/A
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												No Edge Drop-Off Required
	Unsealed Shoulder												Not Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							N/A
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							N/A
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												N/A
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							

Chhach
22/09/23
J.E.

22.09.23
J.E.

22/09/23
J.E.

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Name												
	Vegetation												
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, Kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							N/A
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							
	Other activities												


 22/09/23
 J.P.S.

22-09-23
 ME


 Executive Engineer
 Rural Work Department
 Work Division Patna

Name of The Road :SAIDPUR CHANDASI ROAD - SAHORA VILLAGE ROAD

Length :1.2

Package No. : RM/PA/PAT/19/0005

Division : Patna

Block : Fatuha

Contractor Name : Ranjeet Kumar

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
16/8/23	9:10:13	63	0.1	330	0	3300	3367	G	25.471045	85.22882	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
16/8/23	9:10:23	63	0.1	340	30.2	3400	3424	G	25.471987	85.228803	Normal	$X = 2100$		
16/8/23	9:10:36	63	0.1	300	30.3	3000	3050	G	25.472877	85.228753	Normal	$Y = 2244$		
16/8/23	9:10:48	63	0.1	290	30.3	2900	2918	G	25.473768	85.22882	Normal			
16/8/23	9:10:59	63	0.1	300	20.2	3000	3086	G	25.474648	85.228872	Normal	(R)RURAL ROAD		
16/8/23	9:11:08	63	0.1	310	30.3	3100	3140	G	25.475592	85.228972	Normal	Good	Average	Poor
16/8/23	9:11:24	63	0.1	280	20.2	2800	2899	G	25.476418	85.229192	Normal	<4000	4001-5000	>5001
16/8/23	9:11:35	63	0.1	320	20.2	3200	3250	G	25.477382	85.229258	Normal			
16/8/23	9:11:44	63	0.1	330	30.3	3300	3310	G	25.478218	85.229377	Normal			
16/8/23	9:11:57	63	0.1	370	20.2	3700	3741	G	25.47907	85.229813	Normal			
16/8/23	9:12:09	63	0.1	320	30.2	3200	3244	G	25.479458	85.230437	Normal			
16/8/23	9:12:25	63	0.1	310	30.3	3100	3150	G	25.479322	85.230823	Normal			
Total			1.2	3800	292.7	38000	38579		305.709785	1022.75194				
Average						3166.667	3214.917							

22/09/23
g.e.

22/09/23
AT

22/09/23

analyzer

Name of Customer : Ranjeet Kumar
Name of Work/Road : Jasi Road -Sohora Village Road
Lab Job number :
Date : 16-08-2023
Section No. : 63

Test Date : 16-08-2023 Road Name : Ranjeet Kumar
Machine No : 374 Road Type : (R) RURAL ROAD
Start S No : Side : Interval
Start E No :
Weather : UV Range : 1899 To 5000 1000 mm/km
Start Location : Dist Range : 0 To 13 01 1000 m
End Location : Equation : $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$


Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\leenwdpa\Desktop\Ranjeet Kumar\steco.xlsx Section No. :63. Eqn : $Y = 0 \cdot X^2 + 0.936 \cdot X +$

Name of Customer :Ranjeet Kumar, Name of Work/ Road :Saipur Chandasi Road -Sohora Village Road, Lab Job

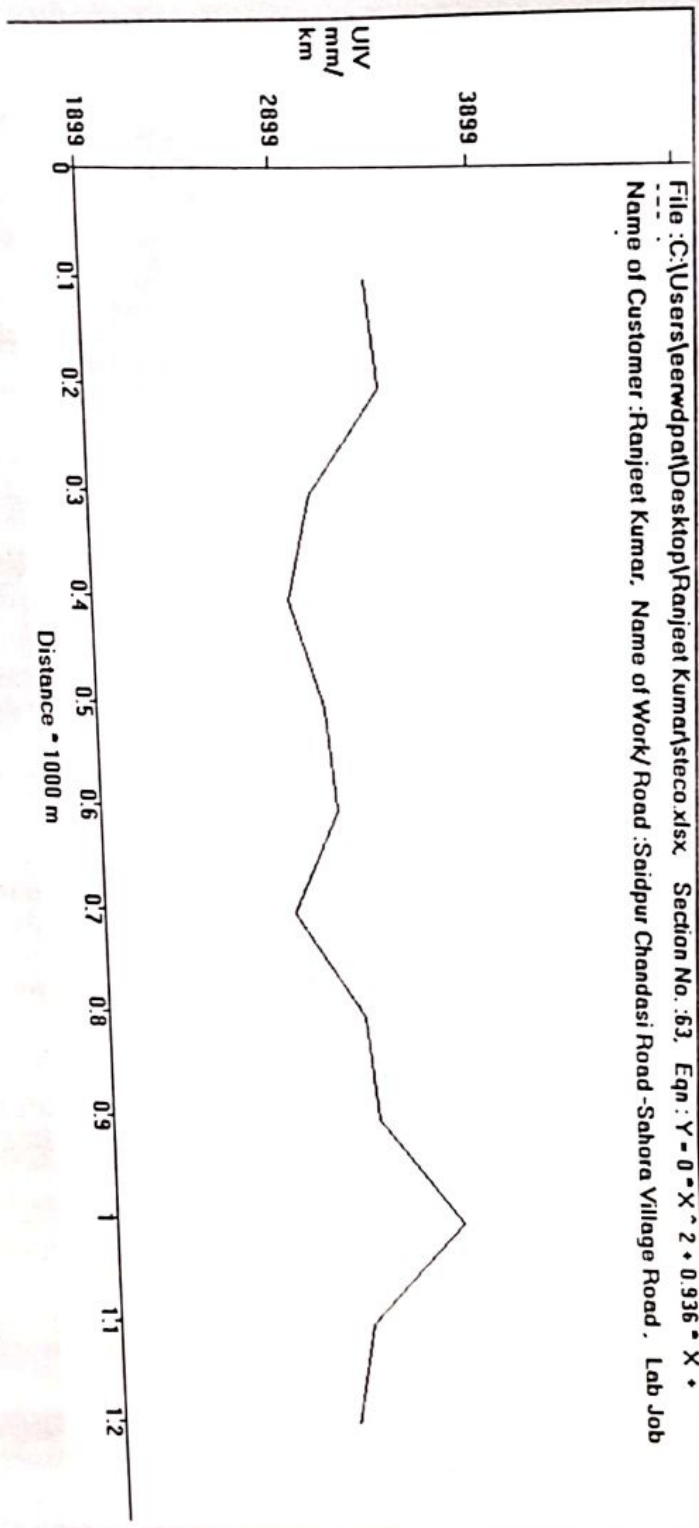

Ch-F
22/09/23
J.E

Hum
22.09.23
AT

22/09/23
