

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2363(अनु०)

/नरकटियागंज, दिनांक 7/12/2024

प्रेषक,

ई० मनीष कुमार,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति-2018” योजनान्तर्गत पथ:-

1. Tikuliya to Gidha (VR45)
2. L105-T06 to Tikachhapar (VR105)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



ई० मनीष कुमार
कार्यपालक अभियन्ता,
ग्रा०का०वि०, का०प्र०, नरकटियागंज


Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/2 4/0007	Tikuliya to Gidha (VR45)	31808902163	1086 01.03.2024	2.270	140.86000	109.88006	20.60611	13/24-25 01.10.2024	30.06.2025		3041	SDBC-25mm	5%	0.00000	0.00000	54.93890	Surface complete
2	RM/WE/NAR/2 4/0007	L105-T06 to Tikachhapar (VR105)	31808902224	1086 01.03.2024	2.400	149.19000	117.65106	20.20084	13/24-25 01.10.2024	30.06.2025		3127	SDBC-25mm	5%	0.00000	0.00000	44.67291	Surface complete

Handwritten: 07/12/24
J.E.

Handwritten: 07/12/24


Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Tikuliya to Gidha (VR45)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Chanda Shahi


Length of Road :- 2.270 KM

Project ID :- 31808902163

Package No. :- RM/WE/NAR/24/0007

Name of Block :- Mainatanr

Certified that all item wise 100% measurement has been taken by me

 07/12/24

JE

Certified that all item wise 50% measurement has been verified by me

 07/12/24

AE

Certified that all item wise 10% measurement has been verified by me

 07/12/24

EE

Name of Road - Tikuliya to Gidha (VR45) (Sec-13)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
6/12/24	9:39:5	13	0.1	310	23.5	3100	3052	G	26.901669	84.582708	Normal
6/12/24	9:40:13	13	0.1	300	23.6	3000	2994	G	26.902147	84.581882	Normal
6/12/24	9:40:48	13	0.1	310	23.6	3100	3068	G	26.902606	84.580980	Normal
6/12/24	9:41:0	13	0.1	350	33.7	3500	3468	G	26.903180	84.580208	Normal
6/12/24	9:41:0	13	0.1	310	23.6	3100	3133	G	26.903821	84.579500	Normal
6/12/24	9:41:23	13	0.1	310	23.6	3100	3121	G	26.904558	84.578921	Normal
6/12/24	9:41:23	13	0.1	300	23.6	3000	3029	G	26.905204	84.578218	Normal
6/12/24	9:42:0	13	0.1	310	13.5	3100	3108	G	26.905754	84.577445	Normal
6/12/24	9:42:0	13	0.1	320	23.6	3200	3238	G	26.906342	84.576662	Normal
6/12/24	9:42:34	13	0.1	310	23.6	3100	3133	G	26.907002	84.575981	Normal
6/12/24	9:43:0	13	0.1	280	23.6	2800	2762	G	26.907385	84.575106	Normal
6/12/24	9:43:9	13	0.1	270	13.5	2700	2657	G	26.908021	84.574377	Normal
6/12/24	9:44:0	13	0.1	320	23.6	3200	3238	G	26.908710	84.573749	Normal
6/12/24	9:44:0	13	0.1	310	23.6	3100	3133	G	26.909590	84.573384	Normal
6/12/24	9:44:19	13	0.1	290	26.6	2900	2866	G	26.910428	84.573368	Normal
6/12/24	9:44:54	13	0.1	320	28.5	3200	3152	G	26.911346	84.573588	Normal
6/12/24	9:45:0	13	0.1	290	26.8	2900	2859	G	26.912226	84.573698	Normal
6/12/24	9:45:29	13	0.1	320	27	3200	3231	G	26.913104	84.573972	Normal
6/12/24	9:45:40	13	0.1	300	26.5	3000	2964	G	26.913809	84.573462	Normal
6/12/24	9:46:1	13	0.1	280	26.5	2800	2830	G	26.914651	84.573202	Normal
6/12/24	9:46:22	13	0.1	280	33.7	2800	2817	G	26.915579	84.573433	Normal
6/12/24	9:46:33	13	0.1	290	33.7	2900	2926	G	26.916452	84.573679	Normal
6/12/24	9:46:54	13	0.07	320	24.8	3200	3175	G	26.916878	84.574122	Normal
Average IRI Value=							3041				

R.D.
07/12/24
J.E.

P.L.
07/12/24

[Signature]
Executive Engineer
Rural Works Department
Works Division Narkattagani

Name of Customer : Chanda Shahi
Name of Work/ Road : Tikuliya to Gidha (VR45)
Lab Job number :
Date : 6/12/2024
Section No. : 13

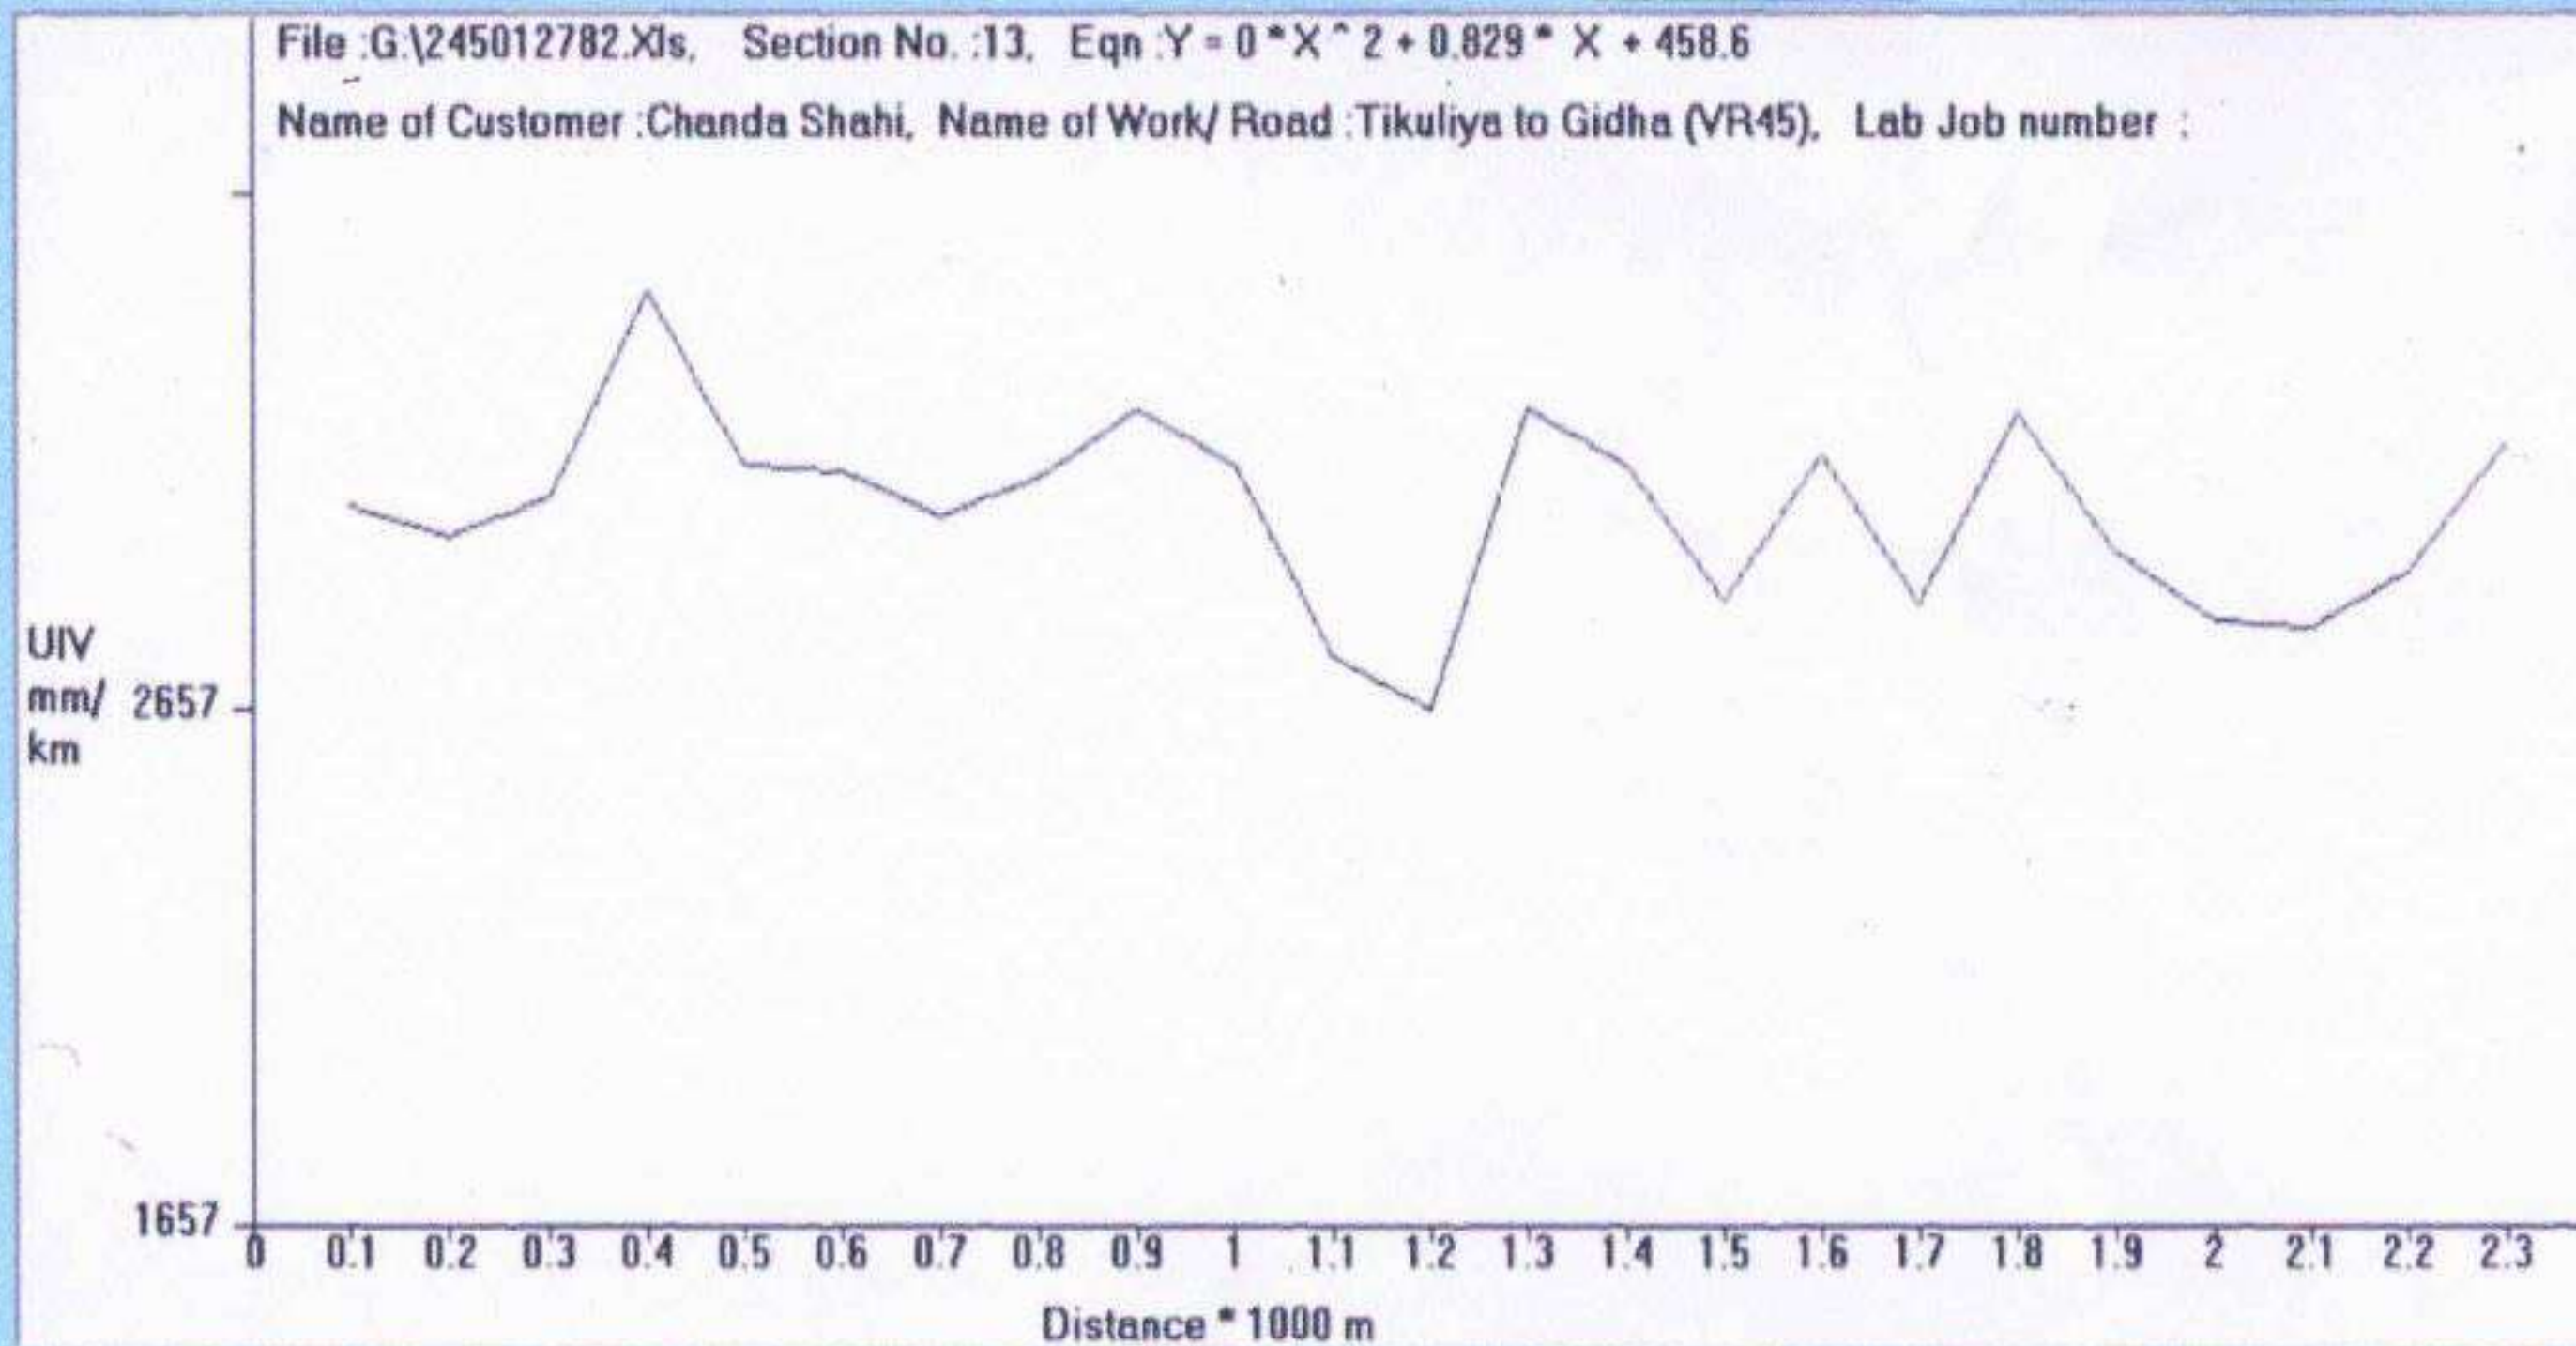
Test Date : 6/12/2024 Road Name : Tikuliya to Gidha (VR45)
Machine No : 472 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1657 To 4000 1000 mm/km
Start Location : 0.000 Dist Range : 0 To 2.4 0.1 * 1000 m
End Location : 2.270 Equation : $Y = 0 * X^2 + 0.829 * X + 458.6$

Print

Generate Report and Graph

Redraw Graph


Map View



R.D. 07/12/24

J.E.

Plt
07/12/24


Executive Engineer
Rural Works Department
Works Division Narkatiagani
