

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2394 (अनु०)

/नरकटियागंज, दिनांक 16/12/24

प्रेषक,

ई० मनीष कुमार,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति-2018” योजनान्तर्गत पथ:-

1. T03 to Senuria via Sindhwalia (VR47)
2. T03 to Purbi (VR46)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन

16/12/24

ई० मनीष कुमार


कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
				Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
RM/WENAR/24/0005	T03 to Senuria via Sindhwalia (VR47)	31808902169	6115 04.12.2023	1.770	97.96000	73.80932	16.96830	03/24-25 03.09.2024	02.06.2025		2969	SDBC-25mm	5%	0.00000	0.00000	73.56352	Surface complete
RM/WENAR/24/0005	T03 to Purbi (VR46)	31808902168	6115 04.12.2023	0.940	49.70600	36.53680	9.41445	03/24-25 03.09.2024	02.06.2025		3034	SDBC-25mm	5%	0.00000	0.00000	36.46770	Surface complete


Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

Handwritten: 6/12/2024

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- T03 to Senuria via Sindhwalia (VR47)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Khurshid Alam

Length of Road :- 1.770 KM

Project ID :- 31808902169

Package No. :- RM/WE/NAR/24/0005

Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


JE

Certified that all item wise 50% measurement has been verified by me


AE

Certified that all item wise 10% measurement has been verified by me


EE

Name of Road - T03 to Senurla via Sindhwalla (VR47) (Sec-11)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	In km	In mm	Rate	mm/km	mm/km	ROAD			
6/12/24	11:39:5	11	0.1	300	23.3	3000	2952	G	27.000255	84.750124	Normal
6/12/24	11:40:13	11	0.1	290	23.4	2900	2894	G	27.001144	84.750231	Normal
6/12/24	11:40:48	11	0.1	300	23.4	3000	2968	G	27.002043	84.750510	Normal
6/12/24	11:41:0	11	0.1	340	33.5	3400	3368	G	27.002464	84.749598	Normal
6/12/24	11:41:0	11	0.1	300	23.4	3000	3033	G	27.002731	84.748643	Normal
6/12/24	11:41:23	11	0.1	300	23.4	3000	3021	G	27.002798	84.747645	Normal
6/12/24	11:41:23	11	0.1	290	23.4	2900	2929	G	27.003114	84.746701	Normal
6/12/24	11:42:0	11	0.1	300	13.3	3000	3008	G	27.003381	84.745736	Normal
6/12/24	11:42:0	11	0.1	310	23.4	3100	3138	G	27.003601	84.744759	Normal
6/12/24	11:42:34	11	0.1	300	23.4	3000	3033	G	27.003869	84.743772	Normal
6/12/24	11:43:0	11	0.1	270	23.4	2700	2662	G	27.004318	84.743161	Normal
6/12/24	11:43:9	11	0.1	260	13.3	2600	2557	G	27.005150	84.743558	Normal
6/12/24	11:44:0	11	0.1	310	23.4	3100	3138	G	27.005876	84.744116	Normal
6/12/24	11:44:0	11	0.1	300	23.4	3000	3033	G	27.006698	84.744298	Normal
6/12/24	11:44:19	11	0.1	280	26.4	2800	2766	G	27.007673	84.744319	Normal
6/12/24	11:44:54	11	0.1	310	28.3	3100	3052	G	27.008323	84.744631	Normal
6/12/24	11:45:0	11	0.1	280	26.6	2800	2759	G	27.006125	84.744824	Normal
6/12/24	11:45:29	11	0.07	310	26.8	3100	3131	G	27.006737	84.745489	Normal
Average IRI Value=							2969				

14/11/24
6/12/24
0.0

Plt
06/12/24

16/12/24

Name of Customer : Khurshid Alam
 Name of Work/ Road : T03 to Senuria via Sindhwalia
 Lab Job number :
 Date : 6/12/2024
 Section No : 11


Test Date : 6/12/2024 Road Name : T03 to Senuria via Sindhwalia
 Machine No : 472 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 1557 To 4000 1000 mm/km
 Start Location : 0.000 Dist Range : 0 To 1.0 0.1 = 1000 m
 End Location : 1.770 Equation : $Y = 0 \cdot X^2 + 0.029 \cdot X + 450.6$

Print

Generate Report and Graph

Redraw Graph

Map View

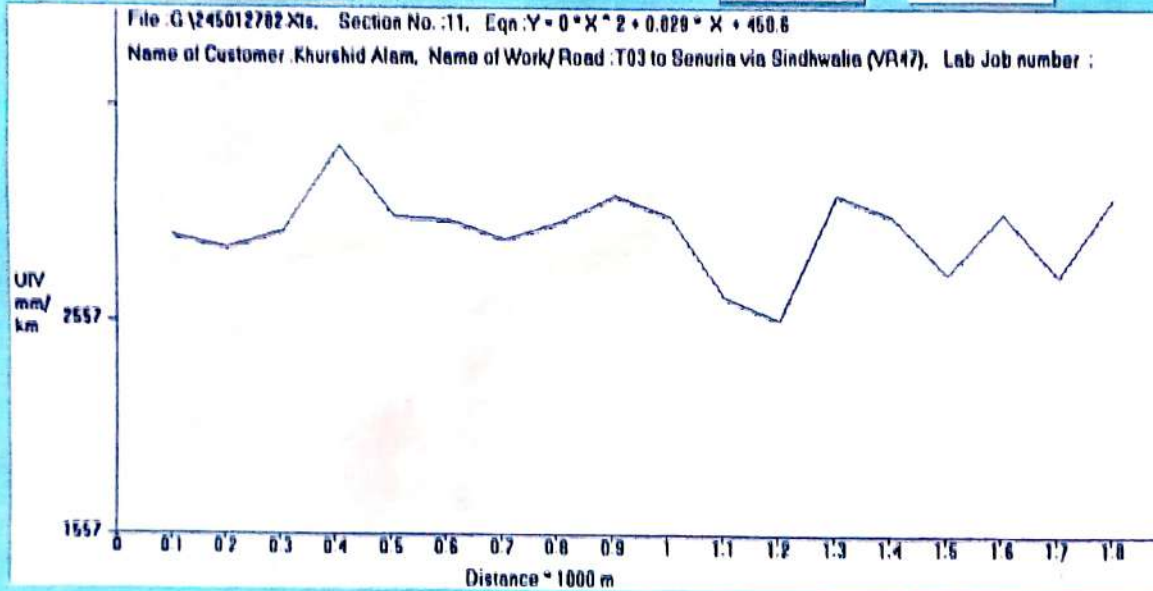

Min
6/12/2024
J-C

Plot
06/12/24
