

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 243(अनु०)

/ नरकटियागंज, दिनांक 07/02/2024

प्रेषक,

ई० मुकेश कुमार सिंह,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति-2018” योजनान्तर्गत पथ:-

1. Triveni main canal to Ahrar Road

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन

ई० मुकेश कुमार सिंह

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज

07/02/2024

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/22/0014	Triveni main canal to Ahrar Road (2.40km)	31808801018	<u>105</u> 03.06.2022	2.400	130.60000	94.85116	26.25330	<u>45/22-23</u> 27.09.2022	26.06.2023		3017	SDBC-25mm	5%	0.00000	0.00000	93,96661	Surface Complete

[Signature]
07/02/24
AE

[Signature]
Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj
[Signature]
08/02/24

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Triveni main canal to Ahrar Road (2.40km)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Ranu Kumar Mishra


Length of Road :- 2.400 KM

Project ID :- 31808801018

Package No. :- RM/WE/NAR/22/0014

Name of Block :- Gaunaha

Certified that all item wise 100% measurement has been taken by me


07-02-2024
JE

Certified that all item wise 50% measurement has been verified by me


07/02/24
AE

Certified that all item wise 10% measurement has been verified by me


31/2/24
EE

Name of Road - Triveni main canal to Ahrar Road (Sec-43)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
27/12/23	8:29:9	43	0.1	300	26.4	3000	3034	G	27.22438	84.450509	Normal
27/12/23	8:30:0	43	0.1	300	26.5	3000	2976	G	27.22501	84.449797	Normal
27/12/23	8:30:16	43	0.1	310	26.5	3100	3050	G	27.22564	84.449072	Normal
27/12/23	8:30:51	43	0.1	350	36.6	3500	3450	G	27.22633	84.448433	Normal
27/12/23	8:31:0	43	0.1	310	26.5	3100	3115	G	27.22701	84.447765	Normal
27/12/23	8:31:26	43	0.1	310	26.5	3100	3103	G	27.22769	84.447112	Normal
27/12/23	8:31:26	43	0.1	300	26.5	3000	3011	G	27.22856	84.446902	Normal
27/12/23	8:32:2	43	0.1	310	16.4	3100	3090	G	27.22945	84.446746	Normal
27/12/23	8:32:37	43	0.1	320	26.5	3200	3220	G	27.23032	84.44665	Normal
27/12/23	8:33:12	43	0.1	310	26.5	3100	3115	G	27.23101	84.446035	Normal
27/12/23	8:33:12	43	0.1	270	26.5	2700	2744	G	27.23157	84.445158	Normal
27/12/23	8:33:47	43	0.1	260	16.4	2600	2639	G	27.23198	84.444335	Normal
27/12/23	8:40:0	43	0.1	320	26.5	3200	3220	G	27.23239	84.443523	Normal
27/12/23	8:40:14	43	0.1	310	26.5	3100	3115	G	27.2327	84.442587	Normal
27/12/23	8:43:11	43	0.1	280	29.5	2800	2848	G	27.23279	84.441585	Normal
27/12/23	8:43:11	43	0.1	310	31.4	3100	3134	G	27.23319	84.44059	Normal
27/12/23	8:43:46	43	0.1	280	29.7	2800	2841	G	27.2334	84.439694	Normal
27/12/23	8:44:0	43	0.1	320	29.9	3200	3213	G	27.23366	84.438722	Normal
27/12/23	8:44:0	43	0.1	290	29.4	2900	2946	G	27.23386	84.437737	Normal
27/12/23	8:44:21	43	0.1	280	29.4	2800	2812	G	27.23368	84.436803	Normal
27/12/23	8:44:21	43	0.1	280	36.6	2800	2799	G	27.23377	84.435796	Normal
27/12/23	8:44:21	43	0.1	290	36.6	2900	2908	G	27.23388	84.434789	Normal
27/12/23	8:44:43	43	0.1	320	27.7	3200	3157	G	27.23398	84.433781	Normal
27/12/23	8:45:11	43	0.1	290	36.6	2900	2879	G	27.23405	84.432769	Normal
Average IRI Value=							3017				

Pruman
07-02-2024
(J.E)

De
07/02/24
AE

W. S. S.
Executive Engineer
Rural Works Department
Works Division Narkataganj
07/02/2024

Name of Customer : Ranu Kumar Mishra
Name of Work/ Road : Triveni main canal to Arhar Road
Lab Job number :
Date : 27-12-2023
Section No. : 43


Test Date : 27-12-2023 Road Name : Triveni main canal to Arhar Road
Machine No : 402 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UV Range : 1639 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 2.5 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

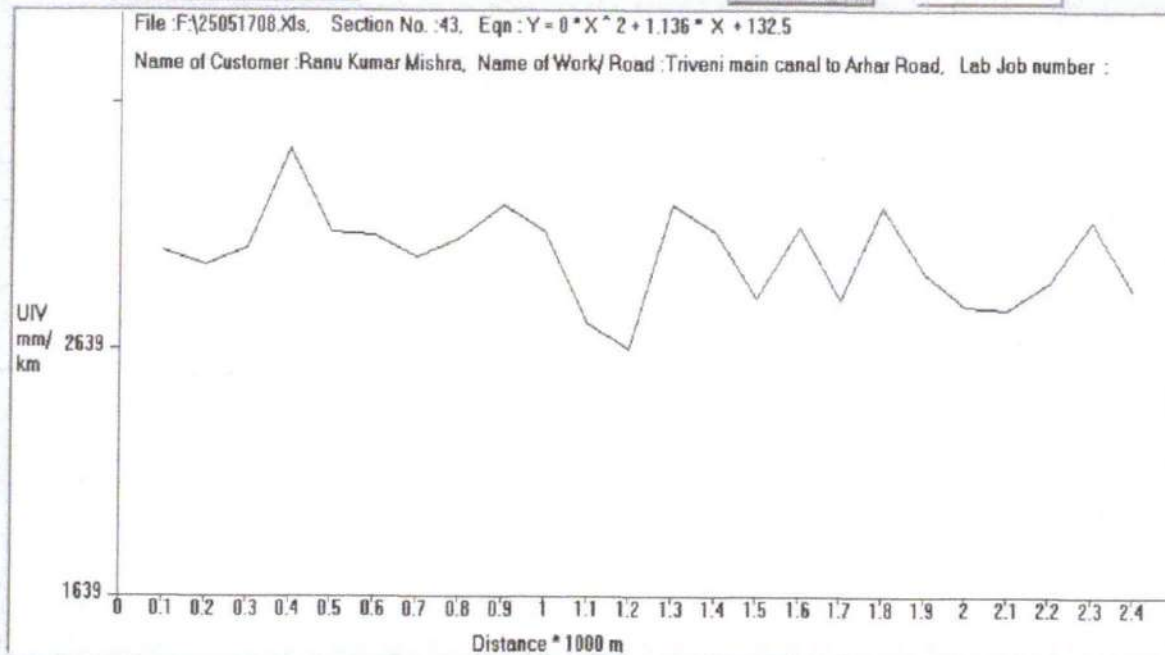

P. Kumar
07-02-2024
(J-E)

P. Kumar
07-02-24
AE

Executive Engineer
Rural Works Department
Works Division Narkatiaganj
07/02/2024
