

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, फुलपरास।

Email ID – cerwdphulparas@gmail.com

पत्रांक.....५१४७८७७

दिनांक.....०७.०५.२०२५

प्रेषक,

ई० सुभाष कुमार
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना ।

विषय:— शीर्ष NEW MAINTENANCE POLICY- 2018 (MR-3054) अनुरक्षण मद में
आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष NEW MAINTENANCE POLICY –
2018 (MR-3054) अनुरक्षण मद योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन
उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:—

1- Quarterly statement

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।


Maintenace Requistion Formate for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy-2018

Road Details				A A Details			Agreement Details								Previous Maintenan		Length as per	Per	Current Demand for maintenance Amount		Current Total	Remarks
SL No	Road Name	Batch No.	Project ID	Actual Completion Date	Main Work Amount	Maintenace Amount	Main Work Amount	Agreement 1	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maintenance Amount	Length	1st Quarter	2nd Quarter			1st Quarter	2nd Quarter		
1	PWD ROAD - KURIBAN	RM/MA/PHU/20/0002	31909802074	24.03.21	62.282	20.963	57.389	4.04004	4.04004	4.04004	4.04004	4.04004	20.2002	2.17	0	0	2.17	3046	1.01001	1.01001		
2	Kriaot Amachiri Road to Hariraha	RM/MA/PHU/20/0002	31909801010	22.07.21	125.61	53.459	117.563	9.72926	9.72926	9.72926	9.72926	9.72926	48.6463	5.5	0	0	5.5	3144	2.432315	0		
3	W.K.T - JHITKI	RM/MA/PHU/20/0002	31909802087	24.03.21	32.328	14.141	30.238	2.57365	2.57365	2.57365	2.57365	2.57365	12.86825	1.45	0	0	1.45	3021	0.6434125	0.643413		
4	Kariaut to amchiri	RM/MA/PHU/20/0002	31909908021	24.03.21	60.86	20.173	56.027	3.73414	3.73414	3.73414	3.73414	3.73414	18.6707	2.03	0	0	2.03	2978	0.933535	0.933535		
5	T03 - AURAHA	RM/MA/PHU/20/0002	31909902010	24.03.21	32.04	15.16	29.954	2.75874	2.75874	2.75874	2.75874	2.75874	13.7937	1.42	0	0	1.42	3059	0.689685	0.689685		
Total															0	0			5.7089575	3.276643	8.98560	


 Executive Engineer
 Rural Works Division
 Phulparas


Name of Customer: Sri Sanjay Kumar Jha, Machine no: 19210, Road: Kriaot Amachliri Road to Haritraha, Date: 28-03-25, Section No: 99, Equation: $y = 0.940x + 239.3$

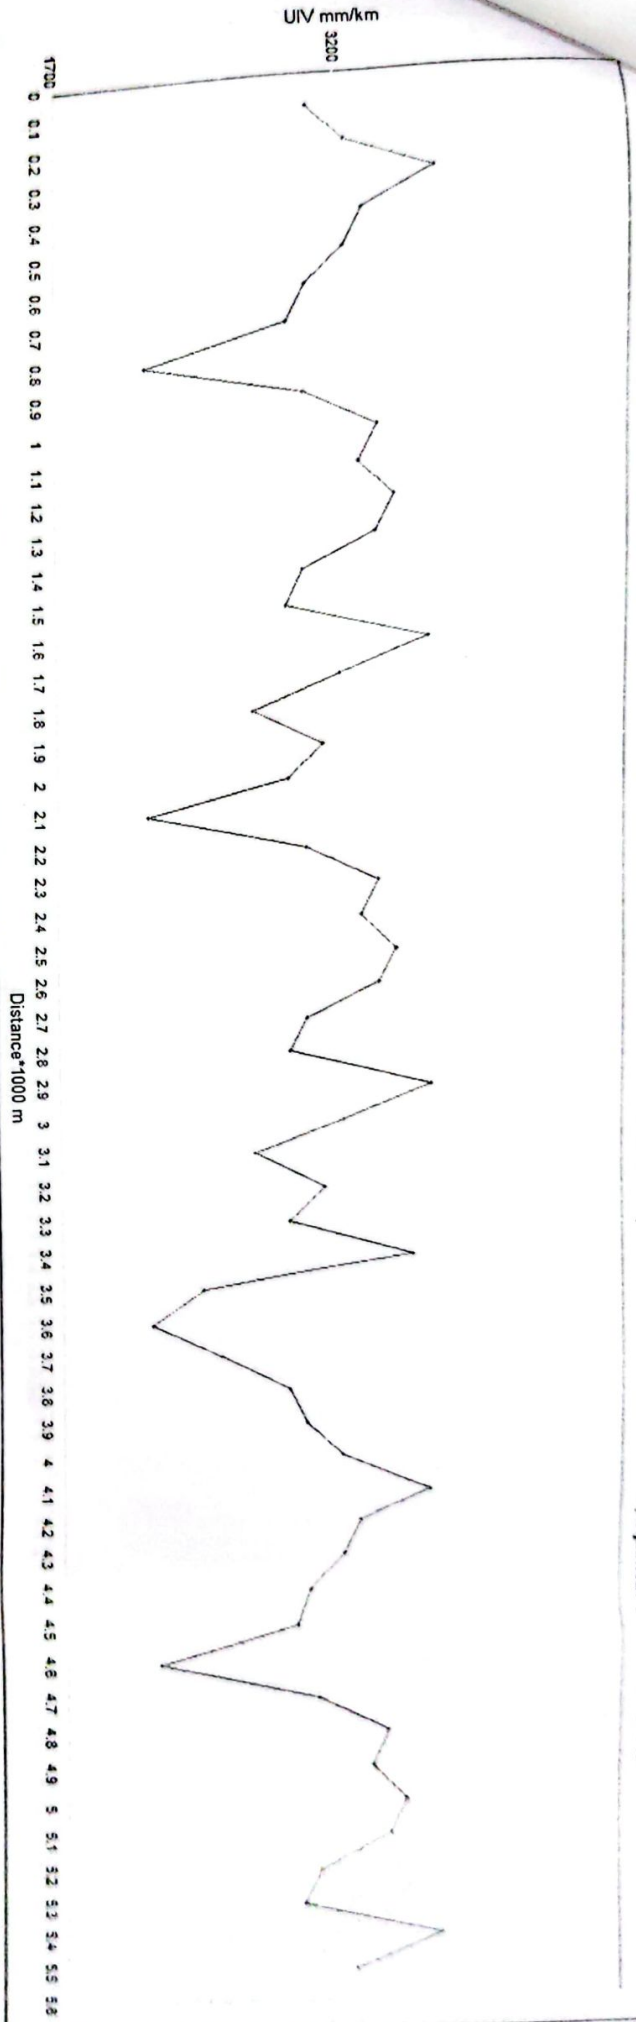

[Signature]
 7/4/25
 A/E

[Signature]
 EXECUTIVE ENGINEER
 Rural Works Department
 Phulparas
 7/4/25

Name of Customer: Sri Sanjay Kumar Jha . Machine no: 19210 , Road: Kriant Amachit Road to Haritraha , Date: 28-03-25 , Section No: 99 , Equation: $Y=0.940 X + 239.3$

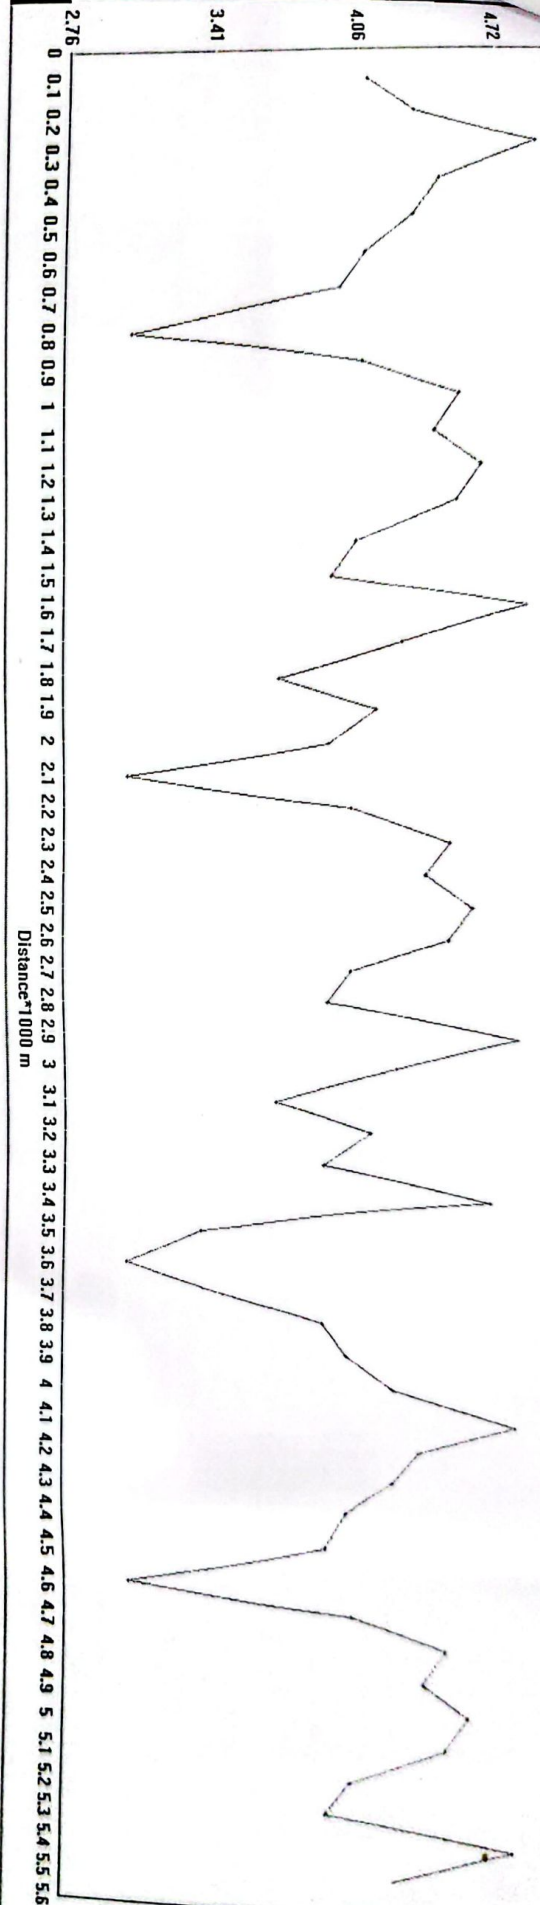

Sr
7/11/25
BE

Sr
7/11/25
EXECUTIVE ENGINEER
Rural Works Department
Gorakhpur Division
Phulparas

Name of work : Kiriad Annachin Road to Hariraha
 Name of customer : Sri Sanjay Kumar Jha

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	Uturn(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
28/03/25	15:54:31	99	100	100	30.0 cm	6.5 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.316251	N	86.392902	E	Normal
28/03/25	15:55:49	99	100	200	32.0 cm	13.9 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.316105	N	86.393152	E	Normal
28/03/25	15:56:36	99	100	300	37.0 cm	11.5 Km/Hr	3700.0 mm/Km	3717	3.88	Good	26.316125	N	86.393190	E	Normal
28/03/25	15:57:05	99	100	400	33.0 cm	15.8 Km/Hr	3300.0 mm/Km	3341	3.44	Good	26.316198	N	86.393213	E	Normal
28/03/25	15:57:49	99	100	500	32.0 cm	1.0 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.316230	N	86.393285	E	Normal
28/03/25	15:58:11	99	100	600	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.316293	N	86.393315	E	Normal
28/03/25	15:59:42	99	100	700	29.0 cm	26.4 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.316331	N	86.393418	E	Normal
28/03/25	16:01:36	99	100	800	21.0 cm	27.4 Km/Hr	2100.0 mm/Km	2213	3.07	Good	26.316397	N	86.393492	E	Normal
28/03/25	16:02:01	99	100	900	30.0 cm	29.6 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.316415	N	86.393514	E	Normal
28/03/25	16:02:34	99	100	1000	34.0 cm	39.7 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.316491	N	86.393645	E	Normal
28/03/25	16:03:19	99	100	1100	33.0 cm	32.0 Km/Hr	3300.0 mm/Km	3341	3.44	Good	26.316521	N	86.393798	E	Normal
28/03/25	16:03:52	99	100	1200	35.0 cm	21.0 Km/Hr	3500.0 mm/Km	3529	3.66	Good	26.316589	N	86.393856	E	Normal
28/03/25	16:04:43	99	100	1300	34.0 cm	8.3 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.316636	N	86.393974	E	Normal
28/03/25	16:05:14	99	100	1400	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.316692	N	86.393987	E	Normal
28/03/25	16:05:51	99	100	1500	29.0 cm	25.4 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.316748	N	86.394005	E	Normal
28/03/25	16:06:15	99	100	1600	37.0 cm	12.9 Km/Hr	3700.0 mm/Km	3717	3.88	Good	26.316779	N	86.394100	E	Normal
28/03/25	16:06:47	99	100	1700	32.0 cm	39.2 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.316846	N	86.394198	E	Normal
28/03/25	16:07:09	99	100	1800	27.0 cm	24.4 Km/Hr	2700.0 mm/Km	2777	3.76	Good	26.316897	N	86.394219	E	Normal
28/03/25	16:07:57	99	100	1900	31.0 cm	14.6 Km/Hr	3100.0 mm/Km	3153	3.21	Good	26.316940	N	86.394293	E	Normal
28/03/25	16:08:34	99	100	2000	29.0 cm	12.2 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.316991	N	86.394360	E	Normal
28/03/25	16:09:30	99	100	2100	21.0 cm	27.4 Km/Hr	2100.0 mm/Km	2213	3.07	Good	26.317005	N	86.394399	E	Normal

27/4/25
 AC

EXECUTIVE ENGINEER
 Rural Works Department
 Works Division
 P. K. S. 25

Name of work : Kriaot Amachiri Road to Hariraha

Name of customer : Sri Sanjay Kumar Jha

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

28/03/25	16.10.01	99	100	2200	30.0 cm	29.6 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.317097	N	86.394413	E	Normal
28/03/25	16.10.34	99	100	2300	34.0 cm	39.7 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.317152	N	86.394467	E	Normal
28/03/25	16.11.19	99	100	2400	33.0 cm	32.0 Km/Hr	3300.0 mm/Km	3341	3.44	Good	26.317197	N	86.394518	E	Normal
28/03/25	16.11.52	99	100	2500	35.0 cm	21.0 Km/Hr	3500.0 mm/Km	3529	3.66	Good	26.317258	N	86.394569	E	Normal
28/03/25	16.12.23	99	100	2600	34.0 cm	8.3 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.317352	N	86.394627	E	Normal
28/03/25	16.13.14	99	100	2700	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.317392	N	86.394680	E	Normal
28/03/25	16.13.51	99	100	2800	29.0 cm	26.4 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.317415	N	86.394756	E	Normal
28/03/25	16.14.15	99	100	2900	37.0 cm	12.9 Km/Hr	3700.0 mm/Km	3717	3.88	Good	26.317496	N	86.394791	E	Normal
28/03/25	16.14.47	99	100	3000	32.0 cm	39.2 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.317502	N	86.395129	E	Normal
28/03/25	16.15.09	99	100	3100	27.0 cm	24.4 Km/Hr	2700.0 mm/Km	2777	3.76	Good	26.311540	N	86.395330	E	Normal
28/03/25	16.15.57	99	100	3200	31.0 cm	14.6 Km/Hr	3100.0 mm/Km	3153	3.21	Good	26.311612	N	86.395436	E	Normal
28/03/25	16.16.34	99	100	3300	29.0 cm	12.2 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.311529	N	86.395512	E	Normal
28/03/25	16.16.59	99	100	3400	36.0 cm	6.5 Km/Hr	3600.0 mm/Km	3623	3.77	Good	26.311239	N	86.395635	E	Normal
28/03/25	16.17.27	99	100	3500	24.0 cm	33.9 Km/Hr	2400.0 mm/Km	2495	3.42	Good	26.311352	N	86.395742	E	Normal
28/03/25	16.17.55	99	100	3600	21.0 cm	27.5 Km/Hr	2100.0 mm/Km	2213	3.07	Good	26.311568	N	86.395875	E	Normal
28/03/25	16.18.31	99	100	3700	25.0 cm	15.8 Km/Hr	2500.0 mm/Km	2589	3.53	Good	26.311652	N	86.395947	E	Normal
28/03/25	16.18.52	99	100	3800	29.0 cm	15.0 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.311475	N	86.395996	E	Normal
28/03/25	16.19.31	99	100	3900	30.0 cm	6.5 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.311963	N	86.396652	E	Normal
28/03/25	16.20.49	99	100	4000	32.0 cm	13.9 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.311598	N	86.396748	E	Normal
28/03/25	16.21.36	99	100	4100	37.0 cm	11.5 Km/Hr	3700.0 mm/Km	3717	3.88	Good	26.311478	N	86.396789	E	Normal
28/03/25	16.22.05	99	100	4200	33.0 cm	15.8 Km/Hr	3300.0 mm/Km	3341	3.44	Good	26.311748	N	86.396874	E	Normal
28/03/25	16.22.49	99	100	4300	32.0 cm	1.0 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.311459	N	86.396914	E	Normal

At

EXECUTIVE ENGINEER
Rural Works Department
Phuprasas

Name of work : Kriaot Amachiri Road to Hairtraha

Name of customer : Sri Sanjay Kumar Jha

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

28/03/25	16.23.11	99	100	4400	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.311567	N	86.397468	E	Normal
28/03/25	16.23.42	99	100	4500	29.0 cm	26.4 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.311625	N	86.397158	E	Normal
28/03/25	16.24.36	99	100	4600	21.0 cm	27.4 Km/Hr	2100.0 mm/Km	2213	3.07	Good	26.311703	N	86.397197	E	Normal
28/03/25	16.25.01	99	100	4700	30.0 cm	29.6 Km/Hr	3000.0 mm/Km	3059	3.1	Good	26.311798	N	86.397201	E	Normal
28/03/25	16.25.34	99	100	4800	34.0 cm	39.7 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.311807	N	86.397295	E	Normal
28/03/25	16.26.19	99	100	4900	33.0 cm	32.0 Km/Hr	3300.0 mm/Km	3341	3.44	Good	26.311963	N	86.397261	E	Normal
28/03/25	16.27.52	99	100	5000	35.0 cm	21.0 Km/Hr	3500.0 mm/Km	3529	3.66	Good	26.311569	N	86.397322	E	Normal
28/03/25	16.28.43	99	100	5100	34.0 cm	8.3 Km/Hr	3400.0 mm/Km	3435	3.55	Good	26.311645	N	86.397391	E	Normal
28/03/25	16.29.14	99	100	5200	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3059	4.1	Good	26.311471	N	86.397452	E	Normal
28/03/25	16.29.51	99	100	5300	29.0 cm	26.4 Km/Hr	2900.0 mm/Km	2965	3.99	Good	26.311789	N	86.397498	E	Normal
28/03/25	16.30.15	99	100	5400	37.0 cm	12.9 Km/Hr	3700.0 mm/Km	3717	3.88	Good	26.311780	N	86.397597	E	Normal
28/03/25	16.30.47	99	100	5500	32.0 cm	39.2 Km/Hr	3200.0 mm/Km	3247	3.32	Good	26.311987	N	86.397468	E	Normal

Sanjay Kumar Jha
Rt

Sanjay Kumar Jha
EXECUTIVE ENGINEER
Rural Works Department
Muzaffarpur Division
Muzaffarpur

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT (Qtr-01)

PIU Name :- RWD(WD), Phulparas

Block Name:- Laukahi

1	Name of the Road	Kriaot Amachiri Road to Harirah		
2	Batch No.	RM/MA/PHU/20/0002		
3	Project ID	31909908021		
4	Total Lenth of Road (in KM)	5.5		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	5.5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	48.6463		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.43232		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				2.43232

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

(Signature)

Signature of person inspecting road

EXECUTIVE ENGINEER
Rural Works Department
Phulparas
24/12/23

Position Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Phulparas

Qtr (01)

Government of Bihar

Rural works Department

Road From- Kriaot Amachiri Road to Harirah

Length of Road: 2.5 KM

Period : From 23.07.21 To 22.10.21

Inspector: J.E RWD Sub Division,

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer
RWD Works Division -Phulparas

Position: J.E

S No	Standard Work item		Units of work required in each kilometre										Comments
	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM101	OM100 Sealed Pavement												
	Pothole Patching	m2	No	No	No	No	No	No	No	No	No	No	No Pothole found
OM102	Surface Depression and Rut Patching	m2	No	No	No	No	No	No	No	No	No	No	No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	No	No	No	No	No	No	No	No	No	No	No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	No	No	No	No	No	No	No	No	No	No	No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	No	No	No	No	No	No	No	No	No	No	No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	No	No	No	No	No	No	No	No	No	No	No Crocodile Cracking found
OM105	Edge Repair	m2	No	No	No	No	No	No	No	No	No	No	No Edge Repair Required
OM106	Digouts	m2											
OM107	Concrete Pavement	m3	No	No	No	No	No	No	No	No	No	No	No Concrete Pavement Repair Required
	Other activities	Lm											
OM200	Shoulder												
	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	No	No	No	No	No	No	No	No	No	No	No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm											required
OM201	(c) Holding Water	Lm	No	No	No	No	No	No	No	No	No	No	No Holding water found
OM202	Embankment Repair	No	No	No	No	No	No	No	No	No	No	No	No Embankment Repair Required
	Other Activite (Raincut)												Defects rectified within stipulated time
OM 300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	No Required
OM302	Culvert Cleaning	Lm	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	No Required

EXECUTIVE ENGINEER
Rural Works Division

Signature of Contractor/Authorized representative

Appendix

Executive Engineer, Rural Work Department,

Work Division, Jehanabad

Work Division, Jember
EXECUTIVE ENGINEER

Rural Works Department

Yorks Division Phulparas

2/1/2020
