

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 468 / नरकटियागंज, दिनांक- 11/03/2025

प्रेषक,

ई0 मनीष कुमार
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण नीति-2018 (MR-3054)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय:- MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) New Maintenance Policy 2018 अन्तर्गत पथ:-


1. KATHWALIA LORIA RD - BHIKHAMPUR
2. Chanpatia Dakhin Railway Gumti to Karnpatti PWD Kaithwaliya

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भरकर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



(ई0 मनीष कुमार)
कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज




Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

SL No.	Package No.	Name of Road	Project IS as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/WE/NA R/24/0007	KATHWALLA LORIA RD - BIIKHAMPUR	31808802089	<u>1086</u> <u>01-03-2024</u>	2.25	137.38000	106.09353	19.68375	<u>13/2024-25</u> <u>01/10/2024</u>	30.06.2025		2905	SDBC-25MM	5%	0.00000	0.00000	92.11671	Surface Complete
2	RM/WE/NA R/24/0007	Chanpatia Dakhin Railway Gumti to Karnpatti PWD Kaithwaliya	318891034668	<u>1086</u> <u>01-03-2024</u>	1.70	108.88000	85.73195	15.17830	<u>13/2024-25</u> <u>01/10/2024</u>	30.06.2025		2820	SDBC-25MM	5%	0.00000	0.00000	85.67485	Surface Complete


Executive Engineer
Rural Works Department
Works Division Narkatiaganj



Scanned with OKEN Scanner

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Chanpatia Dakhin Railway Gumti to Karnpatti PWD Kaithwaliya.
Name of Scheme :-MR 3054 New Maintenance Policy 2018
Name of Contractor : Chanda SHahi
Length of Road :- 1.700 KM
Project ID :- 318891034668
Package No. :- RM/WE/NAR/24/0007
Name of Block :- Chanpatia

Certified that all item wise 100% measurement has been taken by me

R. D. S.
08/03/25

JE

Certified that all item wise 50% measurement has been verified by me

P. S.
08/03/25

AE

Certified that all item wise 10% measurement has been verified by me

M.
11/3/25


EE



OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- KATHWALIA LORIA RD - BHIKHAMPUR
Name of Scheme :-MR 3054 New Maintenance Policy 2018
Name of Contractor : Chanda Shahi
Length of Road :- 2.250 KM
Project ID :- 31808802089
Package No. : - RM/WE/NAR/24/0007
Name of Block :- Chanpatia

Certified that all item wise 100% measurement has been taken by me


08/03/25

JE

Certified that all item wise 50% measurement has been verified by me


08/03/25

AE

Certified that all item wise 10% measurement has been verified by me


11/3/25

EE



Name of Road-Chanpatia Dakhin Railway Gumti to Karnpatti PWD Kaithwalia (Sec-47)

Date	Time	Section No.	Length In km	Bumps In mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
08/03/25	11:7:0	47	0.1	250	0	2500	2970	G	26.97545	84.63621	Normal
08/03/25	11:8:0	47	0.1	260	20.2	2600	3069	G	26.97582	84.63713	Normal
08/03/25	11:8:0	47	0.1	210	30.3	2100	2577	G	26.97534	84.63796	Normal
08/03/25	11:9:0	47	0.1	240	20.2	2400	2872	G	26.97459	84.63834	Normal
08/03/25	11:9:0	47	0.1	280	20.2	2800	3265	G	26.97376	84.63795	Normal
08/03/25	11:9:0	47	0.1	240	30.3	2400	2872	G	26.97293	84.6376	Normal
08/03/25	11:10:0	47	0.1	250	10.1	2500	2970	G	26.97215	84.63753	Normal
08/03/25	11:10:0	47	0.1	230	20.2	2300	2773	G	26.97174	84.63838	Normal
08/03/25	11:10:0	47	0.1	250	20.2	2500	2970	G	26.97094	84.63861	Normal
08/03/25	11:10:0	47	0.1	240	20.2	2400	2872	G	26.97025	84.63924	Normal
08/03/25	11:10:0	47	0.1	190	10.1	1900	2380	G	26.96986	84.64018	Normal
08/03/25	11:11:0	47	0.1	210	10.1	2100	2577	G	26.97013	84.64104	Normal
08/03/25	11:11:0	47	0.1	220	10.1	2200	2675	G	26.96996	84.64195	Normal
08/03/25	11:11:0	47	0.1	230	10.1	2300	2773	G	26.96991	84.643	Normal
08/03/25	11:11:0	47	0.1	210	10.1	2100	2577	G	26.96979	84.64398	Normal
08/03/25	11:12:0	47	0.1	200	10.1	2000	2478	G	26.97013	84.64498	Normal
08/03/25	11:12:0	47	0.1	270	10.1	2700	3167	G	26.97003	84.64592	Normal
Average IRI Value=							2820				

R. D. S.
J.E.
08/03/25

P. D. S.
08/03/25

08/03/25



Name of Customer:	Chanda Shahi
Name of Work/ Road:	Dargah Sahib, Jalandhar
Lab Job number:	
Date:	08.03.2025
Section No.	47

Test Date :	08.03.2025	Road Name :	Chapra Dohri Bypass, Gauraha, Kargali P.S., Dibrugarh				
Machine No :	472	Road Type :	(R) RURAL ROAD				
Start S No :		Side :		Interval			
Start E No :							
Weather :		UV Range :	1717	To	4000	1000	mm/km
Start Location :		Dist Range :	0	To	0.9	0.1	• 1000 m
End Location :		Equation :	$Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$				


Print Generale Report and Graph

Redraw Graph

Map View

File: F:\22021147.Xls, Section No.: 47, Eqn. $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : Chanda Shahi, **Name of Work/Road :** Chanpatia Dakhin Railway Gumti to Karpatti PWD Karthwariya, **Lab Job number :**

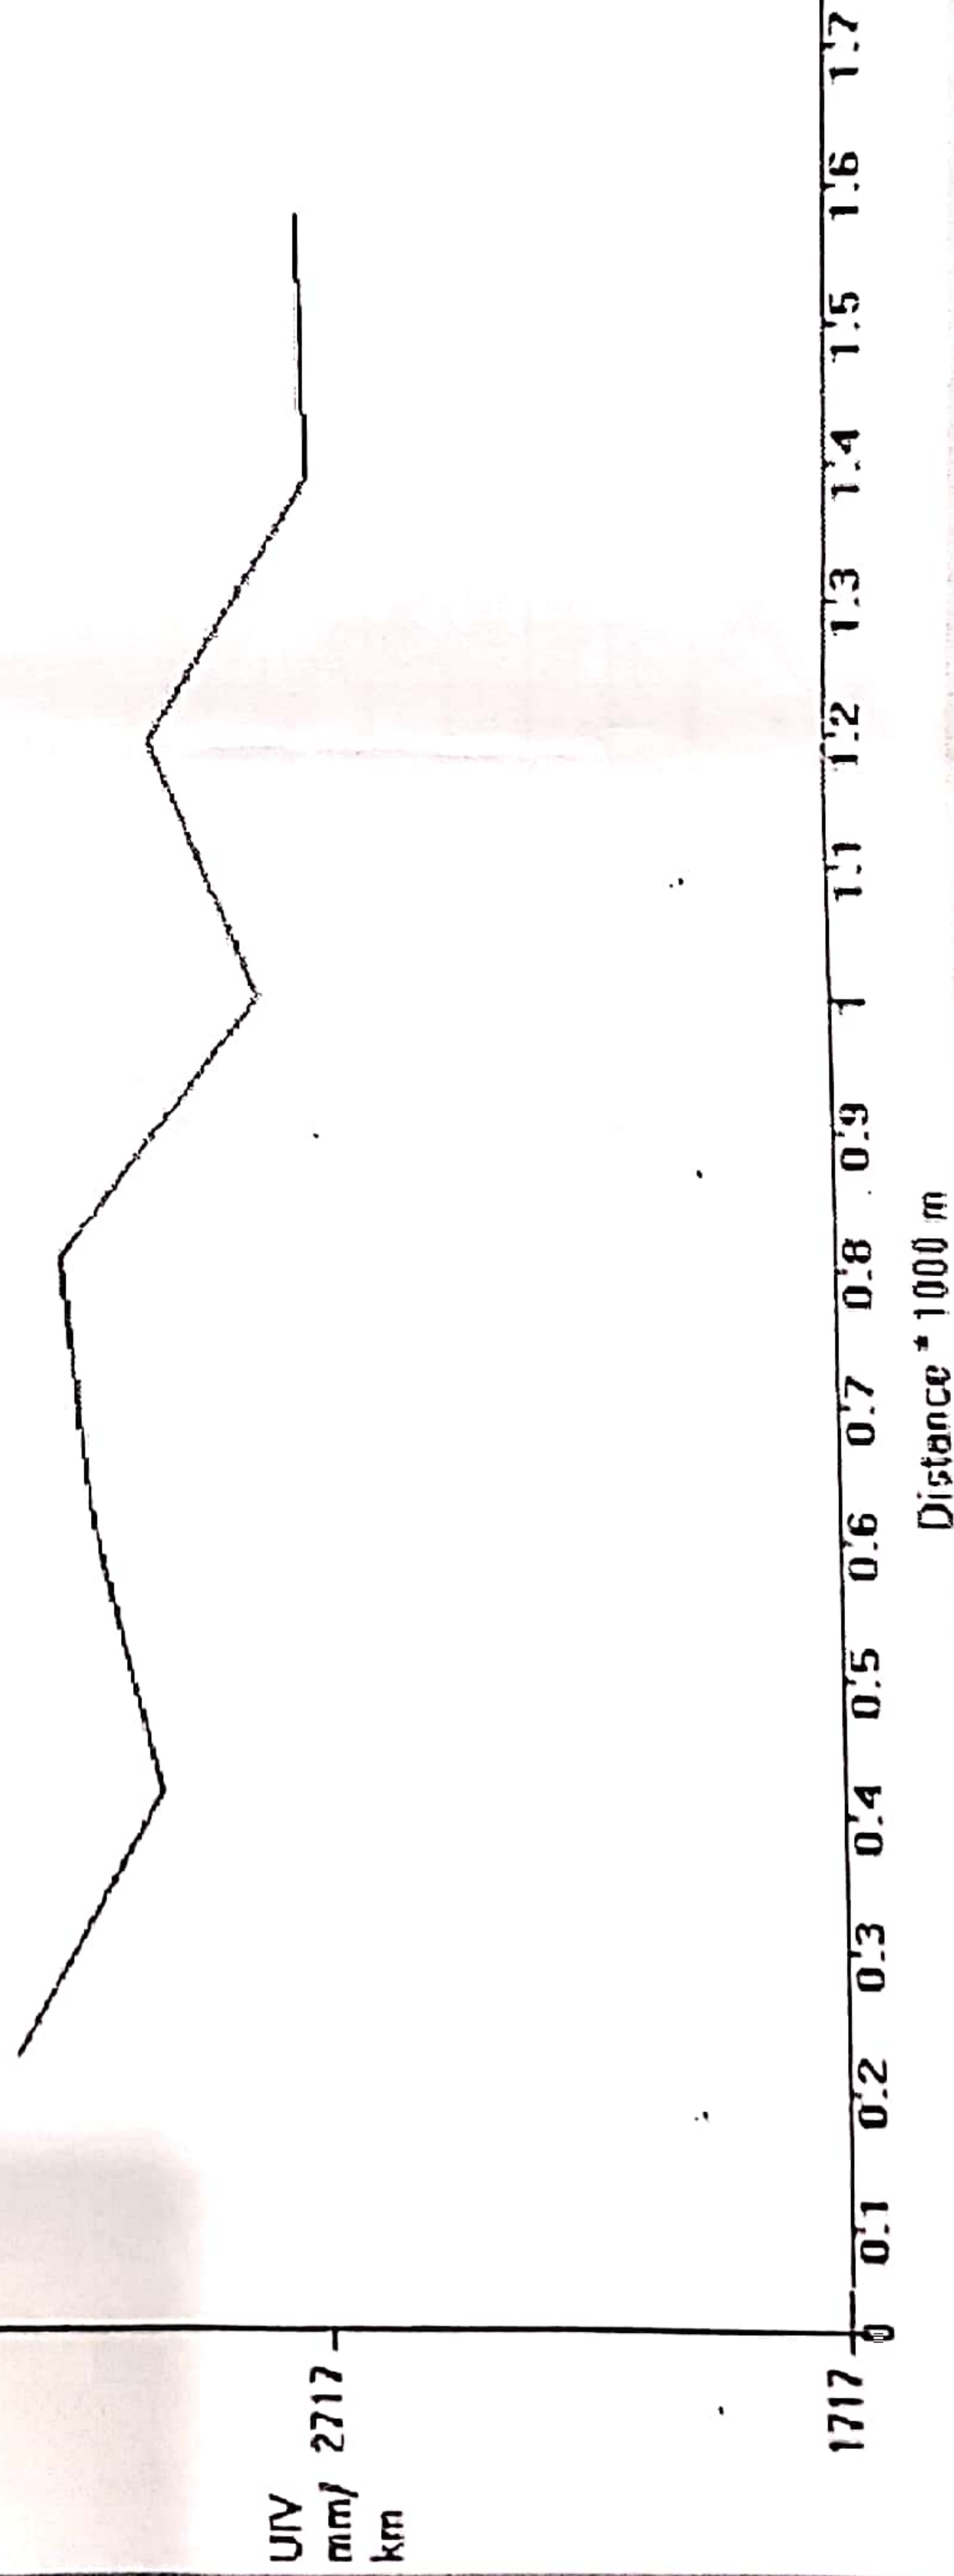

08/02/25

4/3/80

11/3/11

Name of Customer :	Chanda Shahi
Name of Work/Road :	KATHWALIA LORIA RD - BHIKHAMPUR
Lab Job number :	
Date :	08-03-2025
Section No. :	45


Test Date :	08-03-2025	Road Name :	KATHWALIA LORIA RD - BHIKHAMPUR
Machine No :	472	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UIV Range :	1579 To 4000 mm/km
Start Location :		Dist Range :	0 To 2.7
End Location :		Equation :	$Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

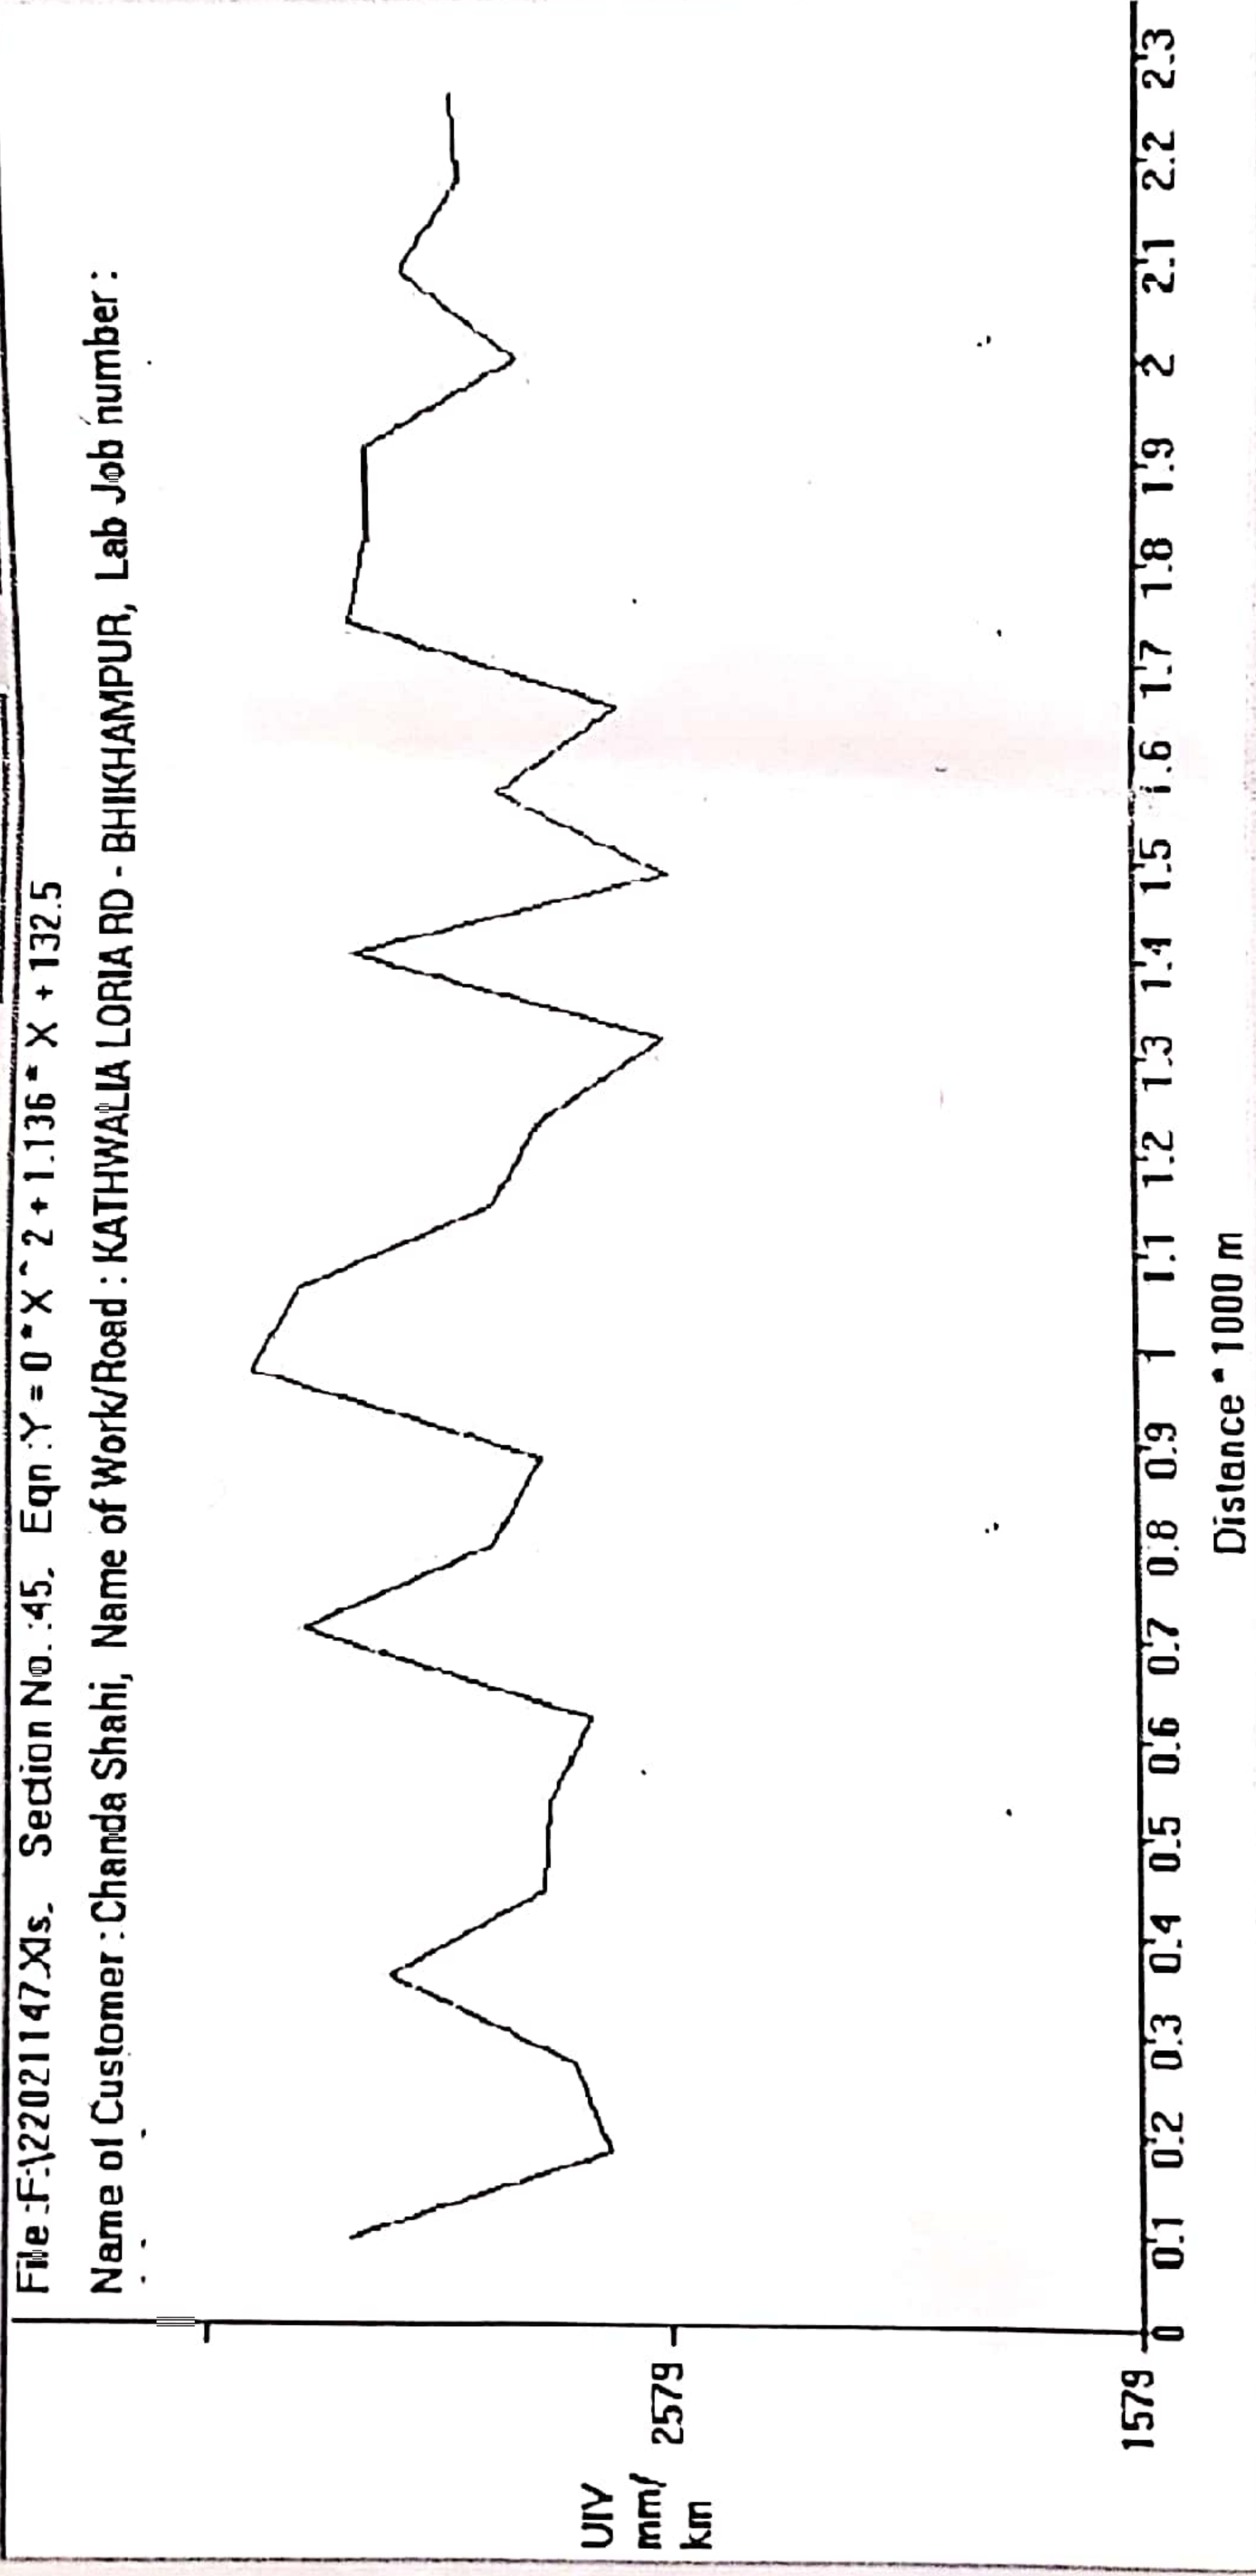

08/03/25

08/03/25

08/03/25

File

Name of Road - KHANAWALIA LORIA RD - BHIKHAMPUR (Sec-45)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	In km	In mm	Rate	mm/km	mm/km	ROAD			
08/03/25	9:58:11	45	0.1	330	0	3300	3272	G	26.913232	84.591665	Normal
08/03/25	9:58:11	45	0.1	270	21.3	2700	2714	G	26.912773	84.592542	Normal
08/03/25	9:58:11	45	0.1	280	21.3	2800	2788	G	26.912362	84.593338	Normal
08/03/25	9:58:47	45	0.1	320	31.4	3200	3188	G	26.911957	84.594528	Normal
08/03/25	9:59:22	45	0.1	290	21.3	2900	2853	G	26.911147	84.597962	Normal
08/03/25	10:0:0	45	0.1	280	21.3	2800	2841	G	26.911103	84.598838	Normal
08/03/25	10:0:32	45	0.1	270	21.3	2700	2749	G	26.910687	84.599713	Normal
08/03/25	10:1:8	45	0.1	340	11.2	3400	3377	G	26.910225	84.600538	Normal
08/03/25	10:1:8	45	0.1	300	21.3	3000	2958	G	26.909668	84.601245	Culvert
08/03/25	10:1:8	45	0.1	290	21.3	2900	2853	G	26.909328	84.602188	Normal
08/03/25	10:1:43	45	0.1	350	21.3	3500	3482	G	26.908918	84.602995	Normal
08/03/25	10:1:43	45	0.1	340	11.2	3400	3377	G	26.908358	84.603855	Normal
08/03/25	10:2:0	45	0.1	300	21.3	3000	2958	G	26.907668	84.604477	Normal
08/03/25	10:2:18	45	0.1	290	21.3	2900	2853	G	26.906953	84.60508	Normal
08/03/25	10:2:18	45	0.1	260	24.3	2600	2586	G	26.906253	84.605773	Normal
08/03/25	10:2:18	45	0.1	330	26.2	3300	3272	G	26.90563	84.606515	Normal
08/03/25	10:2:18	45	0.1	260	24.5	2600	2579	G	26.905163	84.607272	Normal
08/03/25	10:2:54	45	0.1	300	24.7	3000	2951	G	26.904698	84.608147	Normal
08/03/25	10:3:0	45	0.1	270	24.2	2700	2684	G	26.90425	84.608988	Normal
08/03/25	10:3:29	45	0.1	330	24.2	3300	3272	G	26.90385	84.609915	Normal
08/03/25	10:3:29	45	0.1	320	31.4	3200	3228	G	26.903457	84.61079	Normal
08/03/25	10:4:4	45	0.1	320	31.4	3200	3226	G	26.90295	84.611615	Normal
08/03/25	10:4:4	45	0.1	290	22.5	2900	2895	G	26.902387	84.612322	Normal
Average IRI Value=							2905				

08/13/25

R.D. 08/10/25
J.E.
