

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक- ५३५

दिनांक- २५.०३.२५

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति २०१८" (३०५४-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(३०५४) "नई अनुरक्षण नीति २०१८" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(३०५४) "नई अनुरक्षण नीति २०१८" योजनान्तर्गत पथ:-


१. L036 to Mahamadwa (VR48)

का कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज
२५.०३.२५

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No.	Package No.	Name of Road	Project IS as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percent age	Previous Total Allotted Amount (in lakh)	up-to-date expenditure against work done (in lakh)	Requisition on work against work (in lakh)	Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/WE/NA R24/0005	L036 to Mahamadwa (VR48)	31808902171	6115 04/12/2023	2.470	108.78000	60.40063	18.41635	16/2024-25 23.10.2024	22.07.2025		2820	SDBC-25MM	5%	0.00000	0.00000	85.98516	Surface Complete


Executive Engineer
Rural Works Department
Works Division Narkatiaganj



OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- L036 to Mahamadwa (VR48)
Name of Scheme :-MR 3054 New Maintenance Policy 2018
Name of Contractor : KHURSHID ALAM
Length of Road :- 2.47 KM
Project ID :- 31808902171
Package No. : - RM/WE/NAR/24/0005
Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


JE

Certified that all item wise 50% measurement has been verified by me

AE

Certified that all item wise 10% measurement has been verified by me


EE

Name of Customer :	Khurshid Alam
Name of Work/ Road :	L036 to Mahamadwa (VR48)
Lab Job number :	
Date :	15-01-2025
Section No. :	18

Print Generate Report and Graph


Test Date :	15-01-2025	Road Name :	L036 to Mahamadwa (VR48)
Machine No. :	472	Road Type :	(R) RURAL ROAD
Start S No. :		Side :	
Start E No. :		Interval :	
Weather :		UV Range :	1380 To 4000 mm/Km
Start Location :	0000	Dist Range :	0 To 2 0.1 1000 m
End Location :	1880	Equation :	$Y=0 \cdot X^2 + 1.021 \cdot X - 31.77$

Redraw Graph

Map View

File : F:\16041123.xls, Section No. : 18, Egn : $Y=0 \cdot X^2 + 1.021 \cdot X - 31.77$

Name of Customer : Khurshid Alam, Name of Work/ Road : L036 to Mahamadwa (VR48), Lab Job number :

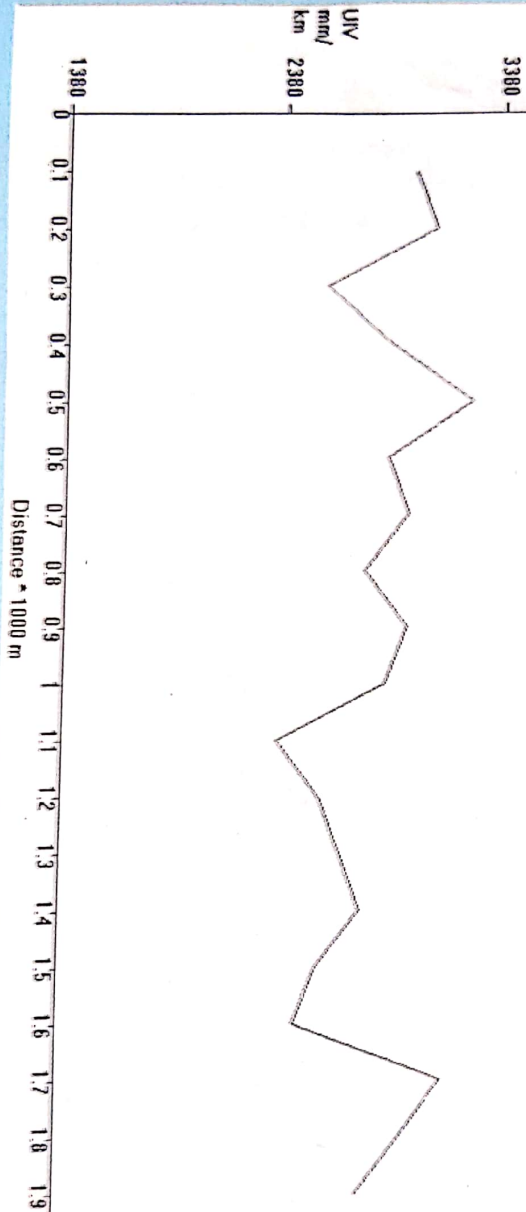

Name of Road - L036 to Mahamadwa (VR48) (Sec-18)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
15/1/25	9:7:0	18	0.1	250	0	2500	2970	G	26.97545	84.63621	Normal
15/1/25	9:8:0	18	0.1	260	20.2	2600	3069	G	26.97582	84.63713	Normal
15/1/25	9:8:0	18	0.1	210	30.3	2100	2577	G	26.97534	84.63796	Normal
15/1/25	9:9:0	18	0.1	240	20.2	2400	2872	G	26.97459	84.63834	Normal
15/1/25	9:9:0	18	0.1	280	20.2	2800	3265	G	26.97376	84.63795	Normal
15/1/25	9:9:0	18	0.1	240	30.3	2400	2872	G	26.97293	84.6376	Normal
15/1/25	9:10:0	18	0.1	250	10.1	2500	2970	G	26.97215	84.63753	Normal
15/1/25	9:10:0	18	0.1	230	20.2	2300	2773	G	26.97174	84.63838	Normal
15/1/25	9:10:0	18	0.1	250	20.2	2500	2970	G	26.97094	84.63861	Normal
15/1/25	9:10:0	18	0.1	240	20.2	2400	2872	G	26.97025	84.63924	Normal
15/1/25	9:10:0	18	0.1	190	10.1	1900	2380	G	26.96986	84.64018	Normal
15/1/25	9:11:0	18	0.1	210	10.1	2100	2577	G	26.97013	84.64104	Normal
15/1/25	9:11:0	18	0.1	220	10.1	2200	2675	G	26.96996	84.64195	Normal
15/1/25	9:11:0	18	0.1	230	10.1	2300	2773	G	26.96991	84.643	Normal
15/1/25	9:11:0	18	0.1	210	10.1	2100	2577	G	26.96979	84.64398	Normal
15/1/25	9:12:0	18	0.1	200	10.1	2000	2478	G	26.97013	84.64498	Normal
15/1/25	9:12:0	18	0.1	270	10.1	2700	3167	G	26.97003	84.64592	Normal
15/1/25	9:13:0	18	0.1	250	10.1	2500	2970	G	26.96955	84.64678	Normal
15/1/25	9:13:0	18	0.1	230	20.2	2300	2773	G	26.96931	84.64768	Normal
Average IRI Value=							2820				

Handwritten notes and signatures in the top left corner, including dates like 15/1/25 and 15/1/25, and signatures.
