

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, झाझा (जमुई)।

मोबाइल न०- 8986915861 ईमेल- rwdjhajha0@gmail.com

पत्रांक- 1307 / झाझा दिनांक- 29.06.2020

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल झाझा।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- 3054(MR)/ नई अनुरक्षण नीति 2018 के अंतर्गत कराये गए निम्न कार्यों के विरुद्ध में आवंटन उपलब्ध कराने के सम्बन्ध में।


महाशय,

उपरोक्त विषय के सम्बन्ध में सूचित करना है कि 3054(MR) / "नई अनुरक्षण नीति 2018" के अंतर्गत (1) Fatehpur More- Ranikura, (2) Dhamna- Jhajha Path Near Harhanja-Chhapa (3) Jagitila More-Jogitila (4) Harhanja-sidhesari एवं (5) Pargaha More To Bhikha Road का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः सादर अनुरोध है कि शीघ्र आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, झाझा।

RWD Works Division, Jhajha (Dist :- Jamui)

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road " New Maintenance Policy 2018" (Initial Rectification and Surface Renewal)

Name of Division:- Jhajha																			
Slr	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)		Agreement Amount (in Lakh)			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI in MM/M	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content (in %)	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (K.M)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	MR-N/19-20 JHAJHA/17	Fatehpur More- Rankura	20804102051	3030 & 16.07.2019	1.166	36.088	20.15227	10.2202	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	26.06.2020	3098	25	5.20	0	0	20.15227	Surface Completed	
2	MR-N/19-20 JHAJHA/17	Dhamna- Jhajha Path Near Harhanja-Chhapa	MR222060742	3030 & 16.07.2019	2.00	61.768	34.50624	17.50013	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	25.06.2020	2897	25	5.00	0	0	34.50624	Surface Completed	
3	MR-N/19-20 JHAJHA/17	Jagtila More-Jogtila	20804102058	3030 & 16.07.2019	1.054	35.448	20.33030	9.44968	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	27.06.2020	3244	25	5.04	0	0	20.33030	Surface Completed	
4	MR-N/19-20 JHAJHA/18	Harhanja-sudhesari	20804102055	3030 & 16.07.2019	1.244	38.812	21.44434	11.25153	05/MBD/MR-N/2020-21 & 18.05.2020	17.02.2021	24.06.2020	3062	25	5.14	0	0	21.44434	Surface Completed	
5	MR-N/19-20 JHAJHA/18	Pargaha More To Bhitha Road	20804101064	3030 & 16.07.2019	1.700	53.877	30.54199	14.75923	05/MBD/MR-N/2020-21 & 18.05.2020	17.02.2021	25.06.2020	3132	25	5.04	0	0	30.54199	Surface Completed	

KPK
19/6/2020
Executive Engineer
RWD Works Division, Jhajha

Name of Road :- Dhamna- Jhalha Path Near Harhanja-Chhapa (Length:- 2.00 KM)

Date	Time	Section No.	Length In km	Bumps In mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
28/6/20	13:21:0	9	0.1	210	10.1	2100	2112	G	2.94	24.8238	86.39441	Normal
28/6/20	13:21:0	9	0.1	240	20.2	2400	2418	G	3.32	24.8243	86.3937	Normal
28/6/20	13:22:0	9	0.1	280	20.2	2800	2827	G	3.82	24.82482	86.39276	Culvert
28/6/20	13:22:0	9	0.1	330	20.2	3300	3337	G	4.42	24.82536	86.39197	Normal
28/6/20	13:22:0	9	0.1	350	20.2	3500	3541	G	4.66	24.82595	86.3913	Normal
28/6/20	13:22:0	9	0.1	360	20.2	3600	3643	G	4.78	24.82617	86.39032	Normal
28/6/20	13:23:0	9	0.1	310	30.3	3100	3133	G	4.18	24.82651	86.38941	Normal
28/6/20	13:23:0	9	0.1	300	30.3	3000	3031	G	4.06	24.82642	86.38848	Normal
28/6/20	13:23:0	9	0.1	270	30.3	2700	2724	G	3.69	24.82653	86.38742	Normal
28/6/20	13:23:0	9	0.1	250	20.2	2500	2520	G	3.44	24.82663	86.38648	Normal
28/6/20	13:24:0	9	0.1	250	20.2	2500	2520	G	3.44	24.82693	86.38562	Normal
28/6/20	13:24:0	9	0.1	350	20.2	3500	3541	G	4.66	24.82693	86.38461	Normal
28/6/20	13:24:0	9	0.1	260	30.3	2600	2622	G	3.57	24.82669	86.38365	Normal
28/6/20	13:24:0	9	0.1	270	30.3	2700	2724	G	3.69	24.8263	86.38274	Normal
28/6/20	13:25:0	9	0.1	240	30.3	2400	2418	G	3.32	24.82647	86.38177	Normal
28/6/20	13:25:0	9	0.1	220	20.2	2200	2214	G	3.07	24.82703	86.38096	Speed Breaker
28/6/20	13:25:0	9	0.1	390	10.1	3900	3950	G	5.14	24.82711	86.38015	Normal
28/6/20	13:26:0	9	0.1	220	30.3	2200	2214	G	3.07	24.82724	86.37911	Normal
28/6/20	13:26:0	9	0.1	330	30.3	3300	3337	G	4.42	24.82737	86.37816	Normal
28/6/20	13:26:0	9	0.1	310	20.2	3100	3133	G	4.18	24.82771	86.37717	Normal

$$Y = 0 * X^2 + 1.021 * X - 31.77$$

$$X = 0$$

$$Y = -32$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

Handwritten signature
 29/6/2020

**Executive Engineer
 Rural Works Department
 Works Division, Jharkhand**

Name of Customer : Rajeev Kumar
 Name of Work/ Road : Dharmajikha Path Near Harhanja-Chhapra
 Lab Job number :
 Date : 6/28/2020
 Section No. : 9


Test Date : 6/28/2020
 Machine No : 385
 Start S No :
 Start E No :
 Weather :
 Start Location : 2.00
 End Location : 0.00
 Road Name : Path Near Harhanja-Chhapra
 Road Type : (R) RURAL ROAD
 Side :
 UV Range : 1112 To 5000 mm/km
 Dist Range : 0 To 21
 Equation : $Y = 0 \cdot X^2 + 1.021 \cdot X - 31.77$

Print

Redraw Graph

Map View

File : G:\Bump Machine\28.06.20\Harhanja-Chhapra\End to 0\28061553.xls, Section No. : 9, Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Name of Work/ Road : Lab Job number :

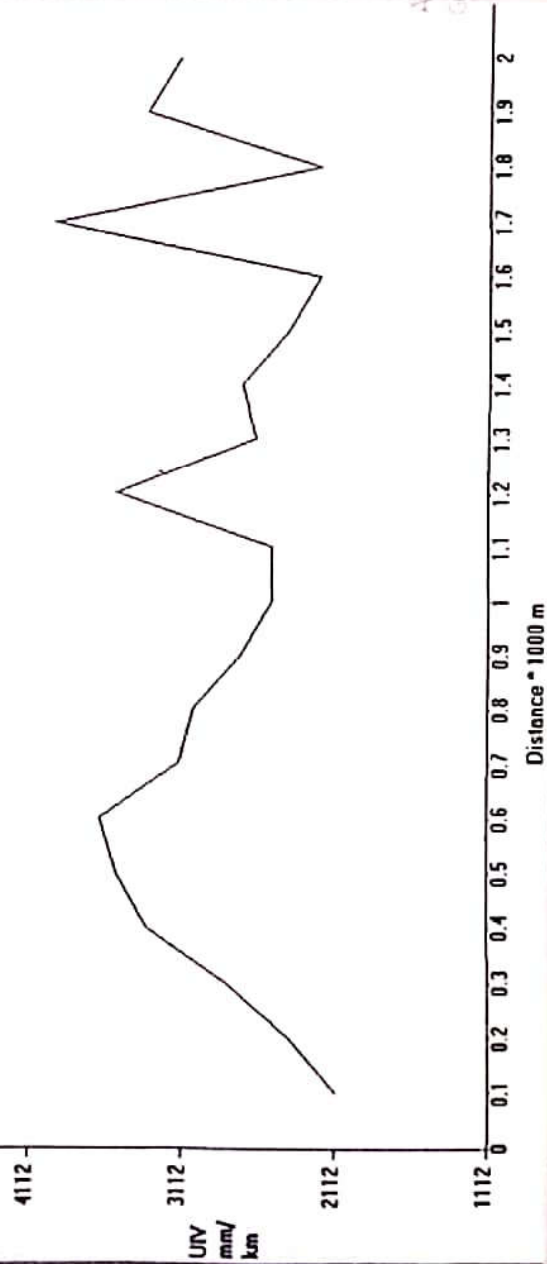

Signature
 27/6/2020
 Executive Engineer
 Rural Works Department
 Works Division, Jharkhand
