

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सासाराम-1

Email ID:-ee.rwd.sasaram1@gmail.com

Mob:- 8986915310

पत्रांक..... 221 अड्डा सासाराम/दिनांक 08.02.2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सासाराम-1

सेवामें,

नोडल पदाधिकारी (MR 3054)
ग्रामीणकार्यविभाग
पटना, बिहार


विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु० :- यथोक्त।

विष्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सासाराम-1


8/02/21

EXECUTIVE ENGINEER
R.W.D. WORKS DIV. SASARAM-1

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)


Form of Utilization Certificate up to Feb 2021


Sl.No	Name of Scheme	Sanction No.&Date With Amount (In lace Rs.)	Amount Received (In lace Rs.)	Particulars
1	Construction of Rural roads Under MR	New Maintenance Policy-2018 MR (3054) BRRDA PATNA Letter No.82, dt. 13.11.2020 Letter No.84, dt. 26.11.2020 Letter No.86, dt. 11.12.2020 Letter No.05, dt. 12.01.2021	24012800.00 19457900.00 65864300.00 142175100.00	Certified that out of Rs. 25,15,10,100.00 lakh of grants-in-aid sanctioned during the years 2020-21 Infavor of EE,RWD works division Sasaram-1 a sum of Rs 187759733.00 lakh has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 63750362.00 lakh remaining unutilized at the end of the period under report.
	Total:		25,15,10,100.00	

2. Certified that I have satisfied my self that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:-

- i. Works have been supervised by Executive Engineer/ Superintending Engineer.
 - ii. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
 - v. All other caudal formalities have been observed.
3. **Physical Progress achieved:-**
- i. Construction of Road Works.
 - ii. Construction of CD works.


Divisional Accounts Officer
R.W.D, works Division
Sasaram-1


Executive Engineer
R.W.D, works Division
Sasaram-1

EXECUTIVE ENGINEER
R.W.D. WORKS DIV. SASARAM-1

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, SASARAM-1

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- Sasaram-1

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	20	PWD Road to Tendua Village	10301008181	3021 16.07.2019	2.830	115.20200	70.281	26.32725	10/MBD/ 2020-21 24.02.20	23.10.2020	-	2415	25.00	5.01	42.16860	42.16860	28.11240	
Total					2.830	115.20200	70.281	26.32725							42.16860	42.16860	28.11240	

Divisional Accounts Office
Rural Works Department,
Works Division, Sasaram-1

Executive Engineer
Rural Works Department
Works Division, Sasaram-1

EXECUTIVE ENGINEER

SD/ DIV. ENGINEER-M-1

Name of Road : PWD Road to Tendua Village

Date	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	ongitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
11/12/20	18:39:34	58	0.1	250	21.3	2500	2915	G	24.8623	83.95921	Normal
11/12/20	18:40:0	58	0.1	180	20.2	1800	2215	G	24.86316	83.95879	Normal
11/12/20	18:40:05	58	0.1	180	25.3	1700	2315	G	24.86522	83.95916	Normal
11/12/20	18:40:18	58	0.1	260	10.1	2600	3015	G	24.86346	83.95793	Normal
11/12/20	18:40:46	58	0.1	230	22.5	2300	2715	G	24.86392	83.957	Normal
11/12/20	18:41:22	58	0.1	200	10.1	2000	2415	G	24.86465	83.9566	Normal
11/12/20	18:41:22	58	0.1	200	20.2	2000	2415	G	24.86519	83.95658	Normal
Total			0.7								

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 2000$$

$$Y = 2415$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

11/12/20
DIRECTOR
A. W. D. (W) DIV. BANGOR

Name of Customer : Basant Kumar
Name of Work/Road : PWD Road to Tendua Village
Lab Job number : 58
Date : 11/12/2020
Section No. : 58

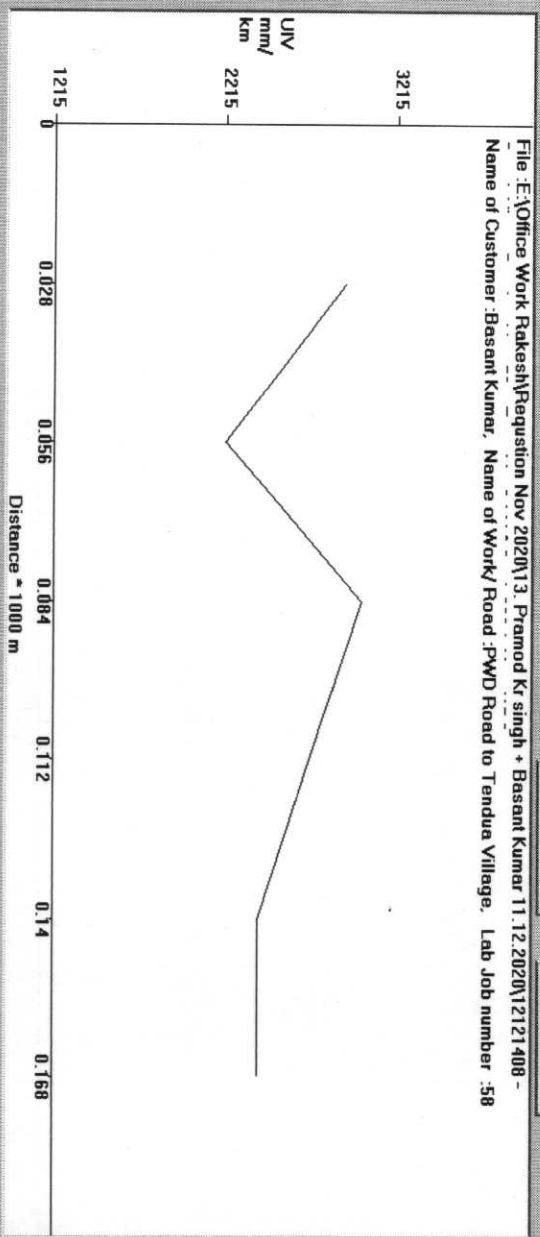
Test Date : 11/12/2020
Machine No. : 391
Start S No. : 5555
Start E No. : 5560
Weather : Normal
Start Location : 24.8623, 83.95
End Location : 24.86519, 83.9
Road Name : PWD Road to Tendua Village
Road Type : (F) RURAL ROAD
Side : Sasaram
U/V Range : 1215 To 4000
Dist Range : 0 To 0.196
Equation : $Y = 0 + X^2 + 1.000 * X + 415.2$

Print

Generate Report and Graph

Redraw Graph

Map View



W. D. (W) Div. Sasaram
 Executive Engineer
 11/12/2020

Name of Road : PWD Road to Tendua Village

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
11/ 12/ 20	18: 43: 0	59	0.1	280	16.4	2800	3215	G	24.86652	83.95643	Normal
11/ 12/ 20	18: 43: 10	59	0.1	200	10.1	2000	2415	G	24.86743	83.95621	Normal
11/ 12/ 20	18: 43: 46	59	0.1	260	22.3	2600	3015	G	24.86825	83.95591	Normal
11/ 12/ 20	18: 44: 0	59	0.1	150	24.1	1500	1915	G	24.86835	83.95582	Normal
Total			0.4								

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 1500$$

$$Y = 1915$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

ms 12/12/20
Executive Engineer
A.W.D.(V) Div. Engineer

Name of Customer : Basant Kumar
Name of Work/Road : PWD Road to Tendua Village
Lab Job number : 59
Date : 11/12/2020
Section No. : 59

Test Date : 11/12/2020
Machine No. : 391
Start S No. : 5561
Start E No. : 5564
Weather : Normal
Start Location : 24.86652, 83.9
End Location : 24.86835, 83.9
Road Name : PWD Road to Tendua Village
Road Type : (R) RURAL ROAD
Side : Sasaram
UIV Range : 915 To 4000
Dist Range : 0 To 0.14
Interval : 1000 mm/km
Equation : $Y = 0 * X^2 + 1.000 * X + 415.2$

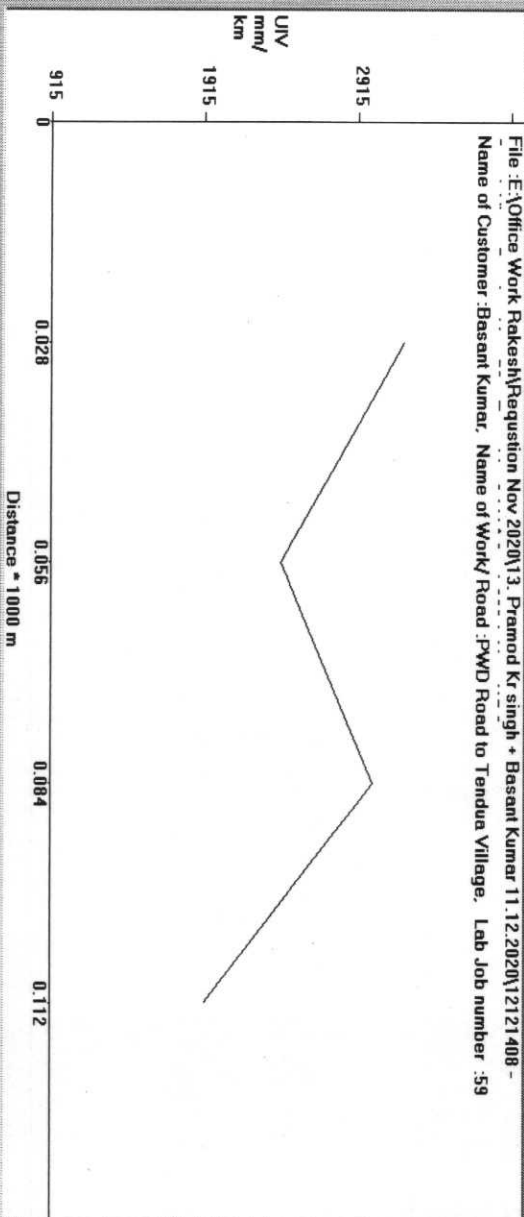
Print

Generate Report and Graph

Redraw Graph

Map View

File : E:\Office Work\Rakesh\Requstion Nov 2020\13. Pramod Kr singh + Basant Kumar 11.12.2020\12121408 -
 Name of Customer : Basant Kumar, Name of Work/Road : PWD Road to Tendua Village, Lab Job number : 59



Wd
 11/12/20
 Executive Engineer
 W.D. (W) Div. Sasaram

Name of Road : PWD Road to Tendua Village

Date	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
11/ 12/ 20	18: 58: 0	60	0.1	180	23.1	1800	2215	G	24.87064	83.95377	Normal
11/ 12/ 20	18: 58: 41	60	0.1	100	24.8	1000	1415	G	24.87151	83.9538	Normal
11/ 12/ 20	18: 59: 15	60	0.1	200	10.1	2000	2415	G	24.87239	83.95382	Normal
11/ 12/ 20	18: 59: 15	60	0.1	220	20.2	2200	2615	G	24.87331	83.95372	Normal
11/ 12/ 20	18: 59: 15	60	0.1	220	20.2	2200	2615	G	24.87421	83.95365	Normal
11/ 12/ 20	19: 0: 0	60	0.1	180	20.2	1800	2215	G	24.87509	83.95375	Normal
11/ 12/ 20	19: 0: 0	60	0.1	160	20.2	1600	2015	G	24.87601	83.95364	Normal
11/ 12/ 20	19: 0: 26	60	0.1	210	22.3	2100	2515	G	24.87688	83.953	Normal
11/ 12/ 20	19: 1: 1	60	0.1	240	10.1	2400	2815	G	24.8777	83.95311	Normal
11/ 12/ 20	19: 1: 1	60	0.1	150	14.2	1500	1915	G	24.87817	83.95251	Normal
11/ 12/ 20	19: 2: 0	60	0.1	220	10.1	2200	2615	G	24.87838	83.95162	Normal
11/ 12/ 20	19: 2: 12	60	0.1	110	20.2	1100	1515	G	24.87851	83.95061	Normal
11/ 12/ 20	19: 2: 12	60	0.1	130	10.1	1300	1715	G	24.87904	83.95017	Normal
11/ 12/ 20	19: 2: 22	60	0.1	130	13.4	1400	1315	G	24.87106	83.95017	Normal
11/ 12/ 20	19: 2: 47	60	0.1	180	20.2	1800	2215	G	24.87993	83.95123	Normal
11/ 12/ 20	19: 3: 0	60	0.1	130	10.1	1300	1715	G	24.8808	83.95047	Normal
11/ 12/ 20	19: 3: 0	60	0.1	180	22.3	1800	2215	G	24.8808	83.95059	Normal
Total			1.7								

W 12/12/20
Executive Engineer
S.D.(V) Div. Baranagar

Y = 0 * X ^ 2 + 1.000 * X + 415.2
X = 1800
Y = 2215
(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Name of Customer : Basant Kumar

Name of Work/ Road : PWD Road to Tendua Village

Lab Job number : 60

Date : 11/12/2020

Section No. : 60

Test Date : 11/12/2020

Road Name : PWD Road to Tendua Village

Machine No : 391

Road Type : (R) RURAL ROAD

Start S No : 5565

Side : Sasaram

Start E No : 5580

Interval : 1000

Weather : Normal

UVI Range : 415 To 4000

Start Location : 24.87064, 83.9

Dist Range : 0 To 0.476

End Location : 24.8808, 83.95

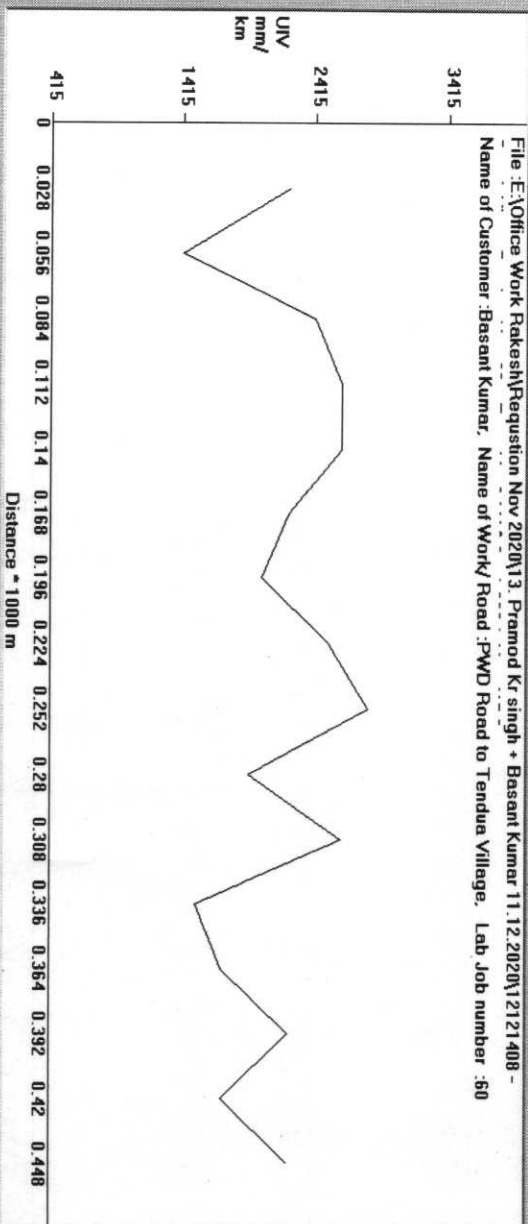
Equation : $Y = 0 * X^2 + 1.000 * X + 415.2$

Print

Generate Report and Graph

Redraw Graph

Map View



W. D. (V) Div. Sasaram
