

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

Email ID:-eerwdaurangabad1@gmail.com

Mob:- 8986915333

पत्रांक...437/अ... ..

औरंगाबाद/दिनांक...12/02/21...

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

[Signature]
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद
12/02/21

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/19/0024	Amba nabhnagar Road - Chakua	10602802022	3140/22.07.2019	6.5	203.08	122.37	12.05	74MIBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3401	25MM	5.041%	61.18500	61.18500	61.18500	Comp.
2	RM/AU/AUR/19/0030	Deo - Bahola	10602802105	3140/22.07.2019	6.52	211.88	130.92	59.68	58MIBD-2019-20 04.02.2020	03.11.2020	21.12.2020	3349	25MM	5.012%	65.46000	65.46000	65.46000	Comp.
3	RM/AU/AUR/19/0030	GT Rd Deo More - Rasalpur	10602802115	3140/22.07.2019	2.62	92.14	57.95	24.22	58MIBD-2019-20 04.02.2020	03.11.2020	17.12.2020	2875	25MM	5.063%	34.77000	34.77000	21.18000	Comp.
4	RM/AU/AUR/19/0031	Khairawan - Barawan	10602802121	3140/22.07.2019	2.07	76.02	48.85	18.91	61MIBD-2019-20 05.02.2020	04.11.2020	17.12.2020	3335	25MM	5.000%	29.31000	29.31000	19.54000	Comp.
5	RM/AU/AUR/19/0015	Deo Jeevabigha - Eroura	10602902011	3140/22.07.2019	1.56	59.49	39.87	13.60	78MIBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3199	25MM	5.014%	23.92200	23.92200	15.94800	Comp.
6	RM/AU/AUR/19/0033	AURANGABAD NABINAGAR ROAD - SORI	NEA22000214	3140/22.07.2019	2.2	71.85	44.54	20.04	80MIBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2961	25MM	5.000%	26.72600	26.72600	17.81400	Comp.
7	RM/AU/AUR/19/0033	Aurangabad Nabhnagar - Sonbarsa Khaira	10602802096	3140/22.07.2019	1.49	53.57	37.18	15.96	80MIBD-2019-20 20.02.2020	19.11.2020	28.11.2020	2988	25MM	5.000%	20.26800	20.26800	15.55000	Comp.
8	RM/AU/AUR/19/0034	Aurangabad Nabhnagar Rd. Charan Vajjapur Rajpur	10602802097	3140/22.07.2019	4.84	157.38	95.33	9.23	64MIBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2404	25MM	5.000%	57.19800	57.19800	38.13200	Comp.
9	RM/AU/AUR/19/0034	Charan Mali Road - Sanoura Khamba	10602802103	3140/22.07.2019	2.57	89.38	55.76	24.65	64MIBD-2019-20 05.02.2020	04.11.2020	18.12.2020	3012	25MM	5.000%	33.45600	33.45600	22.30400	Comp.
10	RM/AU/AUR/19/0010	Khaira to Gram Sonahi Road	10602901035	3140/22.07.2019	2.05	78.8	50.88	19.97	84MIBD-2019-20 25.02.2020	24.11.2020	13.11.2020	3548	25MM	5.011%	0.00000	0.00000	50.88000	Comp.
11	RM/AU/AUR/19/0027	Basudev Kenal to Tamshi village	10602901031	3140/22.07.2019	2.3	76.08	47.32	20.92	62MIBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2934	25MM	5.017%	28.39200	28.39200	18.92800	Comp.
12	RM/AU/AUR/19/0027	Amba Jiwa Bigha Road to Chorrha	10602901012	3140/22.07.2019	5.5	175.66	109.15	48.86	62MIBD-2019-20 05.02.2020	04.11.2020	24.12.2020	3837	25MM	5.093%	54.57500	54.57500	54.57500	Comp.
13	RM/AU/AUR/19/0036	AURANGABAD NABINAGAR ROAD SATTAR	NEA22000221	3140/22.07.2019	1.6	56.81	35.7	15.35	68MIBD-2019-20 08.02.2020	07.02.2020	28.11.2020	2655	25MM	5.195%	21.42000	21.42000	14.38000	Comp.
14	RM/AU/AUR/19/0032	Modernisation & Const of NH-2 Dadpi to deojara Rd via Mahawan art Rd	10602803009	3140/22.07.2019	6.8	258.417	153.52	63.19	69MIBD-2019-20 10.02.2020	09.11.2020	08.12.2020	2770	25MM	5.000%	76.76000	76.76000	76.76000	Comp.

15	RM/AU/AUR/ 19/0028	G.T. Road to Narkappi	10602802400	3140/22.07.2019	4.1	165.66	110.98	42.81	80MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3016	25MM	5.000%	55.49000	55.49000	55.49000	Comp.
16	RM/AU/AUR/ 19/0009	Nabinagar Road - Kunrwa	10602902029	3140/22.07.2019	3.32	118.96	76.06	30.93	82MBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2986	25MM	5.042%	45.63600	45.63600	30.42400	Comp.
17	RM/AU/AUR/ 19/0028	Const of Rd from Madanpur NH-2 Ghorghat more to Ghorghat thawni Rd	10602801016	3140/22.07.2019	5	246.1	174.29	47.12	65MBD-2019-20 05.02.2020	04.11.2020	17.12.2020	2276	25MM	5.000%	87.14500	87.14500	87.14500	Comp.
18	RM/AU/AUR/ 19/0034	AURANGABAD NABINAGAR ROAD - GHAMHARIA	NEA22000211	3140/22.07.2019	1.6	50.44	31.92	13.36	64MBD-2019-20 05.02.2020	04.11.2020	18.12.20	3103	25MM	5.000%	19.15200	19.15200	12.76800	Comp.
19	RM/AU/AUR/ 19/0024	Const of Rd from Amba Nabinagar to persawan	10602801003	3140/22.07.2019	2.5	88.42	55.36	24.09	74MBD-2019-20 20.02.2020	19.11.2020	24.12.2020	2492	25MM	5.012%	33.21600	33.21600	22.14400	Comp.
20	RM/AU/AUR/ 19/0006	Const of Inda bigha pokhar to sokhya talab via western portion of naugrah	10602803011	3140/22.07.2019	3.8	148.32	97.33	36.07	05.02.2020 66MBD-2019-20	04.11.2020	03.11.2020	2125	25.00MM	5.009%	68.24400	65.24400	32.08600	Comp.
21	RM/AU/AUR/ 19/0012	L029 - T01 G.T.ROAD TO KUSA (TRACK29)	10602802064	3140/22.07.2019	5.76	203.59	130.86	52.30	20.02.2020 76MBD-2019-20	19.11.2020	19.12.2020	3071	25.00MM	5.020%	0.00000	0.00000	130.86000	Comp.
22	RM/AU/AUR/ 19/0036	Manjhiyawa Jsoiya Via Ankorha Railway Station raad	10602901065	3140/22.07.2019	7.4	274.03	175.78	70.63	08.02.2020 68MBD-2019-20	07.11.2020	20.11.2020	2574	25.00MM	5.077%	123.04600	123.04600	52.73400	Comp.
23	RM/AU/AUR/ 19/0032	GT Road - Narkappi	10602902016	3140/22.07.2019	3.85	139.12	88.96	36.22	10.02.2020 69MBD-2019-20	09.11.2020	17.11.2020	3225	25.00MM	5.096%	71.16800	71.16800	17.79200	Comp.
24	RM/AU/AUR/ 19/0031	khiriyawanpirthu - chei nawada	NEA22000208	3140/22.07.2019	6	314.39	223.55	56.35	05.02.2020 61MBD-2019-20	04.11.2020	26.11.2020	2556	25.00MM	5.002%	156.48500	156.48500	67.06500	Comp.
TOTAL																1009.916		

Divisional Accounts Officer
Rural Works Department, works Division,
Aurangabad

Executive Engineer
Rural Works Department
Works Division, Aurangabad

Name Of Road Charan Mali Road-Sonoura Khamba

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
18/12/20	18:43:23	67	0.1	220	20.2	2200	2631	G	3.58	24.758648	84.217473	Normal
18/12/20	18:44:0	67	0.1	330	10.1	3300	3881	G	5.06	24.757962	84.218047	Speed Breaker
18/12/20	18:44:34	67	0.1	220	30.3	2200	2631	G	3.58	24.757325	84.218737	Normal
18/12/20	18:45:9	67	0.1	230	30.3	2300	2745	G	3.72	24.756802	84.219528	Normal
18/12/20	18:45:44	67	0.1	230	20.2	2300	2745	G	3.72	24.756318	84.220252	Normal
18/12/20	18:46:0	67	0.1	210	30.3	2100	2518	G	3.44	24.755953	84.221093	Normal
18/12/20	18:46:19	67	0.1	250	30.3	2500	2972	G	3.99	24.75502	84.220875	Normal
18/12/20	18:46:19	67	0.1	240	30.3	2400	2858	G	3.85	24.7542	84.220707	Normal
18/12/20	18:46:19	67	0.1	250	20.2	2500	2972	G	3.99	24.753427	84.22116	Normal
18/12/20	18:47:0	67	0.1	320	30.3	3200	3767	G	3.93	24.753147	84.222137	Normal
18/12/20	18:47:0	67	0.1	250	30.3	2500	2972	G	3.99	24.752803	84.223047	Normal
18/12/20	18:47:0	67	0.1	230	30.3	2300	2745	G	3.72	24.752437	84.223922	Normal
18/12/20	18:47:0	67	0.1	270	30.3	2700	3199	G	3.26	24.752398	84.224948	Normal
18/12/20	18:47:29	67	0.1	200	30.3	2000	2404	G	3.3	24.752252	84.225992	Normal
18/12/20	18:47:29	67	0.1	320	20.2	3200	3767	G	3.93	24.752735	84.22648	Normal
18/12/20	18:47:29	67	0.1	280	20.2	2800	3313	G	3.4	24.753598	84.226648	Normal
18/12/20	18:48:4	67	0.1	290	20.2	2900	3426	G	3.53	24.753832	84.227373	Normal
18/12/20	18:48:4	67	0.1	260	30.3	2600	3086	G	3.13	24.753632	84.22835	Normal
18/12/20	18:48:40	67	0.1	320	30.3	3200	3767	G	3.93	24.753415	84.229343	Normal
18/12/20	18:48:40	67	0.1	240	20.2	2400	2858	G	3.85	24.753648	84.23005	Normal
18/12/20	18:50:25	67	0.1	280	30.3	2800	3313	G	4.4	24.763663	84.238113	Speed Breaker
18/12/20	18:57:24	67	0.1	280	20.2	2800	3313	G	3.4	24.763035	84.238602	Normal
18/12/20	18:58:0	67	0.1	210	20.2	2100	2518	G	3.44	24.762992	84.239578	Normal
18/12/20	18:58:0	67	0.1	230	30.3	2300	2745	G	3.72	24.76298	84.240555	Normal
18/12/20	18:58:0	67	0.1	180	30.3	1800	2177	G	3.02	24.763042	84.241565	Normal
18/12/20	18:58:34	67	0.1									

Total Length

2.5

[Signature]
18/12/20
J.E

[Signature]
21/12/20
A.E

E"E

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2536$$

$$Y = 3012$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Name of Customer : Ram Nandan Singh
Name of Work/ Road : Charan Mali Road - Sanoura Kh
Lab Job number : 67
Date : 18-12-2020
Section No. : 67


Test Date : 28-04-2010 Road Name : Charan Mali Road - Sanoura Kh
Machine No : 377 Road Type : (R) RURAL ROAD
Start S No : 53 Side : Nabinsagar Interval
Start E No : 77
Weather : Normal UV Range : 1177 To 5000 1000 mm/km
Start Location : 24.758648 84: Dist Range : 0 To 26 01 * 1000 m
End Location : 24.763042 84: Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

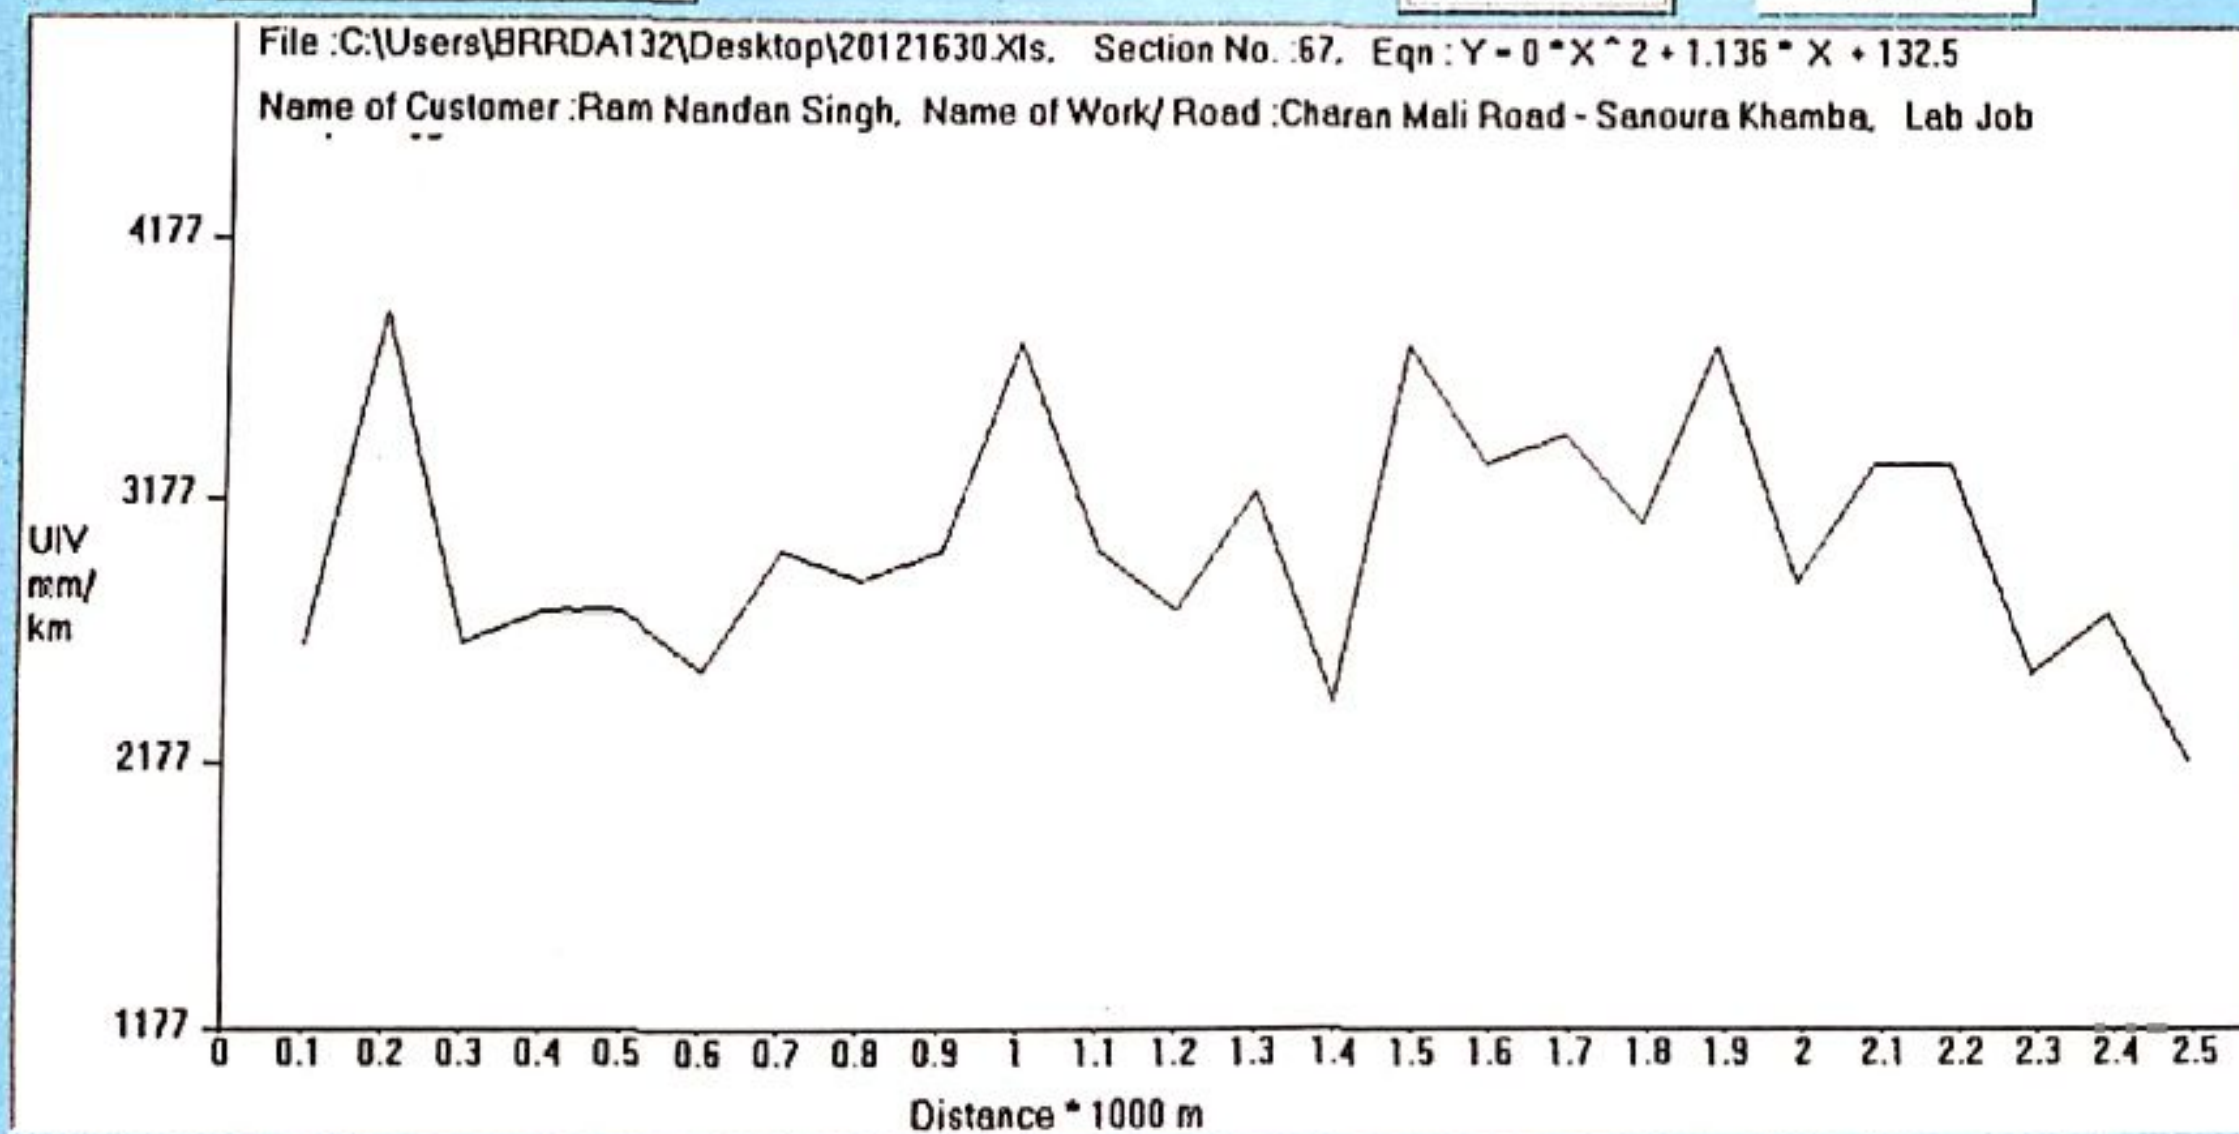

21/12/20
S-E

21/12/20

21/12/20



OM SAI CONSULTANTS

ISO 9001:2015 & ISO/IEC 17025:2017 CERTIFIED NABL ACCREDITED LAB
Address: - Bank of India Colony, Near Jal Street Gas Uddown, South DSS,
P.O.-B.V. College Raja Bazar, Pains-800014, Contact No. +919472909287
Email- omaiconsultantspatna@gmail.com
Per. No: OSC/17/01

TEST REPORT

Issue To:
EXECUTIVE ENGINEER
R.W.D., Works Division,
Aurangabad

Report No: OSC/BR/160620/24

Date of Receiving: 14/11/2020

Testing Period: 14/11/2020 TO 16/11/2020

Date of Reporting: 16/11/2020

Project Name: CONSTRUCTION OF ROAD FROM CHARAN MALI ROAD TO SANOURA KHAMBHA

Sample Description Semi Dense Bituminous Concrete (S.D.B.C.)

Sample Condition: Good (Packed in Bag).

BITUMEN CONTENT TEST

S. No.	Test Parameter	Test Method	Result	Requirements MORTH Specification Table- 500-7	Conformity
1.	Binder Content (%)	IRC SP-11	5.08	5.0 Min.	Yes

-----End of Report-----

Checked By



Authorized Signatory

1. The result listed refers only to the tested samples and applicable parameters endorsement of product is neither inferred nor implied.
2. Total Liability of our Lab. is limited to the invoiced amount.
3. Samples will be destroyed after 90 days from the date of issue of test report.
4. This report is not to be reproduced wholly or in part and cannot be used as an evidence in the court of law and should not be used in any advertising media without our special permission in writing.

NABL ACCREDITED
LABORATORY
