

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, झाझा (जमुई)।

मोबाइल न०- 8986915861 ईमेल- rwdjhajha0@gmail.com

पत्रांक- 45 / झाझा दिनांक- 07.1.2021

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल झाझा।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- 3054(MR)/ "नई अनुरक्षण नीति 2018" के अंतर्गत कराये गए निम्न कार्यों के विरुद्ध में आवंटन उपलब्ध कराने के सम्बन्ध में।


महाशय,

उपरोक्त विषय के सम्बन्ध में सूचित करना है कि 3054(MR) / "नई अनुरक्षण नीति 2018" के अंतर्गत (1) Nakta to sanghara via jhumarbad (2) Jhajha -Chakai PWD Road to Chakai Near Chahabacha Road. (3) Salaia - Gobraha (4) Telwa Bazar-Birajpur Road to Gadi Telwa Road via Nawadih Ghasitari. (5) Ekdara more to Fatehpur Road. (6) Baghwa - Madhopur-Salaiya PMGSY Road एवं (7) Chakai-Deoghar PWD Road to Ghormo Asram (Sahana kothi) chakai-Kiyajori Road का Surface कार्य पूर्ण हो चुका है। कार्यों के विरुद्ध भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः सादर अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०-यथोक्त।

विश्वासभाजन



07.1.2021

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, झाझा।

RWD Works Division, Jhajha (Dist :- Jamui)

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road " New Maintenance Policy 2018" (Initial Rectification and Surface Renewal)

Name of Division:- Jhajha																			
S.N	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)			Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI in MM/KM	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content (in %)	Previous Total Alloted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (K.M)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	MR-N/19-20 JHAJHA/19	Chakai-Deoghar PWD Road to Ghormo Asram (Sahana kothi) chakai-Kiyajori Road.	20804103003	3688 & 29.08.2019	1.50	51.025	30.06911	12.80478	08/M8D/MR-N/2020-21 & 19.05.2020	18.02.2021	02.01.2021	2607	25	5.02	0	0	30.06911	Surface Completed	


 Executive Engineer
 RWD Works Division, Jhajha

Road Name:- Chakai-Deoghar PWD road To Ghormo Asram (Sahana Kothi) Chakai- Kiyajori Road (Length-1.50 KM)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
4/1/21	16:42:0	55	0.1	260	0	2600	2589	G	3.53	24.5637	86.41801	Normal
4/1/21	16:42:29	55	0.1	320	20.2	3200	3147	G	4.2	24.56288	86.41742	Speed Breaker
4/1/21	16:43:4	55	0.1	220	10.1	2200	2217	G	3.07	24.56201	86.41712	Normal
4/1/21	16:43:4	55	0.1	300	20.2	3000	2961	G	3.98	24.56114	86.4171	Normal
4/1/21	16:43:4	55	0.1	320	20.2	3200	3147	G	4.2	24.56021	86.41715	Normal
4/1/21	16:43:40	55	0.1	250	30.3	2500	2496	G	3.41	24.55927	86.41722	Normal
4/1/21	16:44:0	55	0.1	260	20.2	2600	2589	G	3.53	24.55832	86.41729	Normal
4/1/21	16:44:15	55	0.1	270	20.2	2700	2682	G	3.64	24.55746	86.41741	Normal
4/1/21	16:44:15	55	0.1	220	30.3	2200	2217	G	3.07	24.55657	86.41734	Normal
4/1/21	16:44:50	55	0.1	400	20.2	4000	3891	G	5.07	24.55566	86.41714	Speed Breaker
4/1/21	16:46:1	55	0.1	200	30.3	2000	2031	G	2.84	24.55481	86.41668	Normal
4/1/21	16:46:1	55	0.1	230	20.2	2300	2310	G	3.19	24.55421	86.41633	Normal
4/1/21	16:46:1	55	0.1	250	30.3	2500	2496	G	3.41	24.55362	86.41601	Speed Breaker
4/1/21	16:46:1	55	0.1	200	30.3	2000	2031	G	2.84	24.55303	86.41553	Normal
4/1/21	16:46:40	55	0.1	230	20.2	2300	2310	G	3.19	24.55268	86.41501	Normal

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

$$Y = 0 * X^2 + 0.930 * X + 171.20$$

$$X = 2300$$

$$Y = 2310$$

07.01.2021
Executive Engineer
Rural Works Department
Jharkhand

Name of Customer :	Hitesh Kumar Singh
Name of Work/Road :	Chakr-Deegha Rd to Ghormo
Lab Job number :	
Date :	1/4/2021
Section No. :	55

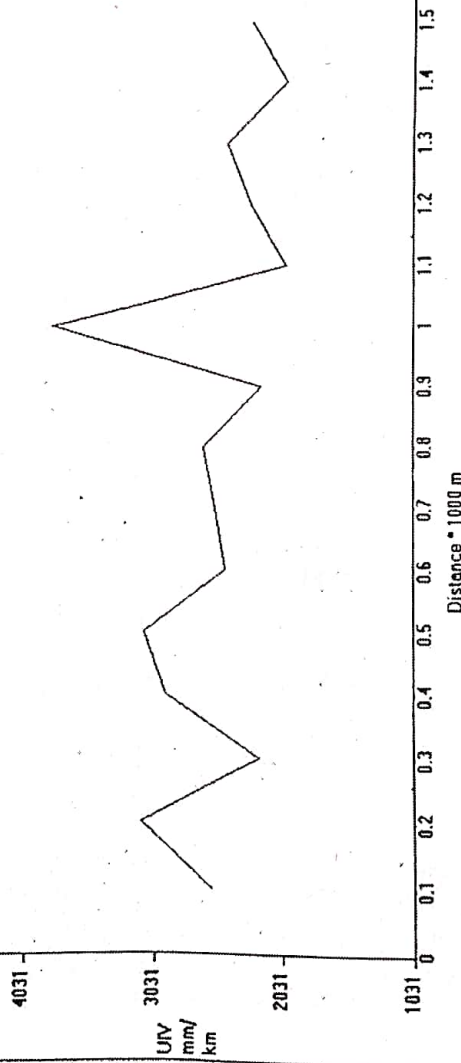
Test Date :	1/4/2021	Road Name :	Sarem (Sohma Kothi) Chakal Ky
Machine No :	411	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UV Range :	1031 To 5000 mm/km
Start Location :	0	Dist Range :	0 To 1.6 • 1000 m
End Location :	1.50	Equation :	$Y = 0 \cdot X^2 + 0.930 \cdot X + 171.20$

Print Generate Report and Graph

Redraw Graph Map View

File : C:\OFFICIAL\Bump Machine\04.01.21\Ghormo Ashram 550 to End\05011632.xls, Section No. : 55, Eqn. : $Y = 0 \cdot$

Name of Customer : Name of Work/Road : Lab Job number :



07.01.2021
Executive Engineer
Rural Works Division, Muzha
