

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, त्रिवेणीगंज।

पत्रांक1416 अ.प्र./त्रिवेणीगंज,
प्रेषक,

दिनांक01/6/2021...../

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, त्रिवेणीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत राशि विमुक्ति हेतु
अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत अधियाचना इस पत्र के साथ संलग्न विहित प्रपत्र में तैयार कर समर्पित की जा रही है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

विश्वासभाजन

01/6/21

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, त्रिवेणीगंज।

01/6/21

Rural Works Department

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division :- Triveniganj

S. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Length (in Km.)	Amount of (in Lacs)	Agreement Amount (in Lacs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Bit (in mm/m)	Thickness of Bituminous Layer (in mm)	Value of Bituminous Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
							Initial Rectification and Surface Renewal	5 Years Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		Construction of Road from Thumha Sirna to Mecha Tola via Mandal Tola in Piprahi Tola under Dinapati Panchayat.	21005 001010	Letter No- 3498 dated- 29.08.19	1.10	40.00900	2570744	1253045	07/MED/ MR-3054/ 2020-21	08.08.2021	On-going	3430	25	8.01	0.00	0.00	2570744	Completed
2		Construction of Road from Sirbortya Sirna to Sirpur Sirna village Chaikapatti under Mahachhapur Panchayat.	21005 001018		2.05	101.95200	40854279	2634720				3475			0.00	0.00	40854279	Completed
Total					3.150	142.76100	9425027	3887775							0.00900	0.00000	9435027	

Executive Engineer
R.W.D. (W.D.) Triveniganj

PM
11/11/21

FORM GER - 19 - A
(See Government of India's Decision (i) below Rule - 150)
Form of Utilization Certificate up to 01.06.2021

(Programming Fund)

Sl. N.	Name of Scheme	Sanction No. & Date with Amount (in Lac.)	Total Amount Received (in Lac.)	Particulars
1	2	3	4	5
1.	Construction of Rural Road under MR-3054 (Bihar Rural Road Maintenance Policy)	Total Allotment received vide Secretary-cum-Empowered Officer BRRDA, Additional CEO, Patna. Letter No-05 Dated-12.01.2021 Letter No-17 Dated-26.02.2021 Letter No-20 Dated-19.03.2021 Letter No-22 Dated-24.03.2021 Letter No-30 Dated-21.05.2021	Rs- 2014.21259	Certified that out of Rs- 2014.21259 lac deposited in sum of Rs- 802.43255 lac has been utilized for the purpose of schemes for which it was sanctioned, Balance Rs. 1211.78004
2.	Certified that I have satisfied myself that the condition on which the grants in aid sanctioned have been duly fulfilled / are being fulfilled and that I have Exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned. i) Works have been supervised by Executive Engineer / Superintending Engineer. ii) Periodical inspection has been conducted by A.E. / Executive Engineer / Superintending Engineer. iii) Construction materials have been tested. iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer. v) All other Codal formalities have been observed.			

Executive Engineer
RWD, Works Division, Triveniganj

[Signature]
01/6/21

[Signature]
01/6/21

Geo Analyst


Name of Customer: SANDEEP KUMAR
 Name of Work/Road: THUNHA SENA TO NEH
 Lab Job number:
 Date: 12-FEB-21
 Section No: 3

Test Date: 12-FEB-21 Road Name: THUNHA SENA TO NEH
 Machine No: Road Type: (R) RURAL ROAD
 Start S No: Side: Interval:
 Start E No:
 Weather: NORMAL UV Range: 2167 To 2420 mm/km
 Start Location: THUNHA Dist Range: 0 To 1.2 0.1 * 1000 m
 End Location: NEHTA TO Equation: $Y = 0.7 * X^2 + 0.034 * X + 210.70$

Print Generate Report and Graph

Redraw Graph

Map View

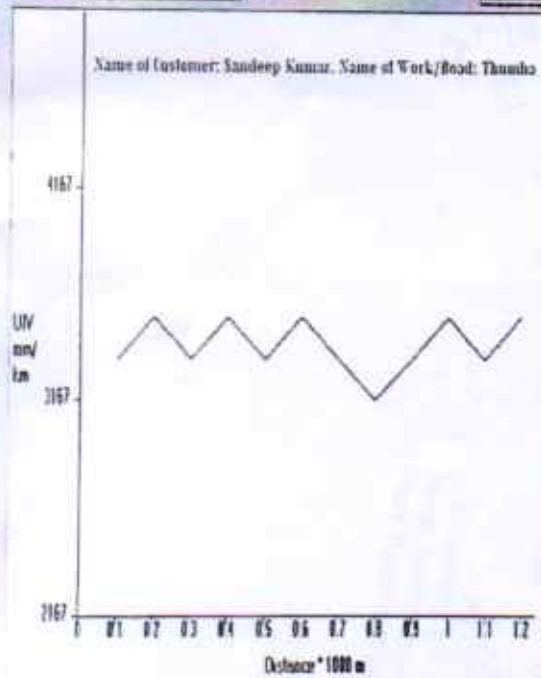

13/2/21
AE

13.2.21
AE

13/2/21
Executive Engineer
Rural Works Department
Jodhpur, Rajasthan

ROAD NAME - THUMHA SIMA TO MEHTA TOLA VIA MANDAL TOLA IN PIPRAHI TOLA UNDER DINAPATTI PANCHAYAT

Date	Time	Section	No.	Length in km	Bumps in mm	Rate	Speed mm/km	OR	IRI	TEGORY	Latitude	ongitude	Event
12/2/21	17:40:31	33	0.1	290	0	2900	3364 G		26.15503	86.7478	Normal		
12/2/21	17:40:31	33	0.1	310	31.2	3100	3561 G		26.15418	86.7547	Normal		
12/2/21	17:41:0	33	0.1	290	32.5	2900	3364 G		26.153	86.7748	Normal		
12/2/21	17:41:0	33	0.1	310	30.3	3100	3561 G		26.15241	86.788	Normal		
12/2/21	17:41:0	33	0.1	290	30.3	2900	3364 G		26.15154	86.8118	Normal		
12/2/21	17:41:0	33	0.1	310	30.3	3100	3561 G		26.15068	86.8002	Normal		
12/2/21	17:41:36	33	0.1	290	30.3	2900	3364 G		26.14978	86.792	Normal		
12/2/21	17:41:36	33	0.1	270	30.3	2700	3167 G		26.14887	86.7	Normal		
12/2/21	17:42:0	33	0.1	290	30.3	2900	3364 G		26.14791	86.788	Normal		
12/2/21	17:42:18	33	0.1	310	31.2	3100	3561 G		26.14708	86.8035	Normal		
12/2/21	17:42:18	33	0.1	290	32.5	2900	3364 G		26.14616	86.795	Normal		
12/2/21	17:43:0	33	0.1	310	31.2	3100	3561 G		26.14528	86.7732	Normal		

$$Y = 0 \cdot X + 2 + 0.384 \cdot X + 510.70$$

$$X = 2700$$

$$Y = 3157$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

13/12/21

Div 9/21
13.2.21

Executive Engineer
Rural Works Department
Work Division, Tivengarh

Name of Customer: SANDEEP KUMAR
Name of Work/Road: SIRHORIYA SIMA S
Lab Job number:
Date: 12-FEB-21
Section No: 12


Test Date: 12-FEB-21 Road Name: SIRHORIYA SIMA TO SR
Machine No: Road Type: (R) RURAL ROAD
Start S No: Side:
Start E No: Interval:
Weather: NORMAL UV Range: 2167 To 5000 1000 mm/km
Start Location: SIRHORIY Dist Range: 0 To 23 01 * 1000 m
End Location: SRIPUR SI Equation: $Y = 0 * X^2 + 0.94 * X + 510.70$

Print Generate Report and Graph

Redraw Graph

Map View

Name of Customer: Sandeep Kumar. Name of Work/Road: Sirhoriya Sima to Sripur Sima Village Chilkapatti U

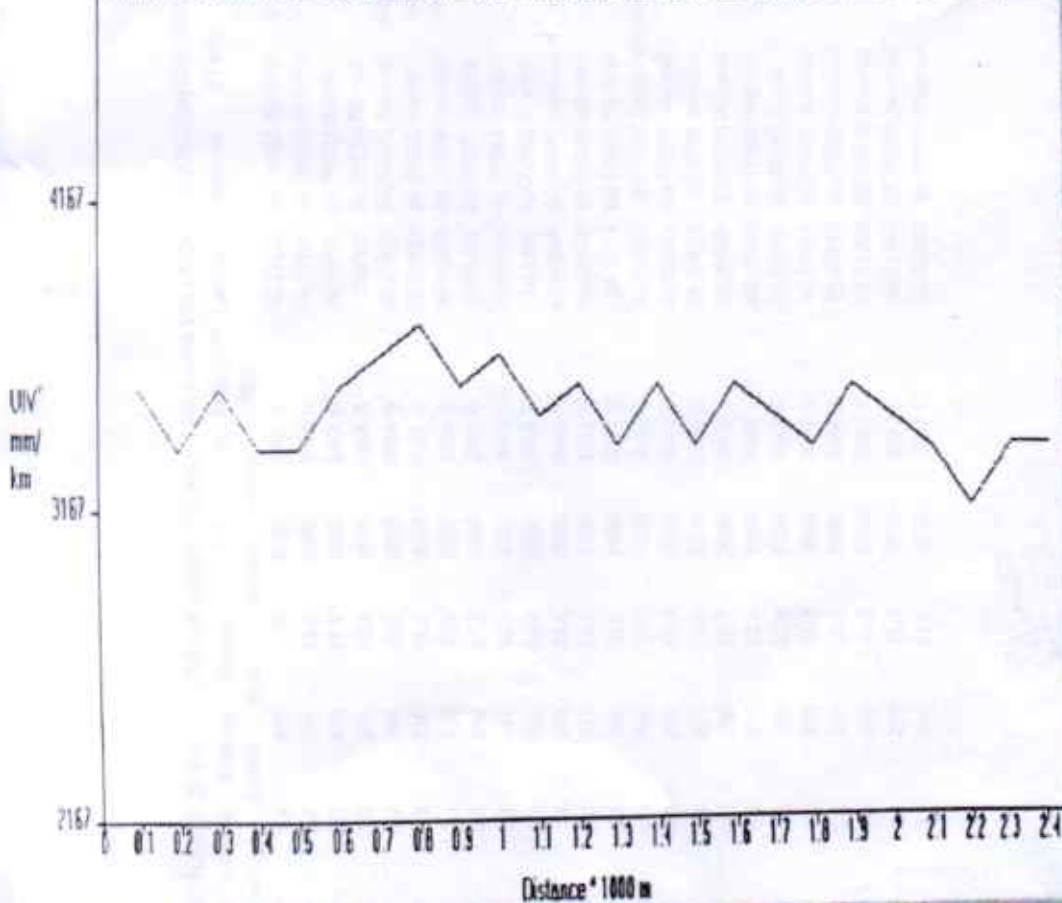

13/2/21

UV
13.2.21
AE.

Executive Engineer
Rural Works Department
Work Division, Trivenigani

ROAD NAME - SIRHORIYA SIMA TO SRIPUR SIMA VILLAGE CHILKAPATTI UNDER MAHESHPUR PANCHAYAT

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	mm/km	OR	mm/km	ROAD	IRI TEGORY	Latitude	ongitude	Event
12/2/21	19:33:0	37	0.1	310	0	3100	3561 G	26.23276	86.78492	Normal			
12/2/21	19:33:31	37	0.1	290	31.2	2900	3364 G	26.23295	86.78396	Normal			
12/2/21	19:34:7	37	0.1	310	32.5	3100	3561 G	26.23305	86.78295	Curve			
12/2/21	19:34:7	37	0.1	290	31.2	2900	3364 G	26.23335	86.78221	Normal			
12/2/21	19:35:0	37	0.1	290	32.5	2900	3364 G	26.23374	86.78128	Normal			
12/2/21	19:35:17	37	0.1	310	31.2	3100	3561 G	26.23397	86.78032	Curve			
12/2/21	19:35:17	37	0.1	320	32.5	3200	3659 G	26.23453	86.77976	Normal			
12/2/21	19:36:0	37	0.1	330	31.2	3300	3757 G	26.23463	86.77875	Normal			
12/2/21	19:36:0	37	0.1	310	32.5	3100	3561 G	26.23481	86.77783	Normal			
12/2/21	19:36:28	37	0.1	320	31.2	3200	3659 G	26.2352	86.77695	Normal			
12/2/21	19:37:0	37	0.1	300	32.5	3000	3462 G	26.23604	86.77673	Normal			
12/2/21	19:37:3	37	0.1	310	31.2	3100	3561 G	26.23693	86.77645	Normal			
12/2/21	19:37:38	37	0.1	290	32.5	2900	3364 G	26.2376	86.77582	Normal			
12/2/21	19:38:0	37	0.1	310	31.2	3100	3561 G	26.23825	86.7751	Speed Breaker			
12/2/21	19:38:14	37	0.1	290	32.5	2900	3364 G	26.23851	86.77421	Normal			
12/2/21	19:38:49	37	0.1	310	31.2	3100	3561 G	26.23872	86.77332	Normal			
12/2/21	19:39:0	37	0.1	300	32.5	3000	3462 G	26.23919	86.77236	Normal			
12/2/21	19:39:24	37	0.1	290	31.2	2900	3364 G	26.23858	86.77207	Normal			
12/2/21	19:40:0	37	0.1	310	32.5	3100	3561 G	26.23768	86.77189	Curve			
12/2/21	19:40:0	37	0.1	300	31.2	3000	3462 G	26.23753	86.77101	Normal			
12/2/21	19:40:35	37	0.1	290	32.5	2900	3364 G	26.23755	86.77002	Normal			
12/2/21	19:41:10	37	0.1	270	31.2	2700	3167 G	26.23759	86.76936	Normal			
12/2/21	19:41:14	37	0.1	290	31.2	2900	3364 G	26.23761	86.76947	Normal			
12/2/21	19:41:20	37	0.1	290	31.2	2900	3364 G	26.23769	86.76872	Normal			

(R) RURAL ROAD

Good <4000
Average 4001-5000
Poor >5001

$$Y = 0 \cdot X^2 + 0.984 \cdot X + 510.70$$

$$X = 2700$$

$$Y = 3167$$

Vib-9
13.2.21
AE

13/2/21
13/2/21

11/6/21
Executive Engineer
Rural Works Department
Work Division, Triveniganj
