

Name Of Road :- Const of Rd from Rajoi Bel pauthu to parasdih karanja

Date	Time	Section	Length	Bumps	Speed	OR	CATEGORY	IRI	Latitude	Longitude	Event
No.	in km	in mm	Rate	mm/km	UIV	ROAD					
1/6/21	8:58:15	29	0.1	150	20.2	2400	2858 G	3.85	24.8131	84.4862	Normal
1/6/21	8:58:50	29	0.1	240	20.2	3100	3654 G	3.8	24.8129	84.4871	Normal
1/6/21	8:59:0	29	0.1	250	30.3	2700	3199 G	3.26	24.8128	84.4881	Normal
1/6/21	8:59:0	29	0.1	220	30.3	2900	3426 G	3.53	24.8125	84.4891	Normal
1/6/21	8:59:0	29	0.1	210	30.3	1600	1950 G	2.74	24.8124	84.4901	Normal
1/6/21	8:59:25	29	0.1	310	10.1	1700	2063 G	2.88	24.8124	84.4911	Normal
1/6/21	8:59:25	29	0.1	200	30.3	1600	1950 G	2.74	24.8129	84.492	Normal
1/6/21	8:59:25	29	0.1	290	10.1	900	1154 G	1.72	24.8132	84.4928	Normal
1/6/21	9:0:1	29	0.1	210	20.2	2100	2518 G	3.44	24.813	84.4938	Normal
1/6/21	9:0:1	29	0.1	240	20.2	2400	2858 G	3.85	24.8126	84.4944	Normal
1/6/21	9:0:1	29	0.1	130	30.3	1300	1609 G	2.31	24.8117	84.4941	Normal
1/6/21	9:0:36	29	0.1	270	20.2	2700	3199 G	3.26	24.8108	84.4938	Normal
1/6/21	9:0:36	29	0.1	280	20.2	1900	2290 G	3.36	24.8106	84.4947	Normal
1/6/21	9:1:0	29	0.1	340	10.1	3200	3694 G	3.19	24.8104	84.4958	Normal
1/6/21	9:1:11	29	0.1	290	20.2	2900	3426 G	3.53	24.8096	84.496	Normal
1/6/21	9:1:11	29	0.1	230	20.2	2300	2745 G	3.72	24.8092	84.4969	Normal
1/6/21	9:1:46	29	0.1	210	30.3	2100	2518 G	3.44	24.8089	84.4978	Normal
1/6/21	9:2:0	29	0.1	280	20.2	2800	3313 G	3.4	24.8088	84.4986	Normal
1/6/21	9:2:22	29	0.1	190	20.2	1900	2290 G	3.16	24.8093	84.4994	Normal
1/6/21	9:2:22	29	0.1	190	30.3	1900	2290 G	3.16	24.8092	84.5004	Normal
1/6/21	9:3:0	29	0.1	140	40.4	1400	1722 G	2.45	24.8089	84.5013	Normal
1/6/21	9:3:0	29	0.1	190	30.3	1900	2290 G	3.16	24.8086	84.5023	Normal
1/6/21	9:3:32	29	0.1	240	20.2	2400	2858 G	3.85	24.8083	84.5033	Speed Breaker
1/6/21	9:4:8	29	0.1	220	30.3	2200	2631 G	3.58	24.8081	84.5043	Normal
1/6/21	9:4:8	29	0.1	220	20.2	1400	1722 G	3.72	24.8081	84.5052	Normal
1/6/21	9:4:43	29	0.1	220	20.2	1100	1382 G	3.38	24.8079	84.5062	Normal
1/6/21	9:5:0	29	0.1	220	20.2	1300	1609 G	3.38	24.8075	84.507	Normal
1/6/21	9:5:18	29	0.1	220	20.2	1700	2063 G	3.68	24.8068	84.5072	Bridge
1/6/21	9:5:18	29	0.1	290	10.1	2900	3426 G	3.88	24.8064	84.5081	Normal
1/6/21	9:6:0	29	0.1	300	20.2	3000	3540 G	3.53	24.8066	84.5087	Normal
1/6/21	9:6:0	29	0.1	280	20.2	2800	3313 G	3.66	24.8084	84.5093	Normal
1/6/21	9:6:29	29	0.1	250	30.3	2500	2972 G	4.4	24.8084	84.5101	Speed Breaker
1/6/21	9:6:29	29	0.1	340	30.3	3400	3994 G	3.99	24.8092	84.5104	Normal
1/6/21	9:6:29	29	0.1	280	30.3	2800	3313 G	3.19	24.8101	84.5107	Normal
1/6/21	9:7:4	29	0.1	290	30.3	2900	3426 G	4.4	24.811	84.5109	Speed Breaker
1/6/21	9:9:15	29	0.1	230	30.3	2300	2745 G	3.53	24.8119	84.5108	Normal
1/6/21								3.72	24.8126	84.511	Normal

Total Len 3.7

J.E

PONCELY
1/6/21
J.E

A.E

E.E

Ymh
2/6/21

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2235$$

$$Y = 2669$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Seco Analyzer


Name of Customer : M/S JAI MAA BHAGWATI CON
 Name of Work/ Road : Const of Rd from Raza Bel paul
 Lab Job number : 29
 Date : 01-06-2021
 Section No. : 29

Test Date : 01-06-2021 Road Name : Bel paulhu to parasdih karanja
 Machine No : 377 Road Type : (R) RURAL ROAD
 Start S No : 315 Side : Aurangabad Interval
 Start E No : 351
 Weather : Normal UV Range : 154 To 5000 1000 mm/km
 Start Location : 2481313 84 Dist Range : 0 To 38 0.1 = 1000 m
 End Location : 24812592 84 Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Print Generate Report and Graph

Redraw Graph

Map View

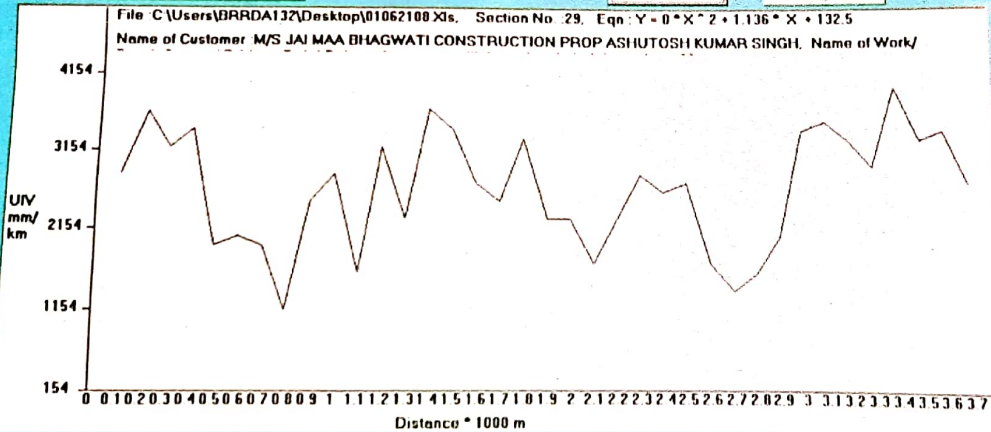

Prakash
 1/6/21 JG

Sham
 1/6/21

Prakash
 2/6/21

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

Email ID:- eerwdaurangabad1@gmail.com

Mob:- 8986915333

पत्रांक.....16.28.21.1..... औरंगाबाद/दिनांक.....02/06/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

(Signature)
21/6/21
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद
(Signature)
02.06.21

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad
Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/20/0004	MADANPUR DEO ROAD TO SIRAUINDHA CANAL PUL HASANBAR	16281032321	5979/30.10.2019	3.335	119.458	76.91	34.73	75MBD-2019-20 21.09.2020	20.01.2021	15.04.2021	2492	25.00MM	5.000%	0.00000	0.00000	76.91	Comp.
2	RM/AU/AUR/20/0004	G.T ROAD (MADANPUR ROAD) TO DURGAPUR MANWA DOHAR	16281032323	5979/30.10.2019	4.8	174.709	110.49	50.64835	75MBD-2019-20 21.09.2020	20.01.2021	15.04.2021	3163	25.00MM	5.000%	0.00000	0.00000	110.49	Comp.
3	RM/AU/AUR/20/0005	AURANGABAD NABINAGAR ROAD - PHULDIHA	NEA22000216	5979/30.10.2019	1.4	50.357	33.56	*13.57	81MBD-2019-20 15.09.2020	14.01.2021	01.06.2021	2468	25.00MM	5.000%	0.00000	0.00000	33.56	Comp.
4	RM/AU/AUR/20/0003	G.T ROAD JASOIYA MORE TO BHARTHAULI VIA LORD BUDHA SCHOOL	16281032315	5979/30.10.2019	4.6	204.221	120.2	40.80975	79MBD-2019-20 03.09.2020	02.03.2021	01.06.2021	3123	25.00MM	5.0780%	0.00000	0.00000	120.2	Comp.
5	RM/AU/AUR/20/0001	AURANGABAD D. NAGAR - JAGDISHIPUR	NEA2200048	5979/30.10.2019	1.45	55.7	31.07	16.296	80MBD-2019-20 19.08.2020	18.08.2021	01.06.2021	3440	25.00MM	5.0733%	0.00000	0.00000	31.07	Comp.
6	RM/AU/AUR/20/0001	AURANGABAD D. NAGAR - KURMAHA	NEA2200049	5979/30.10.2019	1.9	71.737	39.64	17.13	80MBD-2019-20 19.08.2020	18.08.2021	01.06.2021	2883	25.00MM	5.0580%	0.00000	0.00000	39.64	Comp.
7	RM/AU/AUR/19/0019	Niranjanapur to Koyal Nahar Road	10602802086	3140/22.07.2019	2	68.06	42.92	18.19	91MBD-2019-20 24.03.2020	23.12.2020	01.06.2021	3567	25.00MM	5.000%	0.00000	0.00000	42.92	Comp.
8	RM/AU/AUR/19/0019	Const of Pcc Rd from Maharjanj Rd to Murauli khurd Jhuyia tola & Ravidas tola under	10602805002	3140/22.07.2019	0.65	21.6	12.27	4.32	91MBD-2019-20 24.03.2020	23.12.2020	01.06.2021	2479	25.00MM	5.000%	0.00000	0.00000	12.27	Comp.
9	RM/AU/AUR/19/0019	Saidpur naughara Road - Mazahida	10602901040	3140/22.07.2019	1.13	41.72	26.92	10.56	91MBD-2019-20 24.03.2020	23.12.2020	01.06.2021	2910	25.00MM	5.000%	0.00000	0.00000	26.92	Comp.
10	RM/AU/AUR/19/0034	Village Kandi to Navinagar via Senduriya Road	10602901043	3140/22.07.2019	2.5	82.97	50.72	23.85	64MBD-2019-20 05.02.2020	04.11.2020	01.06.2021	2928	25.00MM	5.000%	0.00000	0.00000	50.72	Comp.

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad
Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
 Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
11	RM/AU/AUR/19/0034	AURANGABAD NABINAGAR ROAD - BARIYAWAN	NEA22000248	3140/22.07.2019	3.3	97.75	61.03	26.92	64MBD-2019-20 05.02.2020	04.11.2020	01.06.2021	2848	25.00MM	5.000%	0.00000	0.00000	61.03	Comp.
12	RM/AU/AUR/19/0029	Const of Rd from paharpura to Gurdi via Bhaluari Rd	10602801020	3140/22.07.2019	2.5	109.59	74.85	23.75	63MBD-2019-20 05.02.2020	04.11.2020	01.06.2021	2604	25.00MM	5.0000%	0.00000	0.00000	74.85	Comp.
13	RM/AU/AUR/19/0007	Const of Rd from Rajoi Bel pauthu to parasdih karanja	10602801022	3140/22.07.2019	3.7	143.46	94.55	34.45	87MBD-2019-20 22.06.2020	21.03.2021	01.06.2021	2669	25.00MM	5.0000%	0.00000	0.00000	94.55	Comp.
14	RM/AU/AUR/19/0014	Deo Jeeva Bigha Road - Sargawan	10602802109	3140/22.07.2019	1.5	57.73	37.51	14.37	71MBD-2019-20 15.02.2020	14.11.2020	01.06.2021	2759	25.00MM	5.0557%	0.00000	0.00000	37.51	Comp.
15	RM/AU/AUR/19/0016	Const of Rd from Deo jiwa bigha Chatti to Sargawan	10602801006	3140/22.07.2019	2.5	94.43	60.9	24.01	73MBD-2019-20 15.02.2020	14.11.2020	01.06.2021	2885	25.00MM	5.034%	0.00000	0.00000	60.90	Comp.
		Total			37.84												873.54	

Divisional Accounts Officer
 Rural Works Department, works
 Division, Aurangabad

21/6/21
 Executive Engineer
 Rural Works Department
 Works Division, Aurangabad
 02.06.21
