

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा (नालन्दा)

पत्रांक 926

हिलसा,

दिनांक 26 / 06 / 2021

प्रेषक:- कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,
नोडल पदाधिकारी,
MR, 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-2022 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-2022 में व्यय हेतु संलग्न विवरणी के अनुसार रू0 - 170.17915 (एक करोड़ सत्तर लाख सतरह हजार नौ सौ पन्द्रह) मात्र का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके।

अनु0- यथोक्त।

विश्वासभाजन


26.6.2021

कार्यपालक अभियन्ता
ग्रा0का0वि0, कार्य प्रमण्डल, हिलसा।

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :-Hilsa


Name of Works Division :-Hilsa																			
SI No.	Package No.	Name of Road	Project ID as per MIS	Administ rative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditu re as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks	
					Length (in km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RM/NA/HIL/ 20/0003	Korawan to Barhi Bigha	10200803093	2775/ 19.08.20	1.667	93.65000	69.92138	14.24515	18/MBD/ 2020-21	22.10.2021	22.06.2021	2310	25.00	5.00	0.00	0.00	69.92138	Surface Complete	
2	RM/NA/HIL/ 20/0003	Chiksauna Amat Path to Keshochak	10200813003	2775/ 19.08.20	0.845	42.62100	18.41460	9.20730	18/MBD/ 2020-21	22.10.2021	22.06.2021	2552	25.00	5.00	0.00	0.00	18.41460	Surface Complete	
3	RM/NA/HIL/ 20/0003	T01 Banbarpur via Kamta	10200802082	2775/ 19.08.20	1.750	110.64900	81.84317	15.68645	18/MBD/ 2020-21	22.10.2021	22.06.2021	2528	25.00	5.00	0.00	0.00	81.84317	Surface Complete	
TOTAL																		170.17915	

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.


 Executive Engineer
 RWD, Works Division,
 Hilsa

File: F:\22061719.Xls, Section No. 32, Eqn. $Y = 0 \cdot X^2 + 0.898 \cdot X + 377.8$

Name of Customer: Kumar Construction (Pro-Suresh Kumar), Name of Work/ Road: T01 to Banbaripur via Kamata

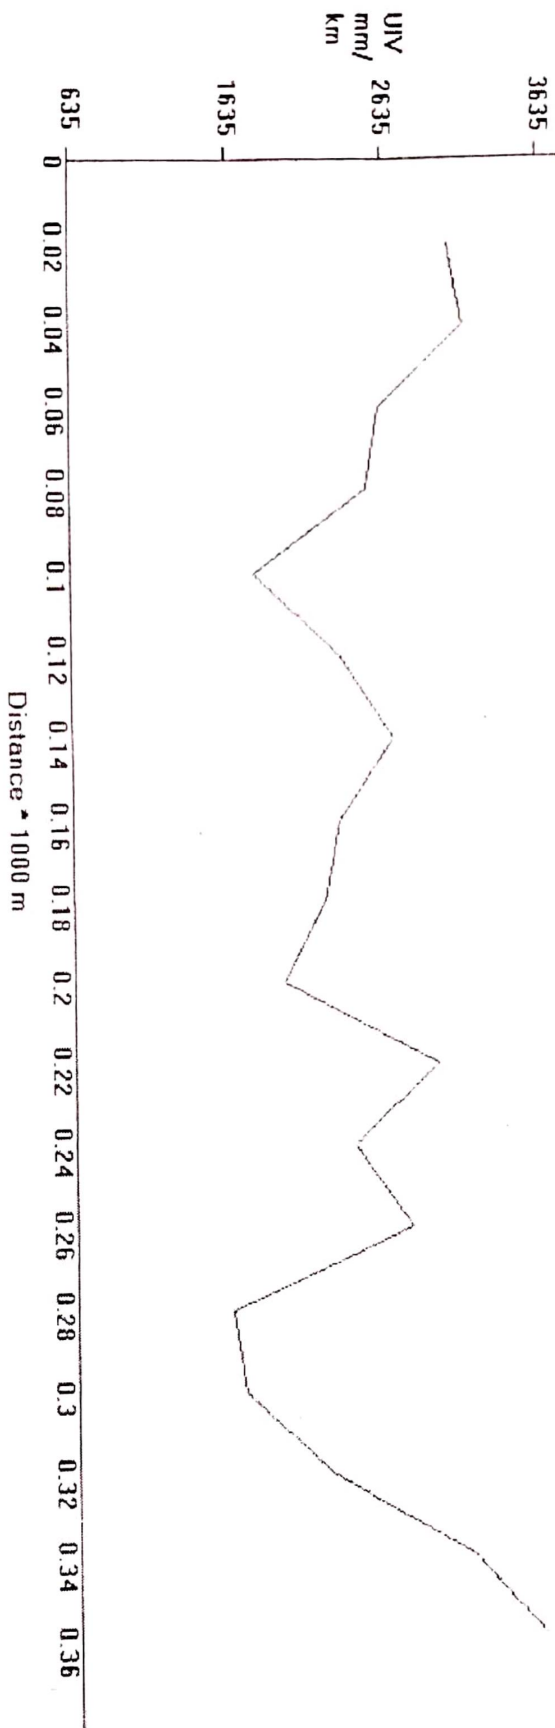

Could not print
ATE

26.9.2021

Name of Road:- T01 to Banbaripur via Kamata Path

Name of Contractor:- Kumar Construction (Pro-Suresh Kumar)

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR am/km	CIV	ROAD	IRI	Latitude	Longitude	Event
		No.										
22/6/21	13:15:14	32	0.1	300	0	3000	3071	G	4.11	25.331547	85.289208	Normal
22/6/21	13:16:0	32	0.1	310	10.1	3100	3161	G	4.22	25.331635	85.289282	Normal
22/6/21	13:16:0	32	0.1	250	20.2	2500	2622	G	3.57	25.331835	85.287288	Speed Breaker
22/6/21	13:16:25	32	0.1	240	10.1	2400	2533	G	3.46	25.331815	85.286363	Normal
22/6/21	13:17:0	32	0.1	160	20.2	1600	1814	G	2.57	25.332058	85.28542	Normal
22/6/21	13:17:0	32	0.1	220	30.3	2200	2353	G	3.24	25.332297	85.284477	Normal
22/6/21	13:17:0	32	0.1	260	30.3	2600	2712	G	3.68	25.33247	85.283502	Normal
22/6/21	13:17:35	32	0.1	220	30.3	2200	2353	G	3.24	25.332063	85.282457	Normal
22/6/21	13:17:35	32	0.1	210	20.2	2100	2263	G	3.13	25.33253	85.282172	Normal
22/6/21	13:18:0	32	0.1	180	30.3	1800	1994	G	2.79	25.333462	85.282305	Normal
22/6/21	13:18:10	32	0.1	290	40.4	2900	2982	G	4	25.33424	85.282255	Normal
22/6/21	13:18:10	32	0.1	230	20.2	2300	2443	G	3.35	25.335243	85.282238	Normal
22/6/21	13:18:46	32	0.1	270	10.1	2700	2802	G	3.79	25.335965	85.28202	Normal
22/6/21	13:19:0	32	0.1	140	20.2	1400	1635	G	2.34	25.335893	85.281027	Normal
22/6/21	13:19:0	32	0.1	150	30.3	1500	1724	G	2.45	25.33595	85.28005	Normal
22/6/21	13:19:0	32	0.1	210	40.4	2100	2263	G	3.13	25.336008	85.27904	Normal
22/6/21	13:19:21	32	0.1	310	10.1	3100	3161	G	4.22	25.336025	85.27803	Speed Breaker
22/6/21	13:20:0	32	0.05	290	10.1	3025	3633	G	4.77	25.335247	85.277995	Normal
Total			1.750	4240	383.8	43125	45519		62.06			

$Y = 0 + X^2 + 0.898 \times X + 377.8$		
$X = 25556$		
$Y = 23327$		
GR RURAL ROAD		
Good	Average	Poor
<4000	4001-5000	>5001

Cealid
26/6/21
nt

26/6/2021
E.C.
