

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 1270 (अभु-)

पालीगंज/दिनांक : 08/9/21

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह-सचिव, (बाडा)
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- MR-3054 New Maintenance Policy-2018 योजनान्तर्गत Patna Jila Antargat Naubatpur Prakhand Ke Antargat Pitwaas PWD Path Se Mahadalit Tola Tak Path Nirmaan निर्माण कार्य में आवंटन हेतु अधियाचना भेजने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 New Maintenance Policy-2018 योजनान्तर्गत Patna Jila Antargat Naubatpur Prakhand Ke Antargat Pitwaas PWD Path Se Mahadalit Tola Tak Path Nirmaan पूर्ण किए गए निर्माण कार्य हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अनु:- (1) अधियाचना विहित प्रपत्र में।

(2) M.B. का छायाप्रति।

(3) IRI जाँच Report की छायाप्रति।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

Requestion Form for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification and Surface Renewal)

Name of Work Division - Palamou

Sl No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) No & Date	Administrative Approval (AA)		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of ISI Bitumen Layer (in mm.km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requestion against work done (in Lakh)	Remarks
					Letter No	Large Amount of h (in km)	Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2																	
1	MR-N-18, 20 Palamou-02	Repair and five Year Maintenance Road from Patna Jilla Antargat Nabadipur Prakarand ke Antargat Pomaas PND Path Se Mahasadi Tota Tai Path Nirman	10100505001	Letter No 6459, Dt- 13.12.2019	1574	52,35,100	39,89,900	16,27,881	05/MRD/20-21 & 18-June-2020	17.3.2021		4.11	0.25	5.02%	13,10,960	13,10,960	19,66,439	Work Completed

Total Amount Rs- 1966439 (Ninteen Lakhs Sixty Six Thousand Four Hundred thirty Nine)

Executive Engineer
RWD, Works Division, Palamou
28/11/21
28/11/21

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R.W.D. GULJARBAH, PATNA

17/6/2024

709

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

1st Year Q.C. Report

Name of Project/Road :- Pit road & road to Pit road Mahadoli Tal

Name of Scheme :- M.R. 2054

Name of Agency :- Sanjesh Kumar

Nature of sample : Stone Metal GR - III

Date of Collection/Received on lab. :- 14/6/2024

Location/Chainage :- 350 M

Date of Test :- 17/6/2024

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Subapur

vide letter No. 70 Dt. 16.5.2021

Agreement No / Package No. :- 05/MR20/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1	21.87.1.	40%

Sl. No	Sieve Size in (mm)	Weight of Sample Taken Kgs 30.225				Required Value			Remarks
		Weight Retained	% of Wt. Retained	% of Cumm. Retained	% of Passing	Grading I	Grading II	Grading III	
1	125	—	—	—	—	100	—	—	
2	75	—	—	—	—	90-100	100	—	
3	63	0.000	0.00	0.00	100	25-60	90-100	100	
4	53	0.907	3.30	3.30	96.70	—	25-75	95-100	
5	45	7.904	26.15	29.45	70.55	0-15	0-15	65-90	
6	22.4	18.830	62.30	91.75	8.25	0-5	0-5	0-10	
7	11.2	1.405	4.65	96.40	3.60	—	—	0-5	

Sanjesh Kumar
17/6/2024

Sanjesh Kumar
A.E.
17/6/2024
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Sanjesh Kumar
E.E.
17/6/2024
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Regional Laboratory
D. Guljarbagh
patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना 800007

पत्रांक-709 अग

पटना/दिनांक : 17.06.2021

प्रेषक ,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला
गुलजारबाग, पटना -7

सेवा में ,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल . पाली राज .

विषय :- जौचफल प्रतिवेदन के संबंध में ।

प्रसंग :- AE, Nawabpur vide letter no - 70 dt 16.4.2021

महाशय ,

उपर्युक्त विषयक के संबंध में जौचफल प्रतिवेदन इस पत्र के साथ संलग्न कर
आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Pitwar Road to Pitwar Mahadevi Tola
2/5000000000

अनु० :- यद्योक्त

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग, पटना -7

OFFICE OF THE EXECUTIVE ENGINEER

708

REGIONAL LABORATORY, R.W.D. GULJARBAUGH, PATNA

17/6/2024

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Pitawas Road to Pitawas Mahadab 7.1a

Name of Scheme :- M.R. - 3054

Name of Agency :- Santosh Kumar

Nature of sample : Mix seal (13.2mm to 9mm) Date of Collection/Received :- 14/6/2024

Location :- 275m

Date of Test :- 17/6/24

Ref :- Material sent by E.E. R.W.D. WORKS Division/Syb Division Nambathpur

vide letter No. 72 Dt. 30/5/24

Agreement No / Package No. : 05 / 2200/2020-24

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 19.350				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Type A	Type B	
1	13.2	0.000	0.00	0.00	100	—	100	
2	11.2	0.629	3.25	3.25	96.75	100	88-100	
3	5.6	9.356	48.35	51.60	48.40	52-88	31-52	
4	2.8	4.992	25.80	77.40	22.60	14-38	5-25	
5	0.09	3.667	18.95	96.35	3.65	0-5	0-5	

Series 3
17/6/2024

Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Regional Laboratory
R.W.D. Guljarbagh
patna - 7

E.E. 17/6/24

Regional Laboratory
R.W.D. Guljarbagh
patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना 800007

पत्रांक - 708 अनुष

पटना/दिनांक : 17.06.2021

प्रेषक,
कार्यपानक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला
गुलजारबाग, पटना - 7

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल . पालीगंज

विषय :- जाँचफाल प्रतिवेदन के संबंध में ।

प्रसंग :- AE, Nambathpuram wide letter no. 72 dt 30/5/2024

महाशय ,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Pitwar Road to Pitwar Mahadalit Talu
Stem chips (132mm to 9mm)

अनु० :- यथोक्त

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग, पटना - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY R.W.D. MULZARBACHH, PATNA

17/6/2024

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Work: Piturua Road In Piturua Mahadalit Taluk

Name of Scheme: 122-2554

Name of Agency: Sambarh L. M. R.

Nature of Sample: Semi Dense Bituminous Concrete Date of Collection/Received: 14/6/2024

Location: 122-2554

Date of Test: 16/6/24

Ref: Material sent by E.E./A.E. R.W.D. WORKS Division/MulzARBACHH Division

vide letter No. 33 of 17/6/2024

Agreement No./Package No.: 05/11/10/2024

S.No.	A.I.V.
Average Test Value	Required Value(Max)
1	30%

S. No.	Size (mm)	Weight of Sample Taken (g)	Weight Retd.	% of 47.5 Retained	% of 75 Cum. Retained	% of Passing	Required Value	Remarks
1	132	0.000	0.00	0.0	0.0	100	100	
2	95	0.950	0.00	0.0	0.0	100	90-100	
3	4.75	1.535	0.00	0.0	0.0	100	35-51	
4	2.36	1.514	0.00	0.0	0.0	100	24-39	
5	1.18	1.514	0.00	0.0	0.0	100	15-30	
6	0.600	1.514	0.00	0.0	0.0	100	9-19	
7	0.075	1.514	0.00	0.0	0.0	100	3-8	

Regional Laboratory
R.W.D. MulzARBACHH
Patna

Regional Laboratory
R.W.D. MulzARBACHH
Patna

Regional Laboratory
R.W.D. MulzARBACHH
Patna

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना 800007

पत्रांक - 710 अग्र-

पटना/दिनांक : 17.06.2021

प्रेषक ,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला
गुलजारबाग, पटना - 7
सेवा में ,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल .प्राप्तीगंत

विषय :- जाँचफल प्रतिवेदन के संबंध में ।

प्रसंग :- ACF, Nababpur vide letter no - 73 dt 3/6/2021

महाशय ,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर
आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Pituras Road to Pituras Mchadab+ Tolg
SOBC

अनु० :- यथोक्त

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग, पटना - 7
17/06/2021

Date 12/10/2021

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULZARBAGH, PATNA - 7

Name of Project/Road :- Pithura Road to Pithura Mahadali Tola

Name of Scheme :- MR-3054

Name of Agency :- Sardar Kumar

Nature of sample :- Bitumens Content for SORC

Location :- 225 M

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division /Sub Division Naubatpur vide letter No. 74 Dt. 05/06/2021

Agreement No / Package No. :

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	508.00	500.00	510.00	
2	Wt. of Dry chips after extraction (b)	483.30	495.00	484.50	
3	Percentage of bitumen (In the mix) $((a-b) \times 100/a)$ (%)	5.06	5.00	5.00	
4	Average % bitumen	5.02			

8/11/2021

Regional Laboratory

R. W. D. GulzARBAGH patna - 7

12/10/2021

Regional Laboratory

R. W. D. GulzARBAGH patna - 7

12/10/2021

Regional Laboratory

R. W. D. GulzARBAGH patna - 7

कार्यपालक अधिवेशन का कार्यालय

राज्य न्याय विभाग, उच्च न्यायालय, मुंबई

फोन 300007

दिनांक - 7.5.2020

पत्र दिनांक 7.16.2020

प्रति,

कार्यपालक अधिवेशन
राज्य न्याय विभाग
उच्च न्यायालय
मुंबई - 400 007

सेवा में,

कार्यपालक अधिवेशन
राज्य न्याय विभाग
उच्च न्यायालय

विषय :- राज्यपाल अधिवेशन के संबंध में

प्रति :- श्री. राज्यपाल अधिवेशन के संबंध में

प्रमाणित

उपरोक्त विषयक न्याय के संबंध में राज्यपाल अधिवेशन के एक से न्याय न्याय के
कार्यपालक अधिवेशन के संबंध में न्याय के एक से न्याय न्याय के

Signature of the President of the State

7.16.2020

Signature of the Secretary

न्याय - न्याय

Signature of the Secretary
राज्य न्याय विभाग
उच्च न्यायालय

Name of Customer : SANTOSH KUMAR

Name of Work/ Road : PITWAS PWD ROAD TO MAH

Lab Job number :

Date : 13-06-2021

Section No. : 28

Print Generate Report and Graph


Test Date :	13-06-2021	Road Name :	ROAD TO MAHADALIT TOLA
Machine No :		Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UV Range :	963 To 5000 mm/km
Start Location :		Dist Range :	0 To 1.6 0.1 1000 m
End Location :		Equation :	$Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Redraw Graph

Map View

File : C:\Users\SHAZ\Desktop\28.Xls. Section No. 28. Eqn : $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Name of Customer : SANTOSH KUMAR, Name of Work/ Road : PITWAS PWD ROAD TO MAHADALIT TOLA, Lab

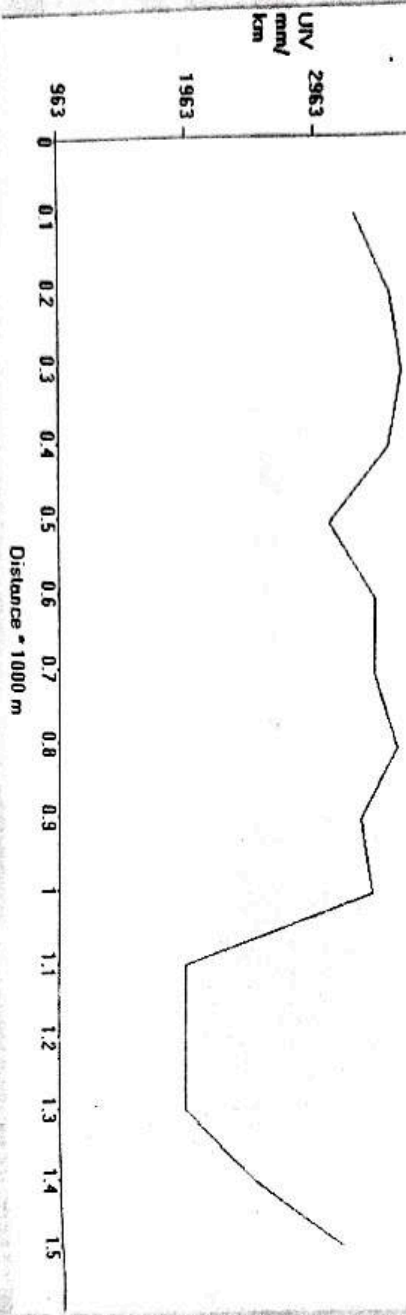

Handwritten signature
28.6.21
D.E.

Handwritten signature
22.06.21
A.E.

25/6

NAME OF THE ROAD : PITWAS PWD ROAD TO MAHADALT TOLA TAK

LENGTH OF THE ROAD : 1.54 KM

PACKAGE NO. : MR-N/19-20/PALIGANU/01

DIVISION : PALIGANU

BLOCK : NAUBATPUR

AGENCY : SANTOSH KUMAR

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event	Y = 0 * X^2 + 0.936 * X + 278.4 X = 3182 Y = 3256		
13/6/21	12:14:33	28	0.1	320	0	3200	3273	G	4.35	25.390398	84.936262	Normal			
13/6/21	12:15:09	28	0.1	350	20.2	3500	3554	G	4.68	25.390698	84.93677	Curve			
13/6/21	12:15:34	28	0.1	360	20.2	3600	3648	G	4.79	25.39158	84.936835	Curve			
13/6/21	12:16:00	28	0.1	350	30.3	3500	3554	G	4.68	25.392013	84.936143	Normal			
13/6/21	12:16:20	28	0.1	300	30.3	3000	3086	G	4.13	25.392325	84.935185	Normal	(R) RURAL ROAD		
13/6/21	12:16:40	28	0.1	340	30.3	3400	3460	G	4.57	25.392888	84.934882	Normal	Good	Average	Poor
13/6/21	12:17:00	28	0.1	340	30.3	3400	3460	G	4.57	25.39381	84.935202	Normal	<4000	4001-5000	>5001
13/6/21	12:17:15	28	0.1	360	10.1	3600	3648	G	4.79	25.394643	84.935453	Speed Breaker			
13/6/21	12:17:30	28	0.1	330	30.3	3300	3367	G	4.46	25.395525	84.935588	Normal			
13/6/21	12:18:06	28	0.1	340	30.3	3400	3460	G	4.57	25.39638	84.935858	Normal			
13/6/21	12:18:16	28	0.1	180	30.3	1800	1963	G	2.76	25.397288	84.936077	Normal			
13/6/21	12:18:26	28	0.1	180	30.3	1800	1963	G	2.76	25.398232	84.936245	Normal			
13/6/21	12:18:41	28	0.1	180	20.2	1800	1963	G	2.76	25.399157	84.936312	Curve			
13/6/21	12:19:00	28	0.1	240	30.3	2400	2524	G	3.45	25.399158	84.937188	Normal			
13/6/21	12:19:16	28	0.044	140	30.3	3182	3256	G	4.33	25.398942	84.937592	Normal			
TOTAL			1.444	4310	373.7	44882	46179		61.65	380.92304	1274.041592				
AVERAGE						2992.133	3078.6		4.11						

22.06.21
J.E.

22.06.21
A.E.

22/6
