

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....४७७ १३०

दिनांक.....24/4/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार **11.13792** (ग्यारह लाख तेरह हजार सात सौ बेरानबे) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन

- 
26.4.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Name of Works Division:- Muzaffarpur East-1


Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Road Details				AA Details		Agreement								Actual Maintenance Expenditure										Current Maintenance Demand						Remarks
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th. Year Maintenance	5th. Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	Total	
1	JHAPHA MINAPUR PATH TO JAMALABAD		315721032554	06.06.2021	92.59	29.57000	79.33000	1.38957	2.78778	8.09209	3.56545	9.05249	24.88738	3.500	0.000	0.000	0.000	0.000	0.000	0.000	3.50	1591.543	1.24437						1.24437	
2	Jahangipur to Itaha Bazar (01-02)	RM/MU/MUZ/19/0008	31507202388	19.03.2020	63.56	31.53600	56.92500	1.66277	3.13612	7.99952	3.78776	8.79700	25.38317	3.050	0.000	0.000	0.000	0.000	0.000	0.000	3.05	1912.00	1.26916	1.26916	1.26916	1.26916	1.26916	1.26916	6.34579	
3	Dwarika nagar pitch road - Budinagar radha path	RM/MU/MUZ/20/0003	NEA220002677	04.04.2021	87.26	42.29000	75.70900	1.97357	3.96924	11.54505	5.07667	12.91305	35.47758	5.000	0.000	0.000	0.000	0.000	0.000	0.000	5.00	1544.00	1.77388	1.77388					3.54776	
Total																													11.13792	

Executive Engineer
R.W.D. Works Division
Muzaffarpur East-1

File : C:\Users\ABPL\Desktop\30031630.Xls, Section No. : 73, Eqn : $Y = 0 * X^2 + 0.969 * X - 74.60$

Name of Customer : Ami Buildtech Pvt Ltd, Name of Work/ Road : Dwarikanagar Pitch Road to Budhnagra Radha

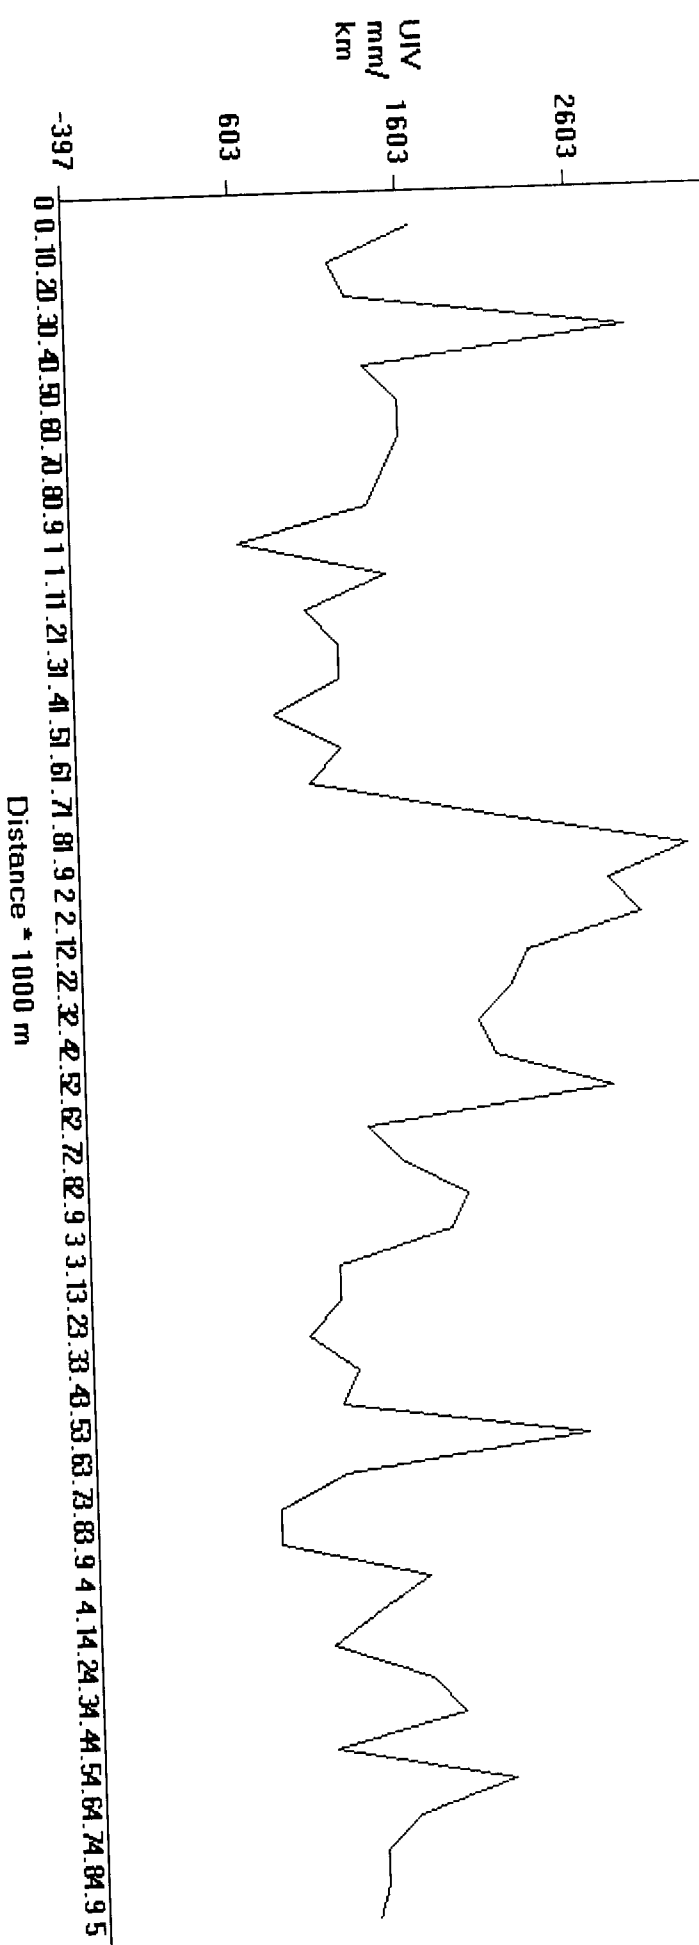

(Ami Buildtech Pvt Ltd)
18/03/22
JS

Smit
28/03/22
(AE)

[Signature]
26.4.22

Dwarikanagar Pitch Road to Budhnagra Radha Path										CATEGORY		Event
Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	UV	ROAD	IRI	Latitude	ongitude	
28/03/22	16: 17: 37	73	0.1	180	0	1800		1669 G	2.38	26.83243	85.49389	Normal
28/03/22	16: 18: 0	73	0.1	130	20.2	1300		1185 G	1.76	26.8375	85.49301	Culvert
28/03/22	16: 18: 12	73	0.1	140	20.2	1400		1281 G	1.88	26.84563	85.49305	Normal
28/03/22	16: 18: 12	73	0.1	310	20.2	3100		2929 G	3.94	26.85373	85.49359	Normal
28/03/22	16: 18: 47	73	0.1	150	20.2	1500		1378 G	2.01	26.8592	85.49293	Normal
28/03/22	16: 19: 0	73	0.1	170	20.2	1700		1572 G	2.26	26.8677	85.49295	Normal
28/03/22	16: 19: 23	73	0.1	170	20.2	1700		1572 G	2.26	26.87693	85.49308	Normal
28/03/22	16: 19: 23	73	0.1	160	20.2	1600		1475 G	2.14	26.88565	85.49343	Normal
28/03/22	16: 19: 23	73	0.1	150	20.2	1500		1378 G	2.01	26.89237	85.49401	Normal
28/03/22	16: 20: 0	73	0.1	70	20.2	700		603 G	0.96	26.8988	85.49333	Normal
28/03/22	16: 20: 0	73	0.1	160	20.2	1600		1475 G	2.14	26.90805	85.49338	Normal
28/03/22	16: 20: 33	73	0.1	110	20.2	1100		991 G	1.5	26.91508	85.49382	Normal
28/03/22	16: 20: 33	73	0.1	130	20.2	1300		1185 G	1.76	26.91945	85.49458	Normal
28/03/22	16: 21: 8	73	0.1	130	20.2	1300		1185 G	1.76	26.92275	85.49529	Normal
28/03/22	16: 21: 8	73	0.1	90	20.2	900		797 G	1.23	26.93105	85.49564	Curve
28/03/22	16: 21: 8	73	0.1	130	20.2	1300		1185 G	1.76	26.94072	85.49574	Curve
28/03/22	16: 21: 44	73	0.1	110	20.2	1100		991 G	1.5	26.94828	85.49525	Normal
28/03/22	16: 22: 0	73	0.1	220	20.2	2200		2057 G	2.87	26.95448	85.49455	Normal
28/03/22	16: 22: 18	73	0.1	340	20.2	3400		3219 G	4.28	26.96138	85.49382	Normal
28/03/22	16: 22: 53	73	0.1	290	20.2	2900		2735 G	3.7	26.968	85.49316	Normal
28/03/22	16: 23: 0	73	0.1	310	20.2	3100		2929 G	3.94	26.975	85.49246	Normal
28/03/22	16: 23: 0	73	0.1	240	20.2	2400		2250 G	3.11	26.98025	85.49165	Normal
28/03/22	16: 23: 29	73	0.1	230	20.2	2300		2154 G	2.99	26.9854	85.49079	Normal
28/03/22	16: 23: 29	73	0.1	210	20.2	2100		1960 G	2.75	26.99225	85.49002	Normal
28/03/22	16: 24: 0	73	0.1	220	20.2	2200		2057 G	2.87	26.99982	85.49019	Normal
28/03/22	16: 24: 4	73	0.1	290	20.2	2900		2735 G	3.7	26.10071	85.49072	Normal
28/03/22	16: 24: 4	73	0.1	140	30.3	1400		1281 G	1.88	26.10142	85.49133	Normal
28/03/22	16: 24: 39	73	0.1	160	30.3	1600		1475 G	2.14	26.10221	85.49195	Normal
28/03/22	16: 24: 39	73	0.1	200	20.2	2000		1863 G	2.63	26.10301	85.49247	Normal
28/03/22	16: 25: 0	73	0.1	190	10.1	1900		1766 G	2.51	26.10322	85.49327	Normal
28/03/22	16: 25: 14	73	0.1	120	20.2	1200		1088 G	1.63	26.1041	85.49357	Normal
28/03/22	16: 25: 14	73	0.1	120	20.2	1200		1088 G	1.63	26.10494	85.49399	Normal
28/03/22	16: 26: 0	73	0.1	100	30.3	1000		894 G	1.37	26.10579	85.49431	Normal
28/03/22	16: 26: 25	73	0.1	130	20.2	1300		1185 G	1.76	26.10603	85.49517	Normal

$$Y = 0 * X^2 + 0.969 * X - 74.60$$

$$X = 1333$$

$$Y = 1217$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Pratik Kumar
 28/03/22
 26
Sumit
 28/03/22
 26
Pratik Kumar
 28/03/22

28/03/22	16: 26: 25	73	0.1	120	20.2	1200	1088 G	1.63	26.10601	85.49618	Normal
28/03/22	16: 27: 0	73	0.1	270	10.1	2700	2541 G	3.47	26.10663	85.497	Normal
28/03/22	16: 27: 0	73	0.1	120	20.2	1200	1088 G	1.63	26.10742	85.49707	Normal
28/03/22	16: 27: 0	73	0.1	80	20.2	800	700 G	1.1	26.10821	85.49761	Normal
28/03/22	16: 27: 35	73	0.1	80	30.3	800	700 G	1.1	26.10909	85.49798	Normal
28/03/22	16: 28: 0	73	0.1	170	10.1	1700	1572 G	2.26	26.10983	85.49774	Normal
28/03/22	16: 28: 11	73	0.1	140	20.2	1400	1281 G	1.88	26.10974	85.49673	Normal
28/03/22	16: 28: 11	73	0.1	110	20.2	1100	991 G	1.5	26.11016	85.49586	Normal
28/03/22	16: 28: 46	73	0.1	170	20.2	1700	1572 G	2.26	26.11096	85.49537	Normal
28/03/22	16: 29: 0	73	0.1	190	20.2	1900	1766 G	2.51	26.11144	85.49458	Normal
28/03/22	16: 29: 0	73	0.1	110	20.2	1100	991 G	1.5	26.11214	85.49512	Normal
28/03/22	16: 29: 21	73	0.1	220	20.2	2200	2057 G	2.87	26.11303	85.49545	Normal
28/03/22	16: 29: 21	73	0.1	160	20.2	1600	1475 G	2.14	26.11367	85.49498	Normal
28/03/22	16: 30: 0	73	0.1	140	20.2	1400	1281 G	1.88	26.11396	85.49401	Normal
28/03/22	16: 30: 0	73	0.1	140	20.2	1400	1281 G	1.88	26.11419	85.49295	Normal
28/03/22	16: 30: 0	73	0.015	20	50.5	1333	1217 G	1.8	26.11422	85.49279	Normal
		AVG									
						1544					

Kim Gurni
 28/3/2022
 15

Smith
 28/03/22
 AC

John
 28.4.22

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-I

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From-Dwarika nagar pitch road - Budhnagar radha path
Length of Road: 5.00 KM
Periode : From.....
Inspector: A.E RWD Sub Division, Mushari

To: Executive Engineer
RWD Works Division Muzaffarpur East-1
Position: A.E

Date:

S No	Standard Work item	Work Units	Units of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM101	OM100 Sealed Pavement												
	Pothole Patching	m2	Nil	Nil	Nil	Nil							No Pothole found.
	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
OM200 Shoulder	Other activities	Lm											
	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
OM202	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil												Not Required
	OM 400 Vegetation																	
	Grass Contorol																	
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil												Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil												Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil												Not Required
OM402	Cutting trees	No	Nil	Nil	Nil	Nil												Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil												Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil												Not Required
OM500	Safety Signage and Road																	Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil												Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A												Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A												Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil												Not Required
	Other activities																	

Prithvika Kumari
Bidder

Prithvika Kumari
28/07/22
28/07/22
PC

Prithvika Kumari
Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East I

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Dwarika nagar pitch road - Budhnagar radha path		
2	Batch No.	RM/MU/MUZ/20/0003		
3	Project ID	NEA220002677		
4	Total Length of Road (in Km)	5		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	35.47758		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.77388		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.77388

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/1 (signature) Date
