

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :- 1194/28/मुज0.

दिनांक :- 25/7/22

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
-सह-सचिव,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय:- शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु
आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु0 19.68118 (उन्नीस लाख अड़सठ हजार एक सौ अठारह) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये कार्य का भुगतान किया जा सके।

अनुलग्नक- 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Name of Works Division:- Muzaffarpur West

5-102
Executive Engineer
R.W.D. Works Division
Muzaffargarh West

Requisition Format for Scheme Head - M/R (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur West

Government of Bihar

OM01

Rural works Department

Road From: BARDABI PUL - BANJARIA PAGHIA HARDI PUL

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Muzaffarpur West

Date:

Length of Road- 2.400 KM

Period : From:

Inspector: A. E RWD Sub Division, Motipur

Position: A. E

Standard Work item				Work Units	Units of work required in each kilometre										Comments
S No	Name		Units	1	2	3	4	5	6	7	8	9	10		
OM101	OM100 Sealed Pavement													No. Pothole found	
	Pothole Patching			m2	Nil	Nil	Nil	Nil						No Surface Depression and Rut Patching found	
	Surface Depression and Rut Patching			m2	Nil	Nil	Nil	Nil						No Crack Sealing found	
	Crack Sealing			km	Nil	Nil	Nil	Nil							
OM104	Surface Treatment													No Loss of Aggregate (Surface Ravelling) found	
	(a) Loss of Aggregate (Surface Ravelling)			m2	Nil	Nil	Nil	Nil						No Bleeding/Flushing Required	
	(b) Bleeding/Flushing			m2	Nil	Nil	Nil	Nil						No Crocodile Cracking found	
	(c) Crocodile Cracking			m2	Nil	Nil	Nil	Nil							
OM105	Edge Repair			m2	Nil	Nil	Nil	Nil						No Edge Repair Required	
OM106	Digouts			m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement			m3	N/A	N/A	N/A	N/A							
Other activities				Lm											
OM200 Shoulder															
OM201	Unsealed Shoulder			No											
	(a) Edge Drop off			Lm	Nil	Nil	Nil	Nil						No Edge Drop off Required	
	(b) Roughness, Scouring or Potholes			Lm	Nil	3%	2%	Nil						Defects rectified within stipulated time.	
	(c) Holding Water			Lm	Nil	Nil	Nil	Nil						No Holding water found	
	Embankment Repair			No	Nil	Nil	Nil	Nil						No Embankment Repair Required	
OM202	Other Activities (Raincut)				3%	1%	2%							Defects rectified within stipulated time.	
OM 300 Drainage including culverts major															
OM301	Surface Drains & Verge			Lm	N/A	N/A	N/A	N/A						Not Required	
OM302	Culvert Cleaning			Lm										Culvert maintain within stipulated time	
OM303	Culvert and Pit repair			m2	Nil	Nil	Nil	Nil						Not Required	

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil	Nil												Not Required
	OM 400 Vegetation																		
	Grass Contour																		Not Required
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil												Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil												Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil	Nil												Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil	Nil												Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil												Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil	Nil												Not Required
OM500	Safety Signage and Road																		Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil												Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A	N/A												Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A	N/A												Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil	Nil												Not Required
	Other activities																		

Bidder

Appendix

Executive Engineer, Rural Work Department,
Work Division, Muzaffarpur West

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	BARDAHI PUL - BANJARIA PAGHIA HARDI PUL		
2	Batch No.	RM/MU/MUZ/19/0026		
3	Project ID	31507202054		
4	Total Length of Road (in Km)	2.400		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.400		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	18.56110		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.92806		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.92806

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certify by E/1 (Signature) Date
Rural Work's Department
Nork's Division Muraharpur West


Name Of Road:-BARDAHI PUL - BANJARIA PAGHIA HARDI PUL

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	ORn MM/Km	TEGORY UIV	Latitude	ongitude	Event	Y = 0 * X ^ 2 + 0.989 * X - 13.58
15/ 6/ 22	16: 29: 0	29	0.1	310	20.2	3100	3052 G	26.11506	85.41793	Normal	X = 2900
15/ 6/ 22	16: 29: 53	29	0.1	300	20.2	3000	2953 G	26.11532	85.41882	Normal	Y = 2854
15/ 6/ 22	16: 30: 0	29	0.1	230	20.2	2300	2261 G	26.11609	85.41916	Normal	
15/ 6/ 22	16: 30: 28	29	0.1	200	20.2	2000	1964 G	26.117	85.41939	Normal	
15/ 6/ 22	16: 30: 38	29	0.1	240	20.2	2400	2360 G	26.11793	85.41949	Normal	(R) RURAL ROAD
15/ 6/ 22	16: 31: 4	29	0.1	280	20.2	2800	2755 G	26.11863	85.42	Normal	Good Average Poor
15/ 6/ 22	16: 31: 14	29	0.1	210	20.2	2100	2063 G	26.11901	85.42098	Normal	<4000 4001-5000 >5001
15/ 6/ 22	16: 31: 39	29	0.1	170	20.2	1700	1667 G	26.11929	85.42194	Normal	
15/ 6/ 22	16: 31: 49	29	0.1	220	20.2	2200	2162 G	26.11977	85.42279	Bridge	
15/ 6/ 22	16: 32: 0	29	0.1	310	20.2	3100	3052 G	26.12043	85.42357	Normal	
15/ 6/ 22	16: 32: 14	29	0.1	300	20.2	3000	2953 G	26.12127	85.42375	Normal	
15/ 6/ 22	16: 32: 25	29	0.1	230	20.2	2300	2261 G	26.12214	85.42401	Speed Breaker	
15/ 6/ 22	16: 32: 50	29	0.1	200	20.2	2000	1964 G	26.12277	85.4247	Normal	
15/ 6/ 22	16: 33: 0	29	0.1	240	20.2	2400	2360 G	26.12331	85.42551	Curve	
15/ 6/ 22	16: 33: 25	29	0.1	270	10.1	2700	2656 G	26.12405	85.42519	Normal	
15/ 6/ 22	16: 33: 29	29	0.1	210	20.2	2100	2063 G	26.1244	85.42433	Normal	
15/ 6/ 22	16: 34: 0	29	0.1	170	20.2	1700	1667 G	26.12487	85.42377	Normal	
15/ 6/ 22	16: 34: 10	29	0.1	290	10.1	2900	2854 G	26.12485	85.42276	Normal	
15/ 6/ 22	16: 34: 35	29	0.1	290	20.2	2900	2854 G	26.12497	85.42177	Normal	
15/ 6/ 22	16: 34: 43	29	0.1	330	20.2	3300	3250 G	26.12496	85.42074	Normal	
15/ 6/ 22	16: 34: 52	29	0.1	300	0	3000	2953 G	26.11579	85.41699	Speed Breaker	
15/ 6/ 22	16: 35: 03	29	0.1	290	10.1	2900	2854 G	26.11555	85.41801	Normal	
15/ 6/ 22	16: 35: 15	29	0.1	190	10.1	1900	1865 G	26.1153	85.41897	Normal	
15/ 6/ 22	16: 35: 22	29	0.1	290	10.1	2900	2854 G	26.11511	85.41993	Normal	
					Avg	2487.375					

16/9/22
AF

5/12
25/07/22
Executive Engineer
Rural Work's Department
Work's Division Muzaffarour West

File : C:\Users\RWD\OneDrive\Desktop\Singh Const\01051639.Xls. Section No. :22, Eqn : $Y = 0 * X^2 + 0.989 * X$
Name of Customer : Singh Construction Private Limited, Name of Work/ Road : BARDAHI PUL - BANJARIA PAGHIA

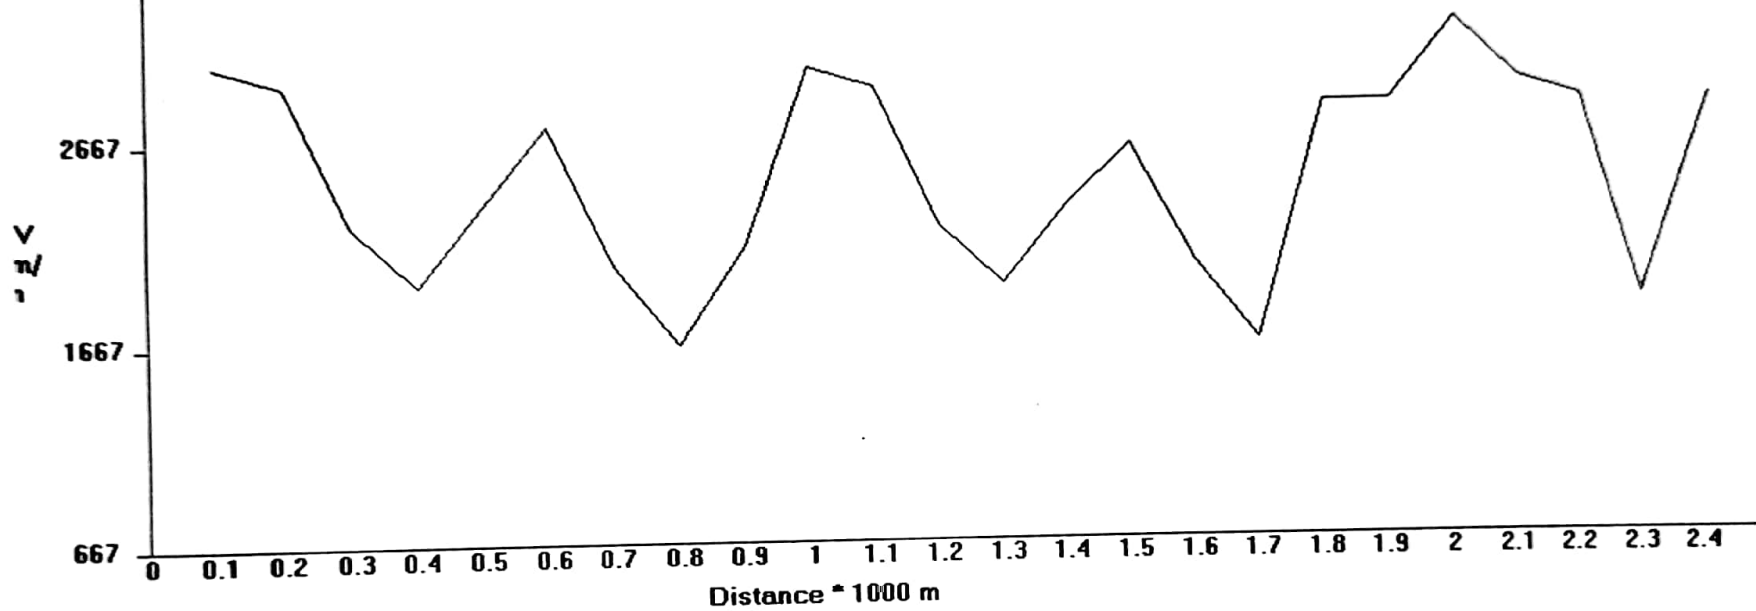

18/1/22

Signature
35107122
Executive Engineer
Rural Work's Department
Work's Division, Muzaffargarh West
