

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :- 1194/28/मुज0.

दिनांक :- 25/7/22

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
-सह-सचिव,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय:- शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु
आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष
2022-23 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु0 19.68118 (उन्नीस लाख अड़सठ
हजार एक सौ अठारह) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये
कार्य का भुगतान किया जा सके।

अनुलग्नक- 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Name of Works Division:- Muzaffarpur West

Scanned with CamScanner

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur West

Government of Bihar

OM01

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Rural works Department

Road From: Brahmnpura high school NHPC Road - Masurpur REO road near Nand kishor

singh house via Brahmnpura vill

To: Executive Engineer

RWD Works Division Muzaffarpur West

Date:

Length of Road-

2.840 KM

Period : From.....

Inspector: A.E RWD Sub Division, Motipur

Position: A.E

S No	Standard Work item		Work Units	Units of work required in each kilometre										Comments
	Name			1	2	3	4	5	6	7	8	9	10	
OM101	OM100 Sealed Pavement													
	Pothole Patching		m2	Nil	Nil	Nil	Nil							No. Pothole found.
	Surface Depression and Rut Patching		m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
	Crack Sealing		Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment													
	(a) Loss of Aggregate (Surface Ravelling)		m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing		m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking		m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair		m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts		m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement		m3	N/A	N/A	N/A	N/A							
OM200 Shoulder	Other activities		Lm											
	Unsealed Shoulder		No											
	(a) Edge Drop off		Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes		Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
OM201	(c) Holding Water		Lm	Nil	Nil	Nil	Nil							No Holding water found
	Embankment Repair		No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Active (Raincut)			3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge		Lm	N/A	N/A	N/A	N/A							
OM302	Culvert Cleaning		Lm											Not Required
OM303	Culvert and Pit repair		m2	Nil	Nil	Nil	Nil							Culvert maintain within stipulated time

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM 400 Vegetation																			
OM401	Grass Controll																		Not Required
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM402	Cutting trees	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Safety Signage and Road																		Not Required
OM500	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities																		

Bidder

Appendix

Executive Engineer, Rural Work Department,
Work Division, Muzaffarpur West

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Brahmpura high school NHPC Road - Masurpur REO road near Nand kishor singh house via Brahmpura vill		
2	Batch No.	RM/MU/MUZ/19/0026		
3	Project ID	31507202088		
4	Total Length of Road (in Km)	2.840		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.840		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	22.26282		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.11314		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.11314

Date of inpection by E/I or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certify by E/I (signature) Date
Executive Engineer
Rular Work's Department
Work's Division Muzaffarpur West

Name Of Road:-Brahmpura high school NHPC Road - Masurpur REO road near Nand kishor singh house via Brahmpura vill

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI In MM/Km UIV	CATEG ORY ROAD	Latitude	Longitu de	Event
18/6/22	12:17:0	81	0.1	150	0	1500	1469 G		26.739	85.22053	Normal
18/6/22	12:17:15	81	0.1	200	10.1	2000	1964 G		26.6478	85.2143	Normal
18/6/22	12:17:32	81	0.1	260	20.2	2600	2557 G		26.5593	85.21615	Normal
18/6/22	12:18:7	81	0.1	300	10.1	3000	2953 G		26.506	85.22508	Normal
18/6/22	12:18:0	81	0.1	180	10.1	1800	1766 G		26.4568	85.23	Normal
18/6/22	12:19:16	81	0.1	260	10.1	2600	2557 G		26.4148	85.24275	Normal
18/6/22	12:19:46	81	0.1	170	10.1	1700	1667 G		26.3555	85.2508	Normal
18/6/22	12:20:0	81	0.1	230	10.1	2300	2261 G		26.3322	85.26093	Normal
18/6/22	12:20:27	81	0.1	250	20.2	2500	2458 G		26.3412	85.27137	Normal
18/6/22	12:20:47	81	0.1	300	10.1	3000	2953 G		26.3448	85.2837	Normal
18/6/22	12:21:2	81	0.1	330	10.1	3300	3250 G		26.35	85.29443	Normal
18/6/22	12:21:38	81	0.1	370	10.1	3700	3645 G		26.3023	85.30437	Normal
18/6/22	12:22:13	81	0.1	300	10.1	3000	2953 G		26.2157	85.30723	Normal
18/6/22	12:22:33	81	0.1	280	10.1	2800	2755 G		26.1762	85.3172	Normal
18/6/22	12:23:0	81	0.1	220	10.1	2200	2162 G		26.908	85.31985	Normal
18/6/22	12:23:23	81	0.1	300	10.1	3000	2953 G		26.63	85.3168	Normal
18/6/22	12:24:0	81	0.1	200	10.1	2000	1964 G		26.47	85.3168	Normal
18/6/22	12:25:0	81	0.1	190	10.1	1900	1865 G		26.1153	85.41897	Normal
18/6/22	12:25:16	81	0.1	170	10.1	1700	1667 G		26.11511	85.41993	Normal
18/6/22	12:25:46	81	0.1	230	10.1	2300	2261 G		26.1148	85.42093	Normal
18/6/22	12:26:0	81	0.1	250	20.2	2500	2458 G		26.11444	85.42185	Normal
18/6/22	12:26:27	81	0.1	260	20.2	2600	2557 G		26.11416	85.42278	Normal
18/6/22	12:26:47	81	0.1	310	20.2	3100	3052 G		26.11407	85.42384	Normal
18/6/22	12:27:2	81	0.1	230	20.2	2300	2261 G		26.11419	85.42483	Normal
18/6/22	12:27:38	81	0.1	300	20.2	3000	2953 G		26.3023	85.30437	Normal
18/6/22	12:28:13	81	0.1	230	20.2	2300	2261 G		26.2157	85.30723	Normal
18/6/22	12:28:33	81	0.1	330	10.1	3300	3250 G		26.1762	85.3172	Normal
18/6/22	12:29:0	81	0.1	370	10.1	3700	3645 G		26.908	85.31985	Normal
18/6/22	12:29:23	81	0.1	300	10.1	3000	2953 G		26.11463	85.42785	Normal

Avg 2533.44

$$Y = 0 * X^2 + 0.989 * X - 13.58$$

$$X = 3000$$

$$Y = 2953$$

(R) RURAL ROAD


Good Average Poor

<4000 4001-5000 >5001

16.07.22
SE

18/7/22
A/E

Executive Engineer
Rural Work's Department
Work's Division, Muzaffarpur West

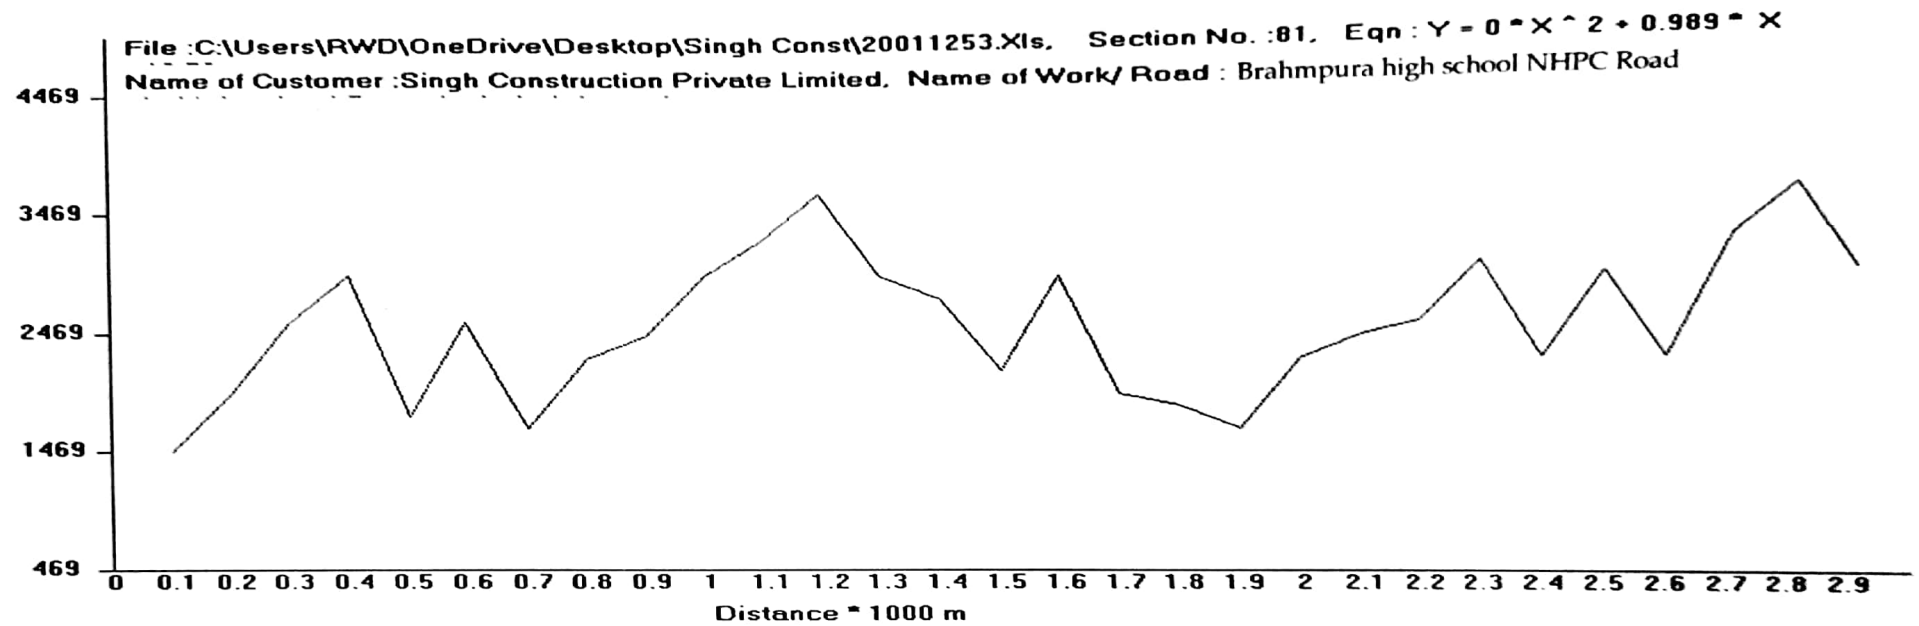

18/1/22
A/E

Executive Engineer
 Rural Work's Department
 Work's Division, Muzaffarpur West
