

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :- 1194/28/मुज०,

दिनांक :- 25/7/22

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
-सह-सचिव,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय:- शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु
आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष
2022-23 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु० 19.68118 (उन्नीस लाख अड़सठ
हजार एक सौ अठारह) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये
कार्य का भुगतान किया जा सके।

अनुलग्नक- 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Name of Works Division:- Muzaffarpur West

Scanned with CamScanner

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur West

Government of Bihar

OM01

Rural works Department

Road From — Dora Chhapra - Hardi Bazar Path

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Muzaffarpur West

Date:

Length of Road-

3.400 KM

Period : — From.....

Position: A.E

Inspector: — A.E RWD Sub Division, Motipur

Inspector:-----		A.E RWD Sub Division,		Municipal		Units of work required in each kilometre										Comments
Standard Work item		Work	Units	1	2	3	4	5	6	7	8	9	10			
S No		Name														
OM100		Sealed Pavement													No. Pothole found.	
OM101		Pothole Patching	m2	Nil	Nil	Nil	Nil								No Surface Depression and Rut Patching found	
OM102		Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil								No Crack Sealing found	
OM103		Crack Sealing	Lm	Nil	Nil	Nil	Nil								No Loss of Agregate (Surface Ravelling) found	
OM104		Surface Treatment													No Bleeding/Flushing Required	
		(a) Loss of Agregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking found	
		(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil								
		(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil								No Edge Repair Required	
OM105		Edge Repair	m2	Nil	Nil	Nil	Nil									
OM106		Dipouts	m2	N/A	N/A	N/A	N/A	N/A								
OM107		Concrete Pavement	m3	N/A	N/A	N/A	N/A									
		Other activities	Lm													
OM200 Shoulder																
OM201		Unsealed Shoulder	No												No Edge Drop off Required	
		(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil								Defects rectified within stipulated time.	
		(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil								No Holding water found	
		(c) Holding Water	Lm	Nil	Nil	Nil	Nil								No Embankment Repair Required	
		Embankment Repair	No	Nil	Nil	Nil	Nil								Defects rectified within stipulated time.	
OM202		Other Activite (Raincut)		3%	1%	2%										
OM 300 Drainage including culverts major															Not Required	
OM301		Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A								Culvert maintain within stipulated time	
OM302		Culvert Cleaning	Lm													
OM303		Culvert and Pit repair	m2	Nil	Nil	Nil	Nil	Nil							Not Required	

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil													Not Required
	OM 400 Vegetation																		
	Grass Contorol																		
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil													Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil													Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil													Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil													Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil													Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil													Not Required
OM500	Safety Signage and Road																		Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil													Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A													Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A													Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil													Not Required
	Other activities																		

Bidder

Appendix

Executive Engineer, Rural Work Department,
Work Division, Muzaffarpur West

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Dora Chhapra - Hardi Bazar Path		
2	Batch No.	RM/MU/MUZ/19/0009		
3	Project ID	NEA220002626		
4	Total Length of Road (in Km)	3.400		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.400		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	26.59746		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.32987		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.32987

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/1 (Signature) Date
Rular Work's Department
Work's Division Muzaffarpur West


Name Of Road:-Dora Chhapra - Hardi Bazar Path

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI IN MM/Km	CATEG ORY ROAD	Latitude	Longitu de	Event	
24/ 6/ 22	12: 8: 8	37	0.1	150	0	1500	1469	G	26.5108	85.39737	Normal	$Y = 0 * X^2 + 0.989 * X - 13.58$
24/ 6/ 22	12: 8: 8	37	0.1	120	30.3	1200	1173	G	26.50965	85.398	Normal	$X = 1900$
24/ 6/ 22	12: 8: 8	37	0.1	190	30.3	1900	1865	G	26.5096	85.39936	Normal	$Y = 1865$
24/ 6/ 22	12: 8: 44	37	0.1	170	20.2	1700	1667	G	26.50788	85.40042	Normal	
24/ 6/ 22	12: 9: 0	37	0.1	120	20.2	1200	1173	G	26.50058	85.40082	Normal	(R) RURAL ROAD
24/ 6/ 22	12: 9: 19	37	0.1	170	20.2	1700	1667	G	26.49138	85.40109	Normal	Good Average Poor
24/ 6/ 22	12: 9: 19	37	0.1	230	20.2	2300	2261	G	26.48507	85.40173	Normal	<4000 4001-5000 >5001
24/ 6/ 22	12: 9: 54	37	0.1	230	10.1	2300	2261	G	26.4789	85.40231	Normal	
24/ 6/ 22	12: 10: 0	37	0.1	200	20.2	2000	1964	G	26.47537	85.40328	Normal	
24/ 6/ 22	12: 10: 29	37	0.1	160	10.1	1600	1568	G	26.46823	85.40392	Curve	
24/ 6/ 22	12: 10: 29	37	0.1	200	10.1	2000	1964	G	26.4668	85.40492	Normal	
24/ 6/ 22	12: 11: 5	37	0.1	230	20.2	2300	2261	G	26.46528	85.40589	Normal	
24/ 6/ 22	12: 11: 5	37	0.1	190	20.2	1900	1865	G	26.4655	85.40692	Normal	
24/ 6/ 22	12: 11: 5	37	0.1	160	30.3	1600	1568	G	26.46462	85.40793	Normal	
24/ 6/ 22	12: 11: 40	37	0.1	160	20.2	1600	1568	G	26.45825	85.40823	Normal	
24/ 6/ 22	12: 12: 0	37	0.1	180	20.2	1800	1766	G	26.44882	85.40813	Culvert	
24/ 6/ 22	12: 12: 15	37	0.1	280	10.1	2800	2755	G	26.43947	85.40793	Normal	
24/ 6/ 22	12: 12: 51	37	0.1	170	10.1	1700	1667	G	26.43085	85.40811	Normal	
24/ 6/ 22	12: 13: 0	37	0.1	90	60.6	1071	1045	G	26.429	85.40825	Normal	
24/ 6/ 22	12: 14: 0	37	0.1	300	10.1	3000	2953	G	26.3448	85.2837	Normal	
24/ 6/ 22	12: 14: 19	37	0.1	330	10.1	3300	3250	G	26.35	85.29443	Normal	
24/ 6/ 22	12: 14: 19	37	0.1	370	10.1	3700	3645	G	26.3023	85.30437	Normal	
24/ 6/ 22	12: 14: 54	37	0.1	300	10.1	3000	2953	G	26.2157	85.30723	Normal	
24/ 6/ 22	12: 15: 0	37	0.1	280	10.1	2800	2755	G	26.1762	85.3172	Normal	
24/ 6/ 22	12: 15: 29	37	0.1	220	10.1	2200	2162	G	26.908	85.31985	Normal	
24/ 6/ 22	12: 15: 29	37	0.1	300	10.1	3000	2953	G	26.63	85.3168	Normal	
24/ 6/ 22	12: 16: 5	37	0.1	200	10.1	2000	1964	G	26.47	85.3168	Normal	
24/ 6/ 22	12: 16: 5	37	0.1	190	10.1	1900	1865	G	26.1153	85.41897	Normal	
24/ 6/ 22	12: 16: 5	37	0.1	170	10.1	1700	1667	G	26.11511	85.41993	Normal	
24/ 6/ 22	12: 17: 40	37	0.1	230	10.1	2300	2261	G	26.1148	85.42093	Normal	
24/ 6/ 22	12: 18: 0	37	0.1	250	20.2	2500	2458	G	26.11444	85.42185	Normal	
24/ 6/ 22	12: 18: 15	37	0.1	260	20.2	2600	2557	G	26.11416	85.42278	Normal	
24/ 6/ 22	12: 18: 51	37	0.1	310	20.2	3100	3052	G	26.11407	85.42384	Normal	
24/ 6/ 22	12: 19: 0	37	0.1	190	10.1	1900	1865	G	26.1153	85.41897	Normal	
						Avg	2114.32					

Sila
3510712
Executive Engineer
Rural Work's Department
Work's Division Muzaffarpur West

18/7/22

File : C:\Users\RWD\OneDrive\Desktop\Singh Const\29111213.Xls, Section No. : 66, Eqn : $Y = 0 \cdot X^2 + 0.989 \cdot X$
 Name of Customer : Singh Construction Private Limited, Name of Work/ Road : Dora Chhapra - Hardi Bazar Path,

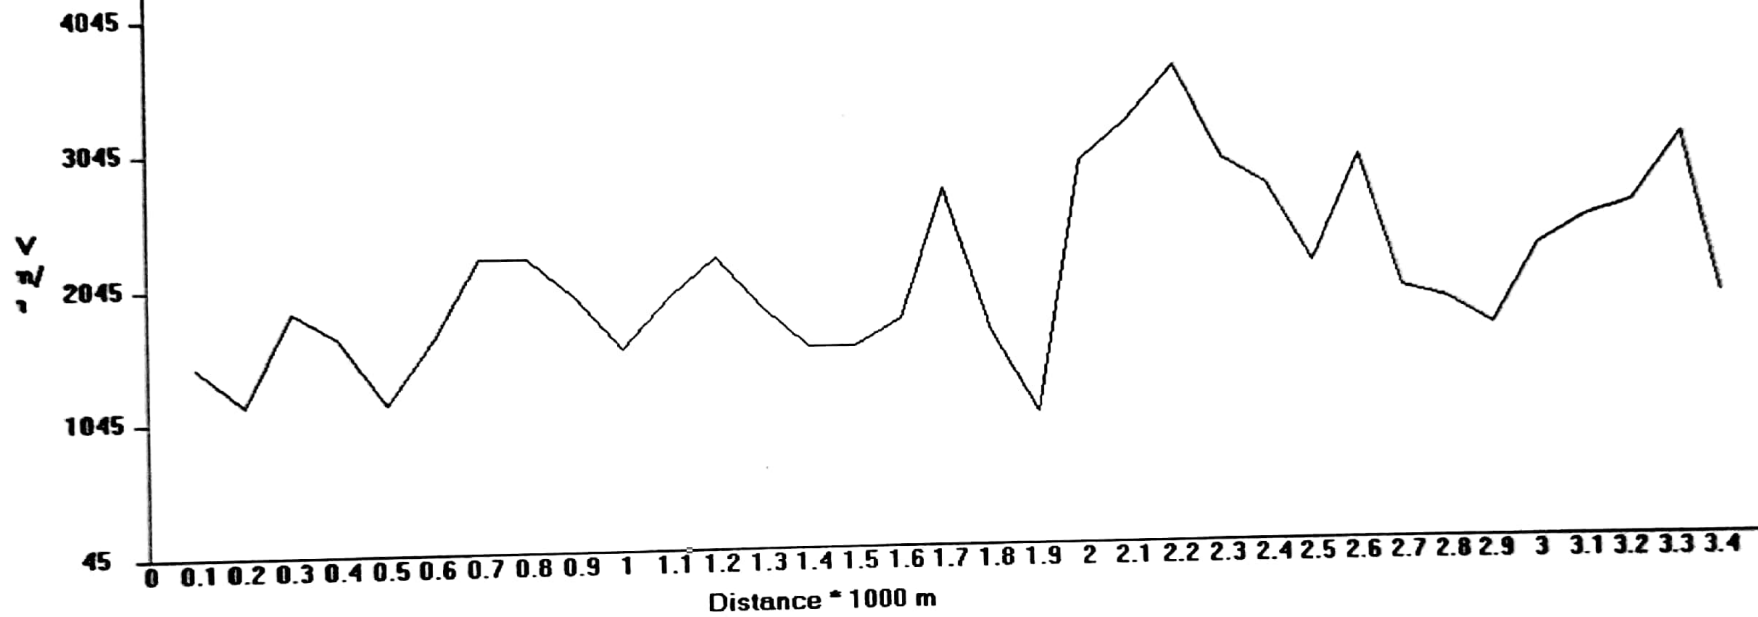

18/8/22
 A Z

Singh
 25/07/22
 EXECUTIVE ENGINEER
 Rural Work's Department
 Work's Division, Muzaffarpur West
