

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नवादा।

पत्रांक :- 855 [अ३०]

/नवादा, दिनांक :- 17.06.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नवादा।

सेवा में,

नोडल पदाधिकारी (एम0आर0-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय: New Maintenance Policy-2018 योजना अन्तर्गत अनुरक्षण मद अन्तर्गत
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय से संबंधित विहित प्रपत्र में वांछित सूचना उपलब्ध कराते हुए
अनुरोध है आवंटन उपलब्ध कराने की कृपा की जाय।
अनु0- यथोक्त।

विश्वासभाजन,

[Signature]
17.6.2022

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नवादा।

Maintenance Requisition Formate for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal) As Per State MIS
Name of works Division- Nawada

Road Details				A.A Details		Agreement Details										Actual Maintenance Expenditure										Previous		Current Demand for Maintenance Amount (In Lacs)										Remarks
Sl No.	Road Name	Batch No.	Project ID	Actual Date of Completion	Major work amount	Maintenance amount	Major Work Amount	Maintenance Agreement Amount 1st year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Station amount	Length	1st Year State Exp.	2nd Year State Exp.	3rd Year State Exp.	4th Year State Exp.	5th Year State Exp.	Total 1st quarter	Total 2nd quarter	Total 3rd quarter	DD Aa For 1st quarter	DD Aa For 2nd quarter	DD Aa For 3rd quarter	DD Aa For 4th quarter	Total											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31								
1	AKUNA-URSA	RNUNA/NA W/19/0003	10502602026	7/10/2020	139.35	78.253	135.843	4.55078	7.09625	17.1119	9.382	18.6958	56.83676	6.200	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	6.200	2855	0.00000	2.84184	0.00000	0.00000	2.84184	2nd QUARTER								
Total					139.35	78.253	135.843	4.55078	7.09625	17.1119	9.382	18.6958	56.83676	6.2	0	0	0	0	0	0	0	0	6.2		0	2.84184	0	0	2.84184									

Executive Engineer
 RWD Works Division, Nawada

[Signature]
 27-6-2022

FORM GFR -19A

(See Government of India's Decision (I) below Rule-150)

Name of PIU: Rural Works Department, Works Division, Nawada

Head: New Maintenance
Policy-2018 (MR-3054)
(Maintenance Fund)

Form of Utilization Certificate for the month of June-2022

SL. No.	Name of Scheme	Sanctioned No. & Date	Amount (Rs.)	Particulars
1	Construction of Rural Roads under New Maintenance Policy-2018 (MR-3054) (Maintenance Fund)	-	=	Certified that out of <u>Rs.Nil/-</u> Of grants upto the year 2022-23 in favour of RWD (W) Division, Nawada (bihar) a sum of <u>Rs. Nil/</u> has been utilized for the purpose Schemes as given in margin for which it was given in which it was sanctioned and that the balance <u>Rs Nil/-</u> remaining unutilized at the end of the period under report.

2. certified that I have satisfied myself that the conditions on which the grants in aid was sanctioned have been duly fulfilled / are being fulfilled and that I have exercised the following checks to see that money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:

- (i) Works have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer
- (iii) Construction materials have been tested
- (iv) Measurements have been recorded in MBs and test check conducted by the Assistant Engineer/ Executive Engineer
- (v) All other codal formalities have been observed
- 3 **Physical Progress achieved**
- (i) Construction of Road works
- (ii) Construction of CD works

[Signature]
7.6.2022
Executive Engineer
RWD(W) Division, Nawada

2nd Quarter

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : Rural Works Department, Works Division, Nawada

1	Name of Road	AKUNA To URSA		
2	Batch No.	RM/NA/NAW/19/0003		
3	Project ID	10502602026		
4	Total Length of Road (in Km)	6.20		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	6.20		
6	No. of Total Quarte (ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	56.83676		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.84184		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non - Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANKEMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.84184

Date of inspection by/E/I or his agent

Prepared by Contractor's self Control Unit

[Signature]

[Signature]
18/6/22
Ran

Date

Signature of person inspecting road

Name and Designation of Executive Engineer

[Signature]
16.6.2022
(Signature)

Certify by E/I [signature] Date :

Name of Road- AKUNA To URSA

Name of Contractor- SUJAY BHAN SINGH										Batch No- RM/NA/NAW/19/0003				
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
29/7/22	12: 58: 0	60	0.1	370	10.1	3700	3713	G	24.93939	85.53367	Speed Breaker	Y = 0 * X ^ 2 + 0.936 * X + 278.4		
29/7/22	12: 58: 6	60	0.1	350	20.2	3500	3554	G	24.9396	85.534612	Normal	X = 6596		
29/7/22	12: 58: 6	60	0.1	300	30.3	3000	3022	G	24.93963	85.535555	Normal	Y = 6452		
29/7/22	12: 58: 6	60	0.1	320	30.3	3200	3209	G	24.93911	85.536363	Normal	(R) RURAL ROAD		
29/7/22	12: 58: 41	60	0.1	300	30.3	3000	3022	G	24.93849	85.537087	Normal	Good	Average	Poor
29/7/22	12: 59: 0	60	0.1	380	20.2	3800	3835	G	24.93787	85.537827	Speed Breaker	<4000	4001-5000	>5001
29/7/22	12: 59: 17	60	0.1	330	20.2	3300	3367	G	24.93726	85.53847	Normal			
29/7/22	12: 59: 17	60	0.1	330	30.3	3300	3341	G	24.93666	85.539123	Normal			
29/7/22	12: 59: 17	60	0.1	370	10.1	3700	3741	G	24.93597	85.539797	Speed Breaker			
29/7/22	13: 0: 0	60	0.1	350	10.1	3500	3575	G	24.93532	85.54047	Speed Breaker			
29/7/22	13: 0: 27	60	0.1	320	10.1	3200	3209	G	24.93475	85.541093	Normal			
29/7/22	13: 0: 27	60	0.1	280	30.3	2800	2899	G	24.93394	85.541463	Normal			
29/7/22	13: 1: 0	60	0.1	310	30.3	3100	3116	G	24.93301	85.541463	Normal			
29/7/22	13: 1: 3	60	0.1	350	10.1	3500	3590	G	24.9321	85.541447	Speed Breaker			
29/7/22	13: 1: 3	60	0.1	310	20.2	3100	3180	G	24.93126	85.54143	Normal			
29/7/22	13: 1: 38	60	0.1	290	30.3	2900	2992	G	24.93036	85.541447	Normal			
29/7/22	13: 2: 0	60	0.1	320	10.1	3200	3207	G	24.92948	85.541565	Speed Breaker			
29/7/22	13: 2: 13	60	0.1	300	30.3	3000	3041	G	24.92864	85.54175	Normal			

30/07/22
 30/07/22 (acc)
 ETE

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
29/7/22	13: 2: 13	60	0.1	310	20.2	3100	3103	G	24.92778	85.541935	Normal			
29/7/22	13: 2: 13	60	0.1	280	20.2	2800	2875	G	24.92694	85.542137	Normal			
29/7/22	13: 3: 0	60	0.1	310	10.1	3100	3116	G	24.92603	85.542357	Normal			
29/7/22	13: 3: 0	60	0.1	270	20.2	2700	2777	G	24.92518	85.542542	Normal			
29/7/22	13: 3: 24	60	0.1	320	20.2	3200	3245	G	24.92436	85.542727	Normal			
29/7/22	13: 3: 24	60	0.1	320	30.3	3200	3209	G	24.92347	85.542928	Normal			
29/7/22	13: 4: 0	60	0.1	310	20.2	3100	3148	G	24.92258	85.54313	Normal			
29/7/22	13: 4: 0	60	0.1	290	20.2	2900	2972	G	24.92173	85.543332	Normal			
29/7/22	13: 4: 34	60	0.1	270	20.2	2700	2713	G	24.92088	85.54348	Normal			
29/7/22	13: 4: 34	60	0.1	330	30.3	3300	3367	G	24.92006	85.543872	Normal			
29/7/22	13: 4: 34	60	0.1	320	20.2	3200	3245	G	24.91941	85.544528	Normal			
29/7/22	13: 5: 10	60	0.1	320	20.2	3200	3209	G	24.91899	85.545353	Normal			
29/7/22	13: 5: 10	60	0.1	240	30.3	2400	2424	G	24.91879	85.546245	Normal			
29/7/22	13: 5: 10	60	0.1	270	30.3	2700	2705	G	24.91895	85.547188	Normal			
29/7/22	13: 5: 10	60	0.1	350	30.3	3500	3554	G	24.91914	85.548182	Normal			
29/7/22	13: 5: 45	60	0.1	270	30.3	2700	2777	G	24.91933	85.549123	Normal			
29/7/22	13: 6: 0	60	0.1	270	20.2	2700	2751	G	24.91956	85.55007	Normal			
29/7/22	13: 6: 20	60	0.1	270	20.2	2700	2732	G	24.92012	85.550892	Normal			
29/7/22	13: 11: 1	60	0.1	340	20.2	3400	3468	G	24.92068	85.551548	Normal			
29/7/22	13: 11: 1	60	0.1	320	10.1	3200	3243	G	24.92134	85.552272	Normal			
29/7/22	13: 11: 37	60	0.1	380	10.1	3800	3807	G	24.92193	85.552945	Speed Breaker			
29/7/22	13: 12: 12	60	0.1	360	10.1	3600	3639	G	24.92252	85.553618	Speed Breaker			
29/7/22	13: 12: 47	60	0.1	360	20.2	3600	3615	G	24.92316	85.554325	Speed Breaker			
29/7/22	13: 13: 0	60	0.1	340	20.2	3400	3496	G	24.92375	85.554998	Speed Breaker			

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event				
29/7/22	13:13:23	60	0.1	350	10.1	3500	3552	G	24.92438	85.55569	Speed Breaker				
29/7/22	13:14:0	60	0.1	360	10.1	3600	3645	G	24.92498	85.556447	Speed Breaker				
29/7/22	13:14:0	60	0.1	320	20.2	3200	3209	G	24.9255	85.557087	Normal				
29/7/22	13:14:33	60	0.1	340	20.2	3400	3496	G	24.92612	85.557895	Normal				
29/7/22	13:14:33	60	0.1	290	30.3	2900	2992	G	24.92665	85.558552	Normal				
29/7/22	13:14:33	60	0.1	320	30.3	3200	3273	G	24.92727	85.559343	Normal				
29/7/22	13:15:8	60	0.1	340	20.2	3400	3460	G	24.92785	85.56007	Normal				
29/7/22	13:15:8	60	0.1	280	30.3	2800	2899	G	24.92841	85.56079	Normal				
29/7/22	13:15:8	60	0.1	300	30.3	3000	3086	G	24.92902	85.561565	Normal				
29/7/22	13:15:8	60	0.1	370	30.3	3700	3741	G	24.92959	85.562272	Normal				
29/7/22	13:15:44	60	0.1	320	30.3	3200	3273	G	24.93016	85.562995	Normal				
29/7/22	13:16:0	60	0.1	300	30.3	3000	3086	G	24.93074	85.56372	Normal				
29/7/22	13:16:19	60	0.1	330	10.1	3300	3339	G	24.93133	85.564493	Normal				
29/7/22	13:16:19	60	0.1	300	20.2	3000	3032	G	24.93179	85.565268	Normal				
29/7/22	13:16:19	60	0.1	290	20.2	2900	2964	G	24.9321	85.566143	Normal				
29/7/22	13:17:0	60	0.1	280	20.2	2800	2807	G	24.93229	85.567153	Normal				
29/7/22	13:17:0	60	0.1	270	20.2	2700	2713	G	24.93244	85.568097	Normal				
29/7/22	13:17:30	60	0.1	350	20.2	3500	3562	G	24.93259	85.568988	Speed Breaker				
29/7/22	13:18:5	60	0.1	300	10.1	3000	3058	G	24.93292	85.570975	Normal				
Total		6.100	19310	1303	193100	195990									
Average			316.56	21.359	3165.57	3212.95									

29/7/22
(AE)

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नवादा

29/7/22

Name of Customer : SUJAY BHAN SINGH
 Name of Work : AKUNA To URSA
 Road :
 Lab Job number : 60
 Date : 7/29/2022
 Section No. : 60


Test Date : 7/29/2022
 Machine No :
 Start S No : 0.000
 Start E No : 6.100
 Weather :
 Start Location : AKUNA
 End Location : URSA
 Road Name : AKUNA To URSA
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 1424 To 5000
 Dist Range : 0 To 62
 Interval : 1000 mm/km
 Equation : $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File : G:\Bump of Nawad\Maintenance Bump Data\Maintenance Bump Data as on 29.07.2022\Sujay Bhan JIVAKUNA -
 Name of Customer : Name of Work/Road : Lab Job number :

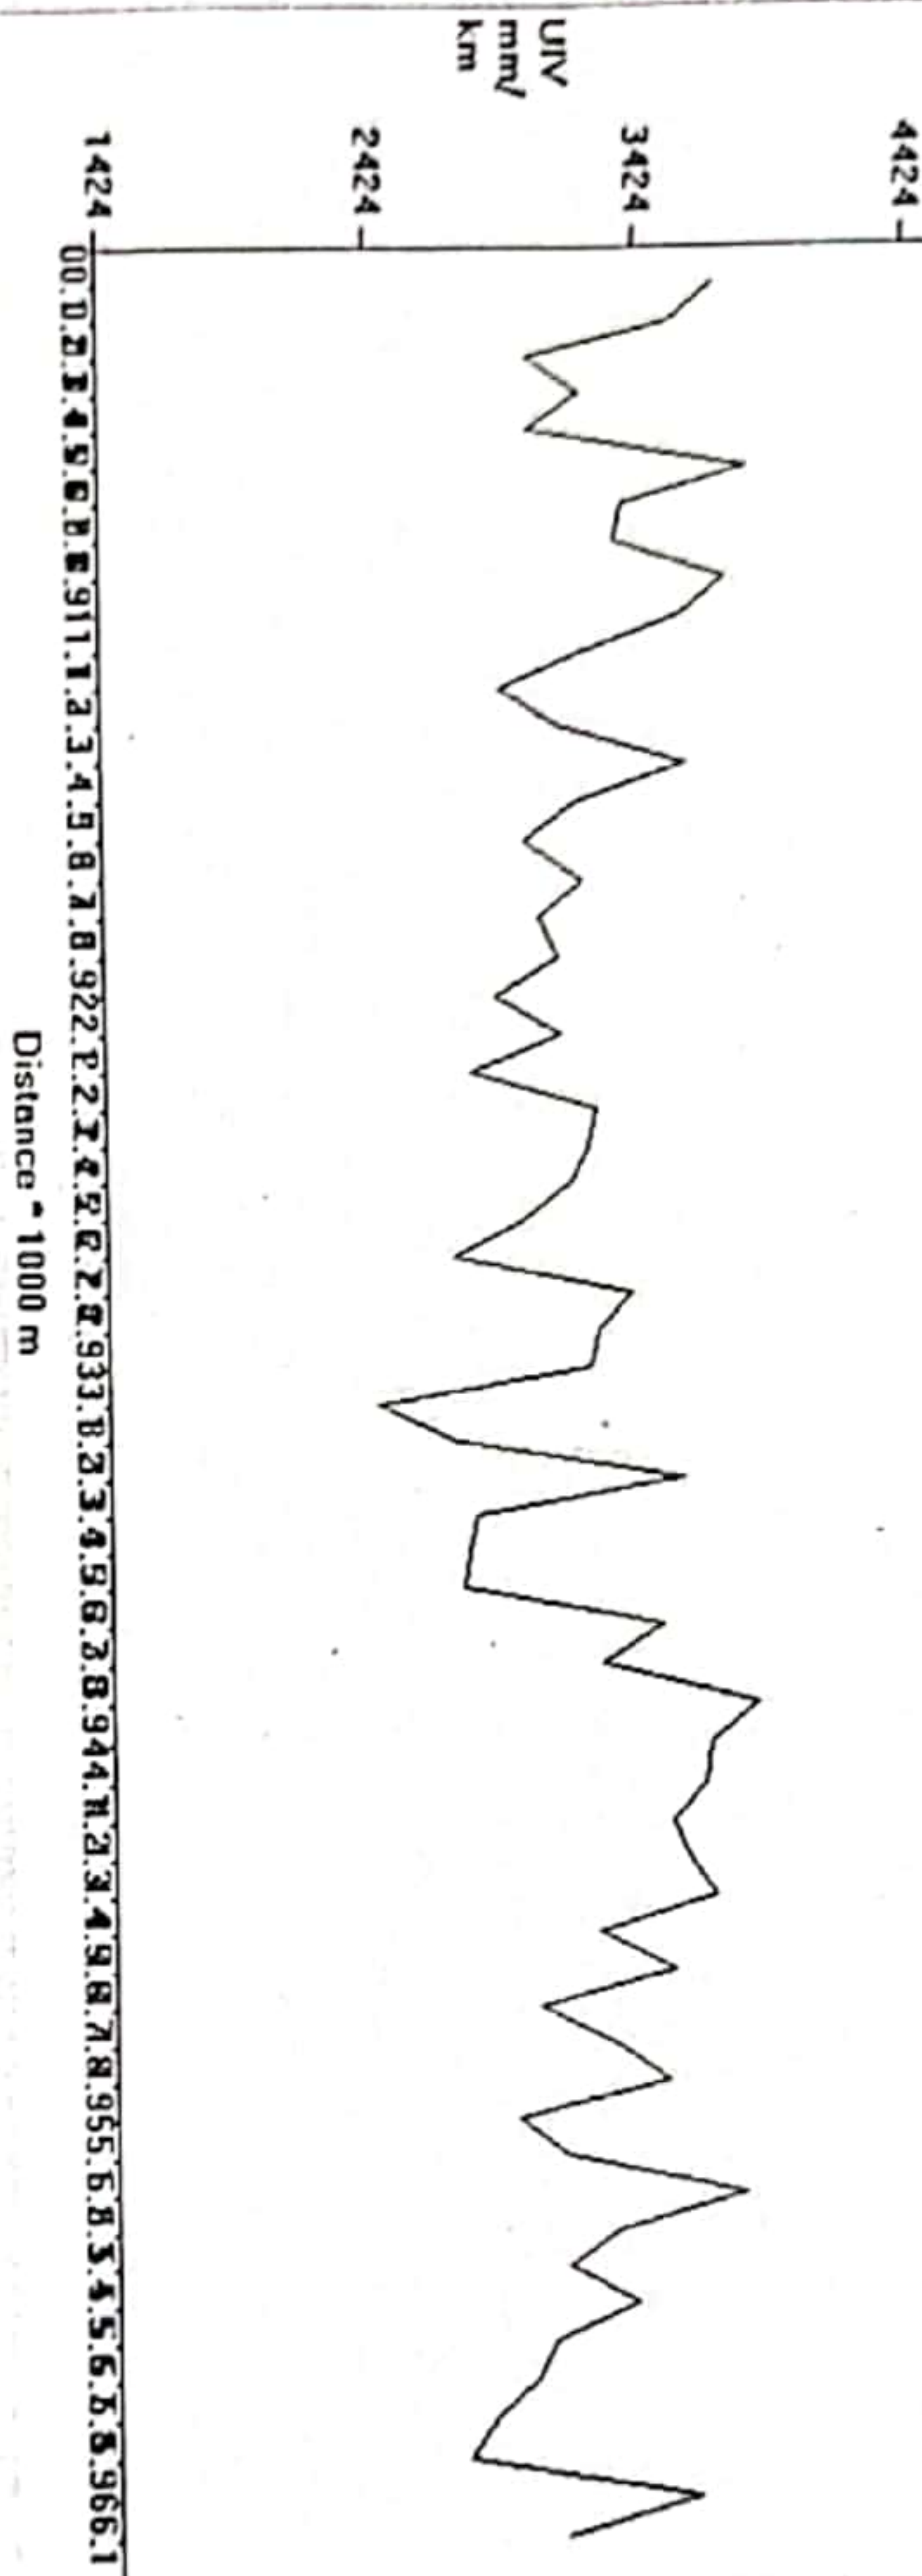

29/07/22
 (PSC)

कार्यपालक अभियन्ता
 सामीप कार्य विभाग
 पोर्वा एसडिल नवादा
